



Technical Proposal for

Project to Create an Electronic Platform for Managing the Competition Lifecycle in Integration with Corporate Systems and Artificial Intelligence Technologies

Reference No.: 250739015178

August 8th, 2025

STATEMENT OF CONFIDENTIALITY

The information comprised in this document is confidential and may not be imparted to any other party without prior approval of KaarTech Technology Pvt. Ltd. The distribution or copying of this document in whole or in part is strictly forbidden. This proposal is solely in response to the requirement received and advises on the estimated costs and timescales of the requested functionalities. This will not abide to any contractual or delivery commitment prior to confirmation. Any change to these conjectures and assumptions may lead to changes in scope, costing and functionalities. This document does not establish any legal bonding. Post acceptance of this proposal, further negotiations may be carried out based on the standard terms and conditions specified herein. Upon unacceptance, this proposal and all related documents should be returned to KaarTech Technology Pvt Ltd immediately. Failure to adhere to the aforementioned clauses is subject to legal action.



Table of Contents

1.	Evaluation Criteria.....	7
2.	Executive Summary	8
2.1	Company Profile	8
2.2	Our Global Locations.....	11
2.3	Our Mobilization Strengths	11
2.4	Our Contribution to Vision 2030.....	11
2.5	Our Value Propositions	13
2.6	Awards Bagged by KaarTech in EMEA Region	13
2.7	Conclusion.....	14
3.	Why KaarTech and Key Success factors?.....	15
3.1	Understanding of SWA Business	16
3.2	Reliable Strategic Partner	16
3.3	Deployment of Right Consultants.....	17
3.4	Flawless Execution and Stringent Governance Model	18
3.5	Assured Delivery Excellence	18
3.6	Process Driven Execution through Ktern.AI Digital Projects	18
3.7	Five Levels of Project Governance	29
3.8	Accreditations & Alliances	30
3.9	SAP Partnership Certification	31
3.10	Experience in Similar Solution	34
3.11	Experience in Similar Geography	39
3.12	Experience in Similar Integrations.....	39
4.	Proposed Solution	42
4.1	Overview	42
4.2	Business Process.....	42
4.3	Standard Features.....	61
4.4	Additional Features.....	62



4.5	Integrations	64
4.6	Workflows	65
4.7	Security.....	66
4.8	Solution Architecture	72
4.9	Technical Specifications	74
4.10	User Interface	76
4.11	Conclusion	88
5.	Project Scope of Work	89
5.1	Language.....	89
5.2	Geography	89
5.3	Service Window	89
5.4	Currency	89
5.5	Legal Entity	90
5.6	Development Scope	90
5.7	Training Scope.....	110
5.8	Testing Scope	112
5.9	Technical Assumptions.....	115
5.10	Technical Exclusions.....	116
6.	Support Scope	118
6.1	Support Period	118
6.2	Service Window	118
6.3	Support Tool	118
6.4	Classification of Calls and Procedures.....	118
6.5	Service Level Parameters for Incident Management.....	119
6.6	Exceptions in SLA	119
6.7	Incident Response and Resolution Time	120
6.8	Support Assumptions	121
6.9	Support Exclusions	121



6.10	Knowledge Transfer	121
7.	Project Execution & Approach	123
7.1	Project Delivery Methodology	123
7.2	Project Plan	124
7.3	Release Plan	125
7.4	Project Deliverables	125
7.5	Project Organization Structure	132
7.6	Project Governance	133
7.7	Project Roles & Responsibilities	135
7.8	Communication Mechanism	141
7.9	Escalation Mechanism	143
7.10	Risk Management	143
7.11	Change Request Management	146
7.12	Quality Management	147
7.13	Prerequisites to Start the Project	148
7.14	Project Assumptions	151
7.15	Project Exclusions	152
8.	Project Team	154
9.	Frequently Asked Questions (FAQs)	156
9.1	Database	156
9.2	Hardware	156
9.3	Licenses	156
9.4	Backend	156
9.5	Workflow	157
9.6	Ariba	157
9.7	Integration with Thiqah System	157
9.8	Contract Management Feature	157
9.9	Change Request Feature in Contract Process	157



9.10	Support Period	158
9.11	Once the RFP approved will the purchasing officer will update the information of Etimad publishing information (Ex. Etimad reference number , BOD, Etc)?	158
9.12	In case of auto generated PR in which it is automatic system creation what will be the proposed scenario?	158
9.13	Will the proposed solution will have the ability for creating contract form in which the purchase order is not at the cycle of this solution.	158
9.14	The mentioned team will be fixed for entire project period in order to avoid any possible disturbance.	158
9.15	The main committees (BOC , BEC , Technical Evaluation committees and BQC) are not fixed since Ex. There are more than 5 BOC and it is periodically changed and for the technical committee is project based committee.	159
9.16	The selection of the above different committees has to be selected on the RFP creation stage.	159
9.17	Since your solution designed to meet the client needs for the procure to pay, all related activities will be not limited to what has been mentioned at your offer (Development Scope Section).	159
9.18	During the hyper care period any necessary changes will be carried out in which it is related to prior going live activities.	159
9.19	The solution will have internal communications between committees if required.	159
9.20	The solution will have the digital signature approach and it will be integrated with Tarasul if required.	159
9.21	No further renewal will be required for the provided solution.	160
9.22	Technical Clarifications	160
9.23	Team Continuity Requirements	165
9.24	Training Scope	166
9.25	Post-Go-Live Support (Hypercare and Standard)	167
9.26	Development Scope Flexibility	168
9.27	Project Team Allocation	168
10.	Statutory Documents	172
10.1	Bid Bond	172



10.2	Commercial Registration Certificate	174
10.3	Classification of Contractors Certificate	175
10.4	ZAKAT Certificate	176
10.5	VAT Certificate	177
10.6	GOSI Certificate	178
10.7	Chamber of Commerce Certificate	179
10.8	Nationalization Certificate	180
10.9	MISA License	181
10.10	LCGPA Certificate	182
10.11	SME Certificate	183
10.12	SAP Partnership.....	184
10.13	Delegation letter	187
10.14	Most Recent Article of Association	188
10.15	National Address.....	189
10.16	ISO Certifications.....	190
10.17	Wage Protection System Certificate.....	194
10.18	Saudi Council of Engineer.....	196
10.19	Recent financial statements	196



1. Evaluation Criteria

KaarTech has published the below table mapping the respective sections to the technical evaluation criteria mentioned in the RFP, released by the SWA.

S. No	Criteria	Section Mapping
1	Proposal compliance with terms and specifications	<u>Section 2:</u> Executive Summary
2	Clarity of the scope of services provided and the timeline	<u>Section 4, 5, 6 & 7:</u> Proposed solution, Project Scope, Support scope, Project Execution & Approach
3	Quality and comprehensiveness of the proposed project	<u>Section 4, 5 & 6:</u> Proposed solution, Project scope of work, Support scope
4	Previous Project Experience	<u>Section 3.10, 3.11:</u> Experience in similar solution, Experience in similar geography
5	Qualifications and experience of the work team	<u>Section 8:</u> Project Team

Below are other requested confirmations as part of the RFP,

S. No	Criteria	Compliance Status
1	Submission of the technical proposal for the Tender	Fully Compliant
2	Providing a Silver or Higher-Level SAP Partner Certificate (SAP Partner Edge Service)	SAP Gold Partner <u>Section 3.9</u>
3	Cybersecurity Requirements	Fully Compliant
4	Non-Disclosure Agreement	Fully Compliant



2. Executive Summary

Kaar Technologies Saudi for IT (hereinafter "KaarTech") would like to thank Saudi Water Authority (hereinafter "SWA") for giving us an opportunity to respond with a technical proposal for Project to Create an Electronic Platform for Managing the Competition Lifecycle in Integration with Corporate Systems and Artificial Intelligence Technologies. With our understanding from SWA, KaarTech has prepared an extensive and comprehensive proposal to fulfil business requirements which in turn aids SWA to become an intelligent enterprise.

In connection to this and through diligent understanding of SWA's requirements, KaarTech has responded through a technical proposal with the best practices in solution development and integration which ensures to provide best of the services to SWA on this digital transformation journey.

KaarTech's AI capabilities span intelligent automation, data-driven insights, predictive analytics, and natural language understanding—empowering organizations to make smarter decisions, improve efficiency, enhance accuracy, and drive innovation across business processes.

With 20+ years of rich experience in implementing various solutions across globe and especially in GCC, KaarTech is highly committed and competent enough to work with SWA closely on this digital transformation initiative, which comes with the best of breed tools to accelerate this project and achieve faster realization of project deliverables and benefits.


KaarTech is known for its commitment, quality of the project and agreed deliverables. With this unique value proposition, KaarTech is very sure of exceeding the expectations of SWA with cost effective services. KaarTech has taken utmost care to be both compliant and responsive to the requirements and commercials of SWA and look forward to working with SWA on the further stages of evaluation process to ensure technical proposal is well understood and received by SWA to move ahead with the next steps on the digital transformation journey.

2.1 Company Profile


KaarTech is a global consulting firm focused on designing, delivering, and deploying the finest ideas and expertise to empower companies in achieving new heights of excellence in today's challenging business landscape. Our true intention to serve the SWA to achieve their business objectives coupled with astounding consulting expertise is the principal reason for KaarTech's success for the past 20+ years.




We have been in the business since 2005, with humble beginnings achieving milestone after milestones. With vast majority of our business coming from middle east especially Kingdom of Saudi Arabia. We are aware of the opportunities Kingdom offers to be one among the best globally through Vision 2030. We, KaarTech is immensely proud to work with SWA in achieving its vision and goals through this comprehensive ERP transformation journey and thereby contribution Saudi Vision 2030.



Our Services Portfolio



SAP Digital Core Services



Edge Solutions

Financial Management	Asset Management	Sales & Marketing	Production Planning & Maintenance
Performance & Profitability Management	Intelligent Asset Management	Commerce Cloud	Digital Manufacturing Cloud
Governance, Risk & Compliance	Intelligent Asset Network	Sales Cloud	Manufacturing for Planning & Scheduling
SAC Planning	Field Service Management	Emarsys Customer Engagement	Quality Issue Resolution
Customer Experience Management	Materials Sourcing & Procurement	Supply Chain	Human Resources
Service Cloud	Concur	Integrated Business Planning	SuccessFactors
Customer Data Platform	Arriba	Extended Warehouse Management	
Customer Identity and Access Management	Fieldglass	Global Track and Trace	
		Transport Management	

Digital Transformation Excellence

Product Engineering	Data Science & Engineering and Analytics
- Mobile Application Development - Custom Application Development - Application Support - Portals - Product Modernization	- ETL & Data Engineering - AI, ML & Deep Learning - Big Data & Business Analytics - Data Lakes & Data Warehousing - Dashboards & Reports - Data Integration Services
Cloud Engineering	Customer Experience & Marketing Automation
- ICT Professional Services - Managed Cloud Hosting - Infrastructure Management Services	- Customer Journey Consulting - Content Strategy & Writing - Campaign Management & Metrics - Implementation & Integration - Communications Strategy - Influencer Marketing - E - Commerce & Content Managed Sites
Business Process Management	
- Workflow Automation & RPA - Block Chain - Low Code Development - Process Mining	


Our Global Footprint



[Handwritten signature]



2.2 Our Global Locations

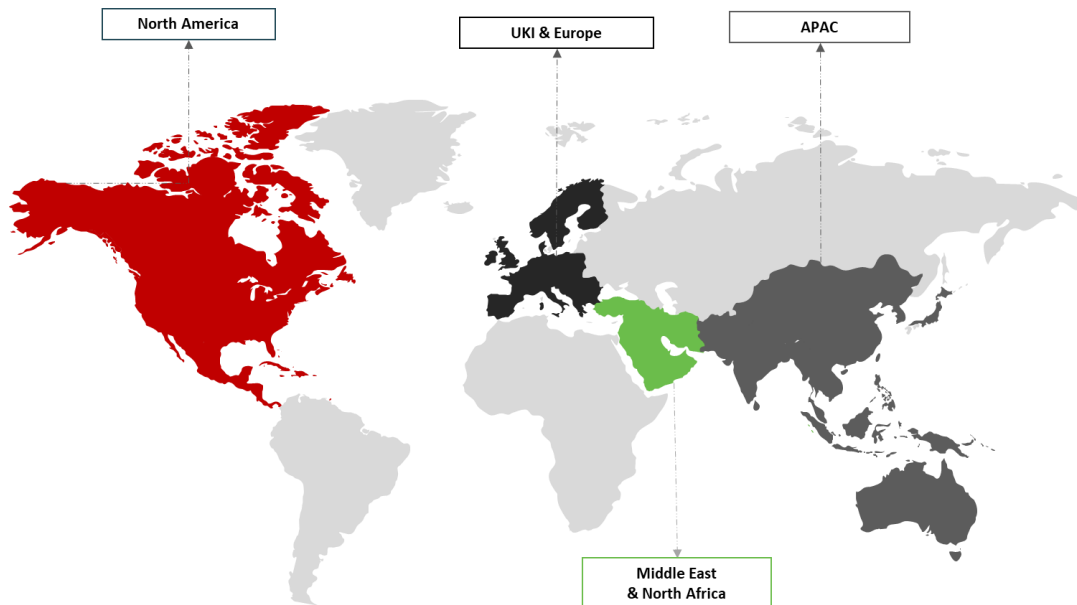

2.3 Our Mobilization Strengths


We maintain good bench strength across skill sets to ensure quick mobilization. KaarTech has a very well-designed HR policy which has helped us retain the best talent in the business without facing high attrition risks. We follow a strict screening process to ensure that all the candidates whom we propose for projects are fully qualified. Our team will do qualifications on all resumes, job applications, interviews, educational or professional experience, the testimony of references, or in-house testing, such as for software knowledge, typing skills and other methods. We provide periodic training at KaarTech to help our resources constantly raise the bar in terms of the skills and knowledge which is a key to creating value- driven project execution.

2.4 Our Contribution to Vision 2030

KaarTech Tech has been a pivotal partner in advancing Saudi Arabia's Vision 2030, contributing significantly to the Kingdom's digital transformation journey. With over 17 years of dedicated service in Saudi Arabia, we have collaborated across various industries, driving innovation and technological advancement. Our commitment to empowering the local workforce is evident in our strategic recruitment and development of Saudi talent, aligning with the Vision 2030 goal of creating a thriving, knowledge-based economy. Through our expertise in SAP and IT solutions, we are helping shape the future of Saudi Arabia, supporting its ambition to become a global leader in technology and innovation.



KaarTech has long-standing partnerships with numerous Vision 2030-focused organizations, playing a crucial role in helping them achieve their strategic goals for 2030. Below is a list of these Vision 2030 accounts.



Recent Wins

Project Wins

Project Go-Lives

TAQA
 Oil, gas & Energy
Project Highlight
 Developed a Golden Template for HR, Finance, Procurement, Sales & Maintenance Services to standardize processes.

QGCC
 Manufacturing
Project Highlight
 By implementing RISE with SAP S/4HANA, we optimized QGCC's processes, aligning with Qatar's Vision 2030.

SIRC
 E-waste Management
Project Highlight
 Revamped SIRC's operational framework, enabling seamless scalability and enhancing efficiency, integration, and decision-making.

Borouge
 Oil, gas & Energy
Project Highlight
 We upgraded Borouge's ERP, improving HCM, finance, supply chain, and sales processes and enhancing global business efficiency.

EDO
 Oil, gas & Energy
Project Highlight
 In 5 months, we streamlined EDO's processes, enhancing hiring, feedback, evaluations, access, and budget controls.

CGCC
 Construction
Project Highlight
 Through our strategic partnership, we streamlined their transition to a unified solution modern ERP.

2.5 Our Value Propositions

KaarTech will provide the following value additions to SWA in terms of:

Strengths	Benefits
Partnership Approach	Ensures Transparency & Knowledge transfer
Flexible Engagement Models	SWA centric focuses on meeting specific client needs of engagement & budget
Skilled Project Team	No learning curve, lesser risks, and smoother execution
Business expertise	We deliver quality solutions and add value in the form of both advice and systems to support the achievement of business objectives
Tools & Accelerators	Rapid deployment ability to deliver innovative services at minimum costs and time
Technical and commercial scalability	Effective management of SWA investment throughout all project phases and expand the relationship
KaarTech methodology	Hybrid Agile Methodology - Rapid Development, better solution.
Comprehensive Services	Ensure accountability, better coordination, and smoother migration.
Digital Experience	Strong experience in executing digital projects for major clients in KSA

2.6 Awards Bagged by KaarTech in EMEA Region

Being quality is the supreme focus for KaarTech in every project and customer, SAP has recognized KaarTech as an outstanding system integrator for SAP services, as a token towards continuous clients' successes KaarTech has secured following quality awards from SAP.



SAP Awards



2024 SAPALM Summit APJ
Cloud ALM Hack2Build
Gurus Awards 1st runner-up



Fastest SAP SuccessFactors
Implementation Award
2023

23+ Awards
2010 - 2023

Partner Excellence
Award for S/4HANA
2022

Best RISE Contributor
In MENA Region
2022

Business
Transformation Award
2021

SAP innovation
award
2021



Fast Delivery Category
Award
2020



SAP S/4HANA
Category Award
2018

Business Awards



Best Employer Brand Award
TN | India | Asia
2023 - 2024

GREAT PLACE TO WORK

3rd Consecutive GPTW Certification:
We consistently foster a culture of
transparency, fairness, and
empowerment.



Analyst Recognitions



Cited in Rise with SAP Ecosystem
2024 ISG Provider Lens™ Study



Everest Group®
Peak Matrix Leader
2024


2.7 Conclusion

- With this unique value proposition, KaarTech is very sure of exceeding the expectations of SWA.
- KaarTech has taken utmost care to be both compliant and responsive to the requirements of SWA and look forward to working with SWA on the further stages of evaluation process to move ahead with the next steps on this digital transformation journey.
- KaarTech is the right partner for this scope of services and for the conversions, transformations, and all other services to come.
- KaarTech can be a long-term value partner for SWA in all its digital initiatives.



3. Why KaarTech and Key Success factors?

KaarTech currently has over 2000+ consultants/Developers spread across the globe with primary business operations in the Middle East. We maintain good bench strength across skill sets to ensure quick mobilization. KaarTech has a very well-designed HR policy which has helped us retain the best talent in the business without facing high attrition risks.

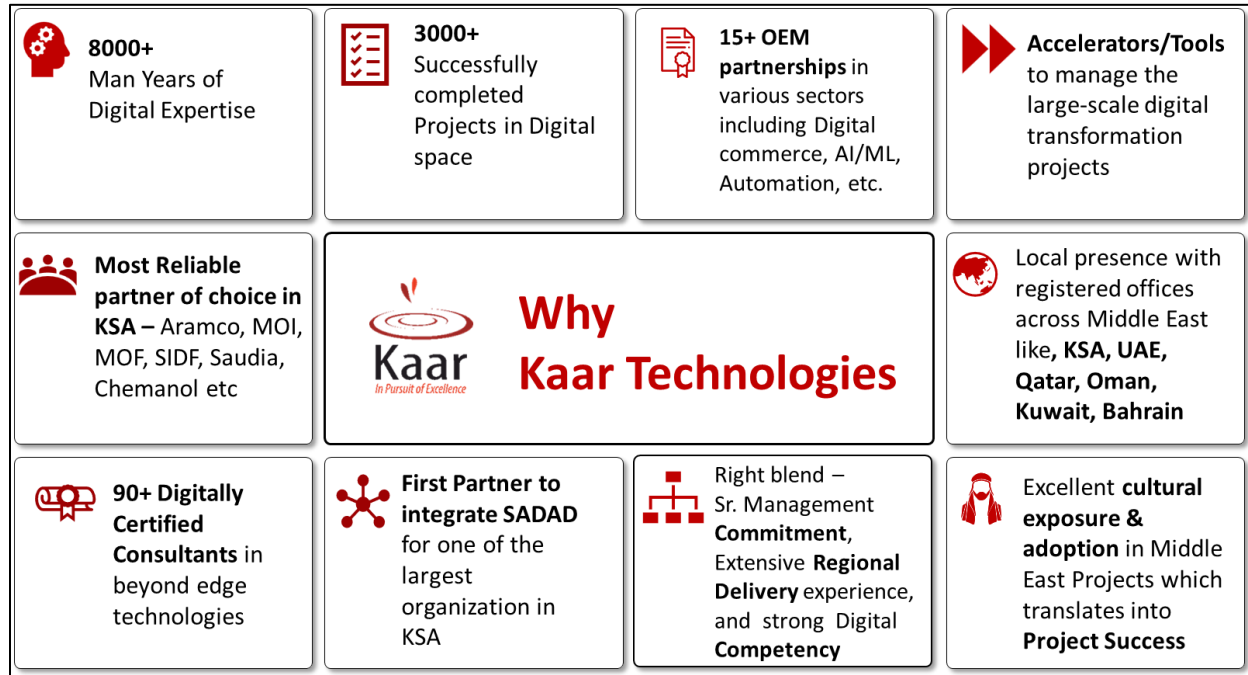

KaarTech provides the services, with the features tailor-made to fit the requirements of the clients. Below depicted, are SWA's benefits from availing us of our Services.



3.1 Understanding of SWA Business

The Saudi Water Authority regulate activities and services related to water operations, oversees them, and develops methodologies that contribute to achieving the objectives of the National Water Strategy in line with the aspirations of Saudi Vision 2030.

The Saudi Water Authority has a mandate to promote water conservation and ensure that water is available to all. The SWA roles are:

1. Beneficiaries Protection
2. Supervising the implementation of Strategic Directions
3. Water Sector Regulation
4. Water Security Planning & Management

Previously, it was known as, Saline Water Conversion Corporation (SWA), a Saudi governmental institution, with has 30 plants, 14 transmission systems, and 4,000 km (2,500 mi) of pipelines, mandated and entrusted with seawater desalination and the delivery of desalinated water to various regions of the Kingdom of Saudi Arabia and beyond. SWA was established in 1974 as an independent governmental institution of a legal personality. It is a government corporation that operates desalination plants and power stations in Saudi Arabia. It is the second largest electrical provider in the country. It is the largest desalinating sea water corporation in the world, responsible for 20% of worldwide desalinated water production.

3.2 Reliable Strategic Partner

It is always imperative for large organizations, especially large companies like SWA, to have a reliable and long-term strategic IT partner for multiple reasons like trust, security, focus on the core business and continuous improvement. KaarTech has been the preferred and reliable partner in Saudi Arabia and the below chart exhibits KaarTech's SWA retention and high-quality and continued services rendered to our esteemed SWAs.





110+ customers engaged with Kaar for more than 5 years



75+ customers engaged with Kaar for more than 3 years



25+ customers engaged with Kaar in the past year



Strong Management Attention



Dedicated PMO for Quality Deliverables



Practice Heads – Right solution



Associate Practice Leads for Daily Governance



Dedicated Centers of excellence for business consulting



Robust quality processes to deliver on-time and on-budget

3.3 Deployment of Right Consultants

It is imperative for any organization to have quality resources deployed in a successful project. KaarTech ensures to deploy right resources having domain experience coupled with skills. Kaar Technologies has the largest number of consultants with more than 2000+ deployed across the globe. At any given point in time, KaarTech has close to 200+ consultants available for the Middle East Region to meet the immediate requirements and demands of our SWAs.



Digital Transformation
Consulting Enabled
Services




SAP Innovations
4 Packaged Solutions in the SAP App
Store for Industry GTM acceleration



Over **500 FTEs** have
already been deployed
in Projects

Resource % to Total consultants

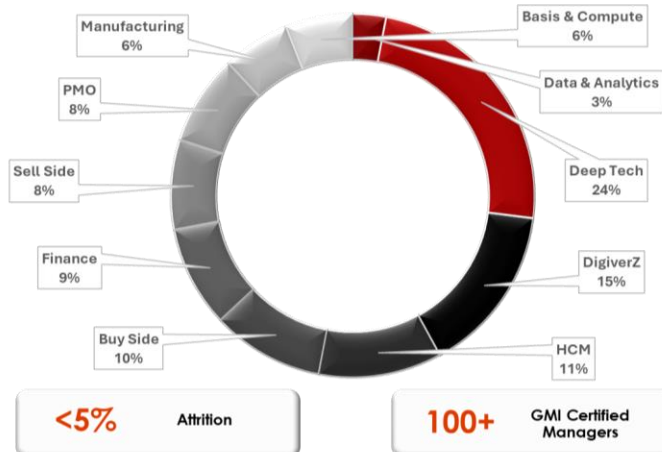

1900+ SAP Consultants

450+ AMS Consultants

450+ DigiverZ/Digital
Solution Consultants

200+ Domain Experts

50 CoE/ DTC Experts

83% Certified Consultants

EDGE.EBS.PRO.FM14 - SAP S4 Applications and Managed Services 17



3.4 Flawless Execution and Stringent Governance Model


In today's business environment, irrespective of the industry type and size, success of any project is determined by how efficiently Project Management Office (PMO) drives the project organization. KaarTech, being an organization founded and built by SAP veterans strongly believes in the principles of stringent project governance and highly committed delivery model which is indeed an integral part of KaarTech's culture. Kaar Technologies has a competent and proven PMO practices put in place supported by Center of Excellence Team who acts as a backbone to support the technical and functional solution to ensure the project timeline is met as per the commitment and the deliverables are accomplished on time.

There are several services provided by PMO depending on the needs of an organization and the vision of the PMO sponsor. In general, the PMO is responsible for deploying a consistent project management methodology within the organization, including processes, templates, and best practices. The common processes and practices adopted by PMO allow projects to be completed better and faster.

3.5 Assured Delivery Excellence

KaarTech has a distinguished and differentiated way of executing the projects to stay ahead of the competition in terms of quality of execution and its success rate.

The following engagement model is unique in nature for all its strategic SWAs. The involvement of different stakeholders from KaarTech shall be there in this engagement right from the PMO Head, PMO Quality Audit, Practice Team which comprises of the respective Practice leads of each business functions apart from the core project team, Center of Excellence, Digital Transformation Consulting Team, Industry Value Team etc.




3.6 Process Driven Execution through KTERN.AI Digital Projects

KTERN.AI is an independent product division of Kaar Technologies, a consulting firm with 15+ years of SAP excellence. KTERN.AI's vision is to inspire and democratize SAP centric Digital Transformation as a Service (DXaaS). It offers the SAP DXaaS Automation Platform with cognitive digital workplace

for enterprises. Aided by inbuilt data-driven hyper-automation, and with no-code digital automation capabilities KTer.AI accelerates the SAP implementations and transformations and streamlines business operations to drive productivity for SAP customers, partners, system integrators, QA and Auditing Office. KTer.AI has established strong partnerships and SAP Account Executive engagements across the Middle East and Africa.

With KTer.AI, SWA can ensure continuous value throughout the entire Digital Transformation Lifecycle. KTer.AI is currently the preferred platform of SAP's Global RISE with SAP S/4HANA Adoption Acceleration Program.



KTer.AI Highlights

KTer.AI is an SAP Spotlight App that allows the evolution and transformation of businesses without a worry of integration and data or system risks. It addresses most demanding business challenges and helps gain immediate value, thereby maximizing investments in SAP solutions and helps in gaining more return on SAP solution investments.

KTer.AI is recognized by SAP as one of the Top five (05) Apps in SAP ERP and Finance. It is one of the Top three (03) tools for SAP ERP Software in G2 Grid. KTer.AI is listed in the SAP Store, upon successful SAP Readiness and Compliance Checks. KTer.AI is an SAP Qualified Partner Packaged Solution, an SAP ERP solution that is developed by an SAP partner with its intellectual property (IP) and industry expertise that is evaluated and tested for optimized integration with SAP technologies.

KTer. AI – SAP Digital Transformation Platform

KTern.AI provides a Digital PMO embedded with Activate framework for large digital transformations. The autonomous KTern.AI controls your digital transformation with its SAP tribal knowledge and data powered intelligence. Its remote digital workplace helps you ensure continuity and increase productivity of businesses & projects.

3.6.1 KTern.AI Digital Projects


KTern.AI Digital Projects provides the digital automation value to manage & govern the project activities. It ensures the different users including Project Managers, PMO Heads, IT Consultants, Architects, IT Director, ERP Manager, LoB Manager, Business SMEs & Business Users collaborate, manage and monitor the overall project in an organized way with digital footprint. KTern.AI Digital Projects ensures 28% improved workforce productivity and ensures integrity-led experience. Using Digital Projects, a seamless project governance platform is set up to offer continuous value across the complete project lifecycle to manage all activities digitally.

3.6.2 Onboarding

KTern.AI Digital Projects is the Digital Stream which orchestrates collaborative engagement, enables on-time phase closures, ensures knowledge transfer and change management of all the digital transformation stakeholders – customers, partners, system integrators & SAP. The KTern.AI enterprise product suite drives productivity for the businesses and projects on a larger scale in one digital platform, by adhering to the SAP Activate methodology. Using KTern.AI Project Setup & Project Settings, the project calendar, project plan can be defined and updated by the Project Manager.

Once the project is created, you can invite additional project participants and stakeholders (from both the system integrator and the customer sides) into KTern.AI, so that everyone can participate in the project. It only takes a simple step to invite users with role-based access control defined by levels – Limited, Basic, Standard, Super. KTern.AI automatically creates an organizational structure based on the hierarchy specified while inviting the users. This will enable you to comprehend the project's reporting structure, in line with users invited to the project from different teams.



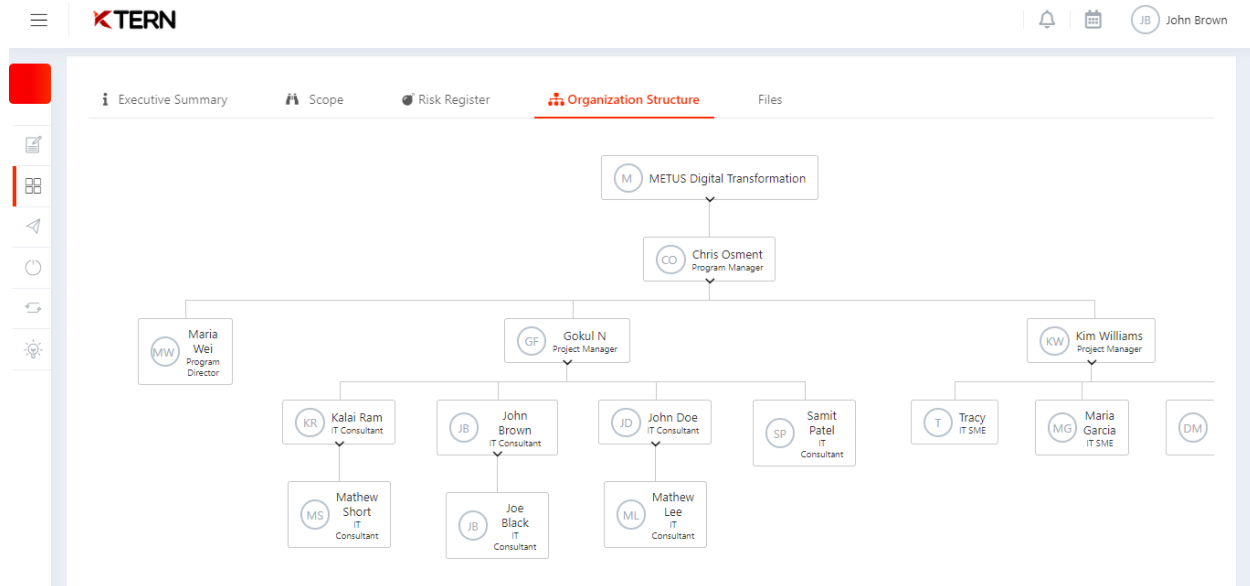

3.6.3 My Workspace


Any user will by default arrive at the 'My Workspace' screen after launching a project. It is a user-specific digital workspace that gives you a summary of all the project work items to which the specific user is accountable, with contribution and participation. The tasks, issues, test cases, signoffs, user stories, risks, Call-To-Actions (CTA) are the major categories of work items given in the workspace of the platform.

#	Title	Status	Signoff Gro	Planned To	Your Action
1	OCM signoff 3	Approved	S/4HAN...	Aug 4, 2...	Approve
2	Data migration approach and strategy	Approved	S/4HAN...	Apr 4, 20...	Pending
3	Matarat	New	Strategy ...	Sep 13, ...	Pending
4	Mock Signoff	Approved	Prepare	Mar 7, 2...	Approve
5	G/L Account Changes Chart of Accounts View	Approved	S/4HAN...	Aug 16, ...	Approve
6	Invoice Management	New	S/4HAN...	Apr 8, 20...	Pending

3.6.4 Control Centre

The Control Center provides a comprehensive overview of the project and allows PMO team to steer the project with a defined mechanism. From a single location within KTERN.AI, you can define

the functional scope and IT scope and keep track of communication cadence, and guarantee project cadence. During the project, the project manager can additionally add and keep an eye on any risks. You can manage the risk indicators, risk response, and responsible party from within Ktern.AI.

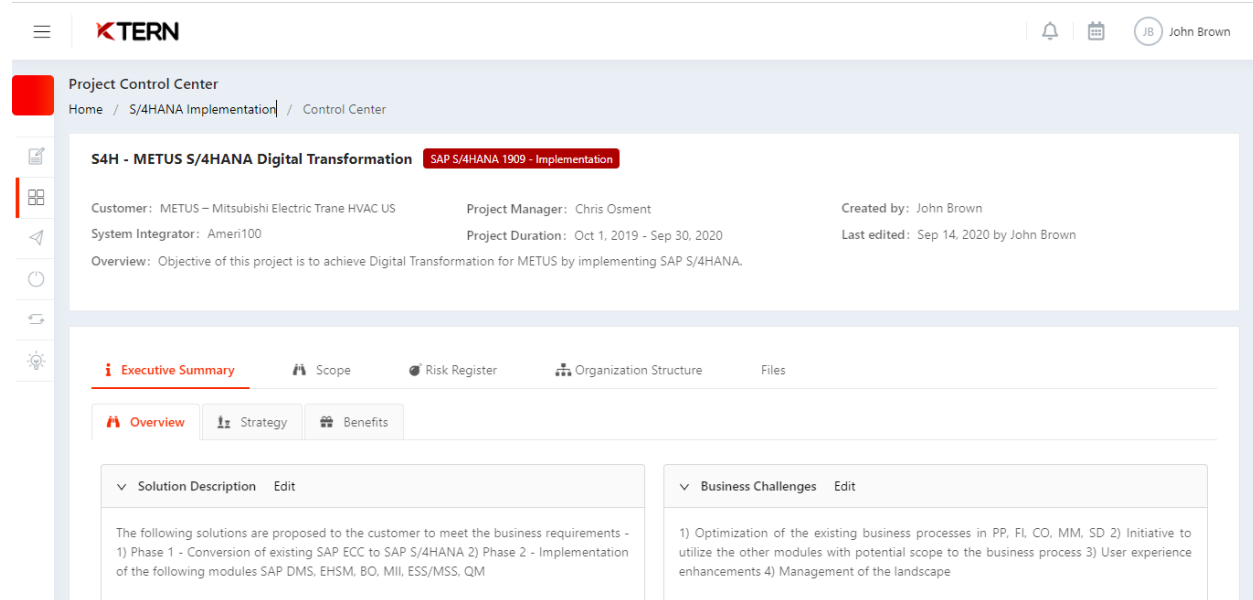

3.6.5 Signoffs & Change Management


Ktern.AI brings in accountability to project stakeholders with digitalized signoffs driven workflow automation. It offers Signoff Cockpit, Signoff Item Wizard, Configurable Signoff Reports to simplify the work during the project execution –

- Streamline multi-level stakeholder approvals for the entire project team including customer & system integrator
- Orchestrate your deliverable reviews, phase closures, Q gate audits, OCM with signoff enabled workflow automation
- Drive hassle-free approvals in digital approach, thereby avoiding the use of papers, mails, meetings in the case of traditional approach
- Manage your cutover deliverables with organized signoff matrix

The Implementation project effort is extensive and fraught with uncertainties. Therefore, adhering to the project's schedules and making sure the activities are completed in the right order are crucial for the project's success. The Ktern.AI sign-off wizard aids in the methodical approval of successive phases and ensures that the system goes live according to schedule. The users can build numerous sign-off groups and items within Ktern.AI.

Following that, the users can map a number of activities, problems, and test cases under each sign-off item. These sign-off items may receive hierarchical approval from the appropriate stakeholders. Each scenario and sub-scenario have a single root node from which sign-off items

The Project Managers can add and modify tasks in the project plan on the timeline in a user-friendly way similar to workbook experience. KTern.AI allows to establish dependencies between activities by linking these newly produced tasks to the jobs that came before them. Each task is listed in the workbook's view, which resembles an excel sheet, along with its corresponding phase, work package, status, and anticipated and actual dates. This workbook is designed to make it simple to add, assign, and update the status of tasks. The Gantt View of the timeline provides the hierarchical work items with dependencies that could be mapped based on preferences. The critical path can be identified, and project milestones can also be defined to track the project execution.

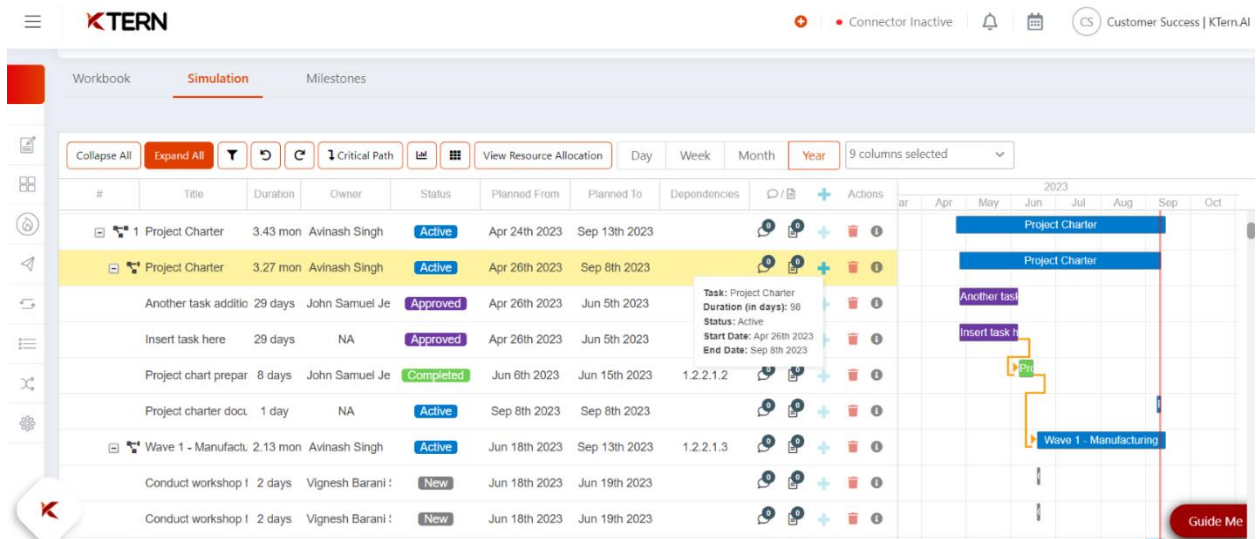

3.6.7 Tasks Wizard

The SAP Activate framework is the foundation for KTERN.AI. The Activate methodology's phases and work packages break down to each activity with tasks. The task wizard allows a comprehensive management of stakeholders, activity execution, planned vs actual timeline, references, discussions, history, files, notes – all specific to the particular task. This primarily ensures each user undertakes a participative management of his/her activities during the project execution. The activity updation of each task in this digital task wizard allows the bottom-up mapping to the overall project plan in detailed, yet organized way of tracking. It offers complete control to PMO stakeholders over the execution of each team member in project.

The screenshot shows the KTERN Tasks Wizard interface. It features a sidebar with navigation options like Dashboard, Control Center, Users, Backlog, Sign Off, Boards, Calendar & Events, Files, Tasks (highlighted), Issues, Test Cases, Clone & Create, Forum, and Maps. The main area is titled '# Application value and scoping' and includes a search bar. Below the search bar, there are sections for 'Stakeholder Information', 'Planned Vs Actual', 'References', 'Discussions', 'History', 'Files', and 'Wiki / Notes'. The 'References' section is expanded, showing details for 'K100 Master Data'. This section includes fields for 'Created By' (Customer Success | KTERN.AI), 'Category' (Category not found), and 'Product' (S/4HANA). There are also buttons for 'Component' and 'Process Item'.

3.6.8 Issues Wizard

In Ktern.AI, the user can leverage Issue Wizard to create and manage the defects pertaining to test cases or general issues associated with the project execution. You can specify stakeholders, planned vs actual dates, and the problem's relationship to a certain parent task when generating an issue. As a result, Ktern.AI allows the Project Managers and important stakeholders to track issues in a single view digitally.

3.6.9 Calendar & Events

The Calendar offers a view of all your tasks, issues, and test cases along with their associated statuses. Importantly, Ktern.AI offers the ability to build Events to drive digitalized cadence meetings, workshops, steering committee meetings and capture the meeting moments within the platform.

The screenshot displays the Ktern.AI interface for managing events. The top navigation bar shows the Ktern.AI logo, a 'Connector Inactive' status, and user information for 'Customer Success | Ktern.AI'. The main content area is titled 'HANA - SAP Landscape Architecture and database Discovery' and includes a 'Completed' status. A sidebar on the left contains various navigation icons. The 'Meeting Summary' table lists several events with columns for Title, Type, Owner, Planned To, and Created By. A modal form is open for creating a new event, with fields for Type, Title, Assigned To, and Planned To. The table data is as follows:

Title	Type	Owner	Planned To	Created By
New Information	Status			VB
Upload SDD in the respective Signoff	Information	AB	Aug 17, 2022	VB
Configrauto	CTA	VB	Feb 22, 2023	CS
Signoff template to be shared	CTA	NV	Jun 9, 2023	CS
sample - 1	Issue			CS

You can invite guests, schedule repeating meetings, and link these events to specific tasks or work packages. As a value-added capability, you can create meetings from Ktern.AI, which would also ensure that your Microsoft Teams invite gets created, scheduled & calendar of participants blocked automatically.

3.6.10 File Explorer


The main objective of the files/document repository is to have all the project related files and documents in one single place within KTERN.AI. The advantage is that entire knowledge and information regarding the project can be found by anyone, accessed from anywhere in one single place in line with the activities, issues, signoffs of the project.

3.6.11 Collaboration Forum

The Enterprise Collaboration forum provides a digital platform where all the project members can have discussions regarding the happenings of the project. It includes global announcements,




important notifications, and ensures every conversation during the ongoing project is captured digitally and becomes one unified place for discussions.




3.6.12 Clone & Create Agile Automation


During iterative sprint activity execution which involves an extensive no. of repetitive activities, KTern.AI offers first-of-its-kind Clone & Create to assist the team in rapid creation and management of activities. With this agile delivery automation, the rules can also be defined based on owners and dates to simulate and generate based on defined agile templates in KTern.AI. The various repetitive activities in design, configure, develop, test, deploy related for each user story & process item can now be orchestrated rapidly using Clone & Create capability in KTern.AI.



3.6.13 Dashboard & Reports


Ktern.AI offers a comprehensive dashboard with analytics of the work items that can be viewed as per the different phases, work packages, status of the work items, stakeholders, process items, signoffs, etc. It comprises everyday tracker, resource utilization analytics, overdue alerts, risk insights and project progress tracker based on count and weightage. Ktern.AI offers an added advantage in reporting with configurable dashboards across different lines of business.

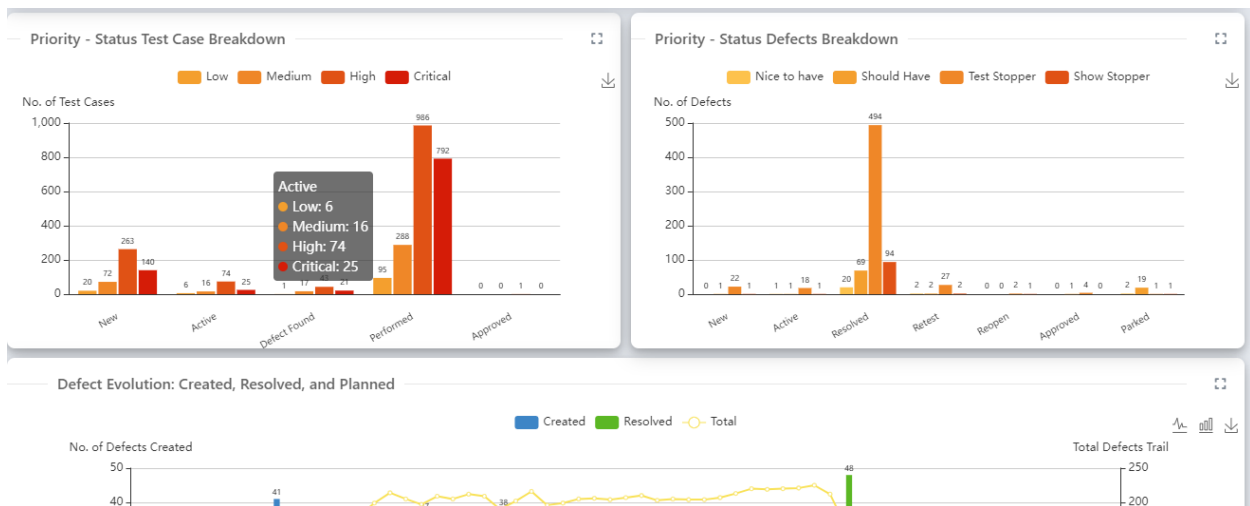

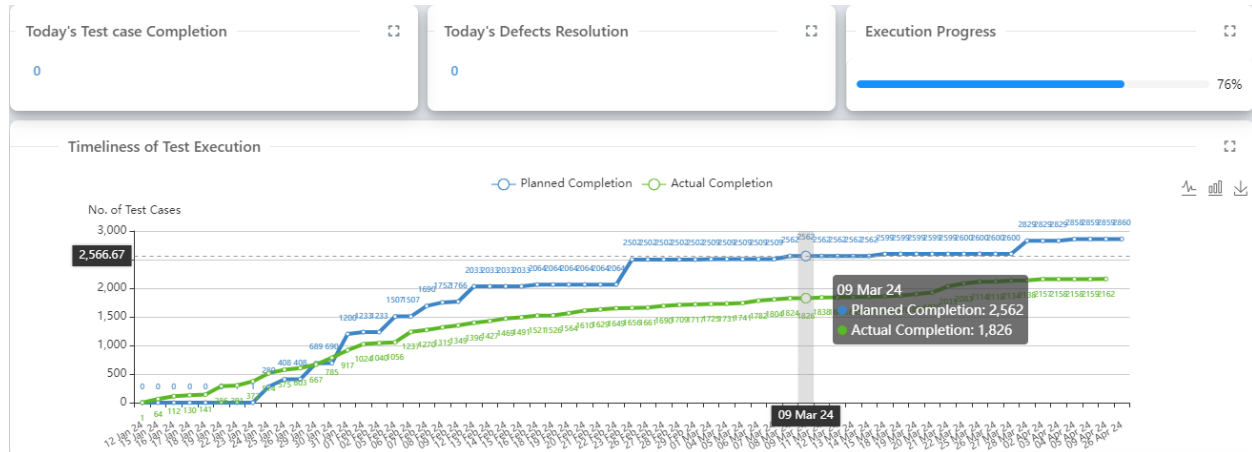3.7 Five Levels of Project Governance

Each phase of the project shall be governed, supervised by the Module Leads from the solution perspective. Likewise, each deliverable shall be governed and audited by the KaarTech's PMO before the deliverables are released to SWA. The pillars of KaarTech's organization shall be part of the non-core team to ensure the project success, arrest any risks during the execution and consult/suggest best practices. KaarTech's Project Execution framework shall have 5 levels of governance/ audit before releasing any deliverables like Solution Design documents, Training Strategy documents, Testing Strategy documents etc. as mentioned below:



Some of the key business outcomes to SWA for the project governance are:

- 100% Quality Deliverables to SWA
- Adoption of best practices
- On Time Project Delivery without any delays
- Risk Identification and Mitigation in a much advance stage of the engagement.

3.8 Accreditations & Alliances

Accreditations




Alliances



[Handwritten signature]



3.9 SAP Partnership Certification

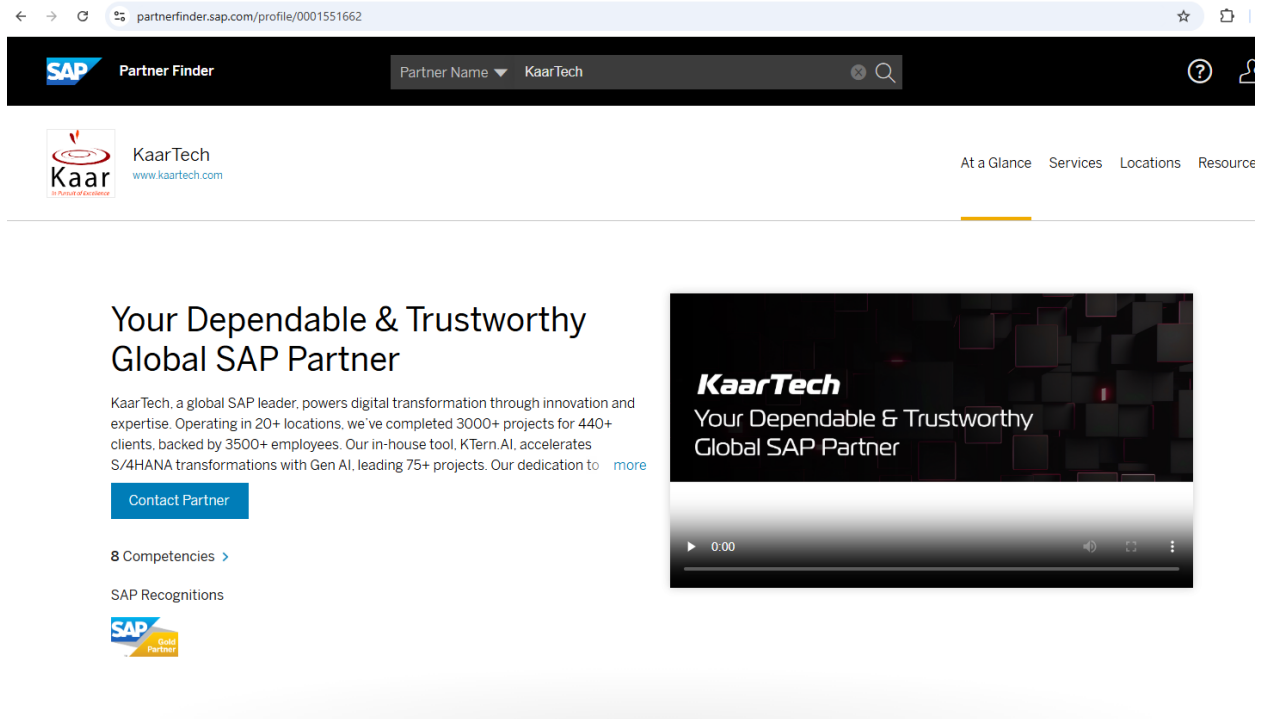

partnerfinder.sap.com/profile/0001551662

SAP Partner Finder Partner Name KaarTech

KaarTech
www.kaartech.com

At a Glance Services Locations Resource

Your Dependable & Trustworthy Global SAP Partner

KaarTech, a global SAP leader, powers digital transformation through innovation and expertise. Operating in 20+ locations, we've completed 3000+ projects for 440+ clients, backed by 3500+ employees. Our in-house tool, K.Tern.AI, accelerates S/4HANA transformations with Gen AI, leading 75+ projects. Our dedication to [more](#)

[Contact Partner](#)

8 Competencies >

SAP Recognitions

SAP Gold Partner

Partnership

Kaar Technologies Saudi for Informa ID 2816763

Overview Program & Tracks **Level** Authorizations Qualifications Certifications



Partnership Level

SAP Gold Partner

800 Points

This account has reached Gold Partnership Level

New Partner Leveling Framework (2025) Preview

- **New system launching in 2025.** This dashboard previews the projected level for Kaar Technologies Saudi for Information Technology under the new framework.
- **This preview is NOT the currently active, published level but may be identical to it.** The currently active level is Silver. SAP Gold Partners and SAP Platinum Partners can verify this on SAP Partner Finder.
- **Use this preview to prepare.** Understand the new system and take action to reach or maintain the desired level.
- **Progress updates are dynamic.** Updates occur daily or quarterly, depending on the specific metric.
- **Safeguarding:** The level will enter "safeguarding" if points drop below the required threshold for the current level.
- **Official Level:** After the preview period, the displayed level becomes official and any active safeguarding countdown resets to 200 days.




CERTIFICATE
SAP hereby certifies that
Kaar Technologies Saudi for Information Technology

Country : Saudi Arabia
City : Riyadh
Partner ID : 0002816763

is currently an SAP Gold partner, participating in the following engagement model/s*:

SAP PartnerEdge Service	Consulting Services: SAP solution design, development, implementation, and integration guidance
-------------------------	---

COMPETENCY

On the date of issue, the partner has achieved the following competency and specialization designation(s). These designations demonstrate an SAP partner's maturity and expertise in delivery of the solution, or line of business level (LoB), or end-to-end process transformation.

COMPETENCY	SPECIALIZATION	TIER
Intelligent Enterprise	Recruit to Retire	None
Human Capital Management	Compensation and Commission Core HR and Payroll Learning Talent Management	Expert
SAP Business Technology Platform	Analytics and Planning Application Development and Integration Database and Data Management	Expert
Customer Relationship Management	Sales and Service	Essential
GROW with SAP	SAP S/4HANA Cloud Public Edition	Essential

SAP PartnerEdge

CERTIFICATE

Kaar Technologies Saudi for Information Technology - Saudi Arabia - Riyadh

Continuation

Spend Management	Strategic Sourcing	Essential
Supply Chain Management	Supply Chain Logistics	Essential

*For additional information on engagement models, partner level, partner dimensions and competencies please reference
https://partnedge.sap.com/content/dam/public/dni/cert/Partner_Certificate_Info.pdf

Upon request and in accordance with applicable statutory provisions, regulations or procurement law, SAP is able to issue this certificate in local language and signed by an SAP signatory. To request, please contact the following email-address: partner@sap.com

This is a system generated certificate and therefore not signed by SAP. This certificate is subject to the terms and conditions of the signed and currently valid SAP PartnerEdge agreement and its schedules entered into by and between SAP and Kaar Technologies Saudi for Information Technology.

SAP PartnerEdge



3.10 Experience in Similar Solution

SIDF - Procure to Pay Implementation Project

This section highlights KaarTech's expertise in P2P application, using various technologies to meet SWA's requirements.



Business Transformation Study | Public Sector | Kaar Technologies

Procure to Pay Solution implementation for a leading Public Sector Agency in Kingdom of Saudi Arabia



The Client is a leading Public Sector organization who provides financial and advisory services for various companies in the Kingdom. They support growth and development of local industries and assist in upgrading their level of performance.

The client needed a streamlined and efficient approach to manage the procurement process from the initial Request for Proposal (RFP) to the certificate of completion. Kaar Tech's expertise in providing end-to-end solutions proposed implementing the P2P (Procure-to-Pay) solution, structured into four main stages: RFP Process, Committee Process, Contract Preparation, and Certification of Completion, ensuring accuracy and compliance throughout the process.





Procure to Pay Solution implementation for a leading Public Sector Agency in Kingdom of Saudi Arabia





Industry Public Sector Products & Services Financial and Industrial Services Location Kingdom of Saudi Arabia Employees 2500+ Solution KaarTech's Procure to Pay Solution	Kaar Technologies implemented P2P Procure-to-Pay System, a streamlined and efficient approach for procurement management from RFP to completion certificate. Before: Challenges and Opportunities • Users usually need to fill all data in a form and submit it manually for the concerned stakeholders for their approval. On approval, manual PR creation is required in SAP. • The evaluation & qualification of vendor after submissions is tedious and involves heavy paperwork involving several stakeholders • Awarding of contract again requires tedious manual document preparation. Why implement KaarTech's Procure to Pay Solution • There is no standard process available in SAP to cover the Business specific requirements on custom approval mechanisms. • The pre-approvals & workflows required for both RFP floating, as well as vendor evaluation and selection varies business to business based on industry standards. After: Value Driven Results • Automates the current manual process for form filling and departmental approvals. • Reduces approval time, significantly boosting efficiency and simplifying tracking, monitoring, and recording changes. • Delivers customized solutions tailored to specific business needs with flexible approval mechanisms. • Enables seamless configuration, ensuring relevant departments efficiently handle RFP approvals, vendor evaluation, selection, and contract awarding.	Automates the existing manual process Accelerates Approval times Provides Bespoke solutions with adaptable approval workflows Facilitates seamless configuration, ensuring relevant departments effectively manage RFP approvals, vendor evaluations, selections, and contract awards.
---	---	--

MWAN - Procure to Pay Automation Project

Transparent and Efficient Procurement Processes for a Leading Public Sector Organization in KSA



The client is a national entity focused on enhancing resource management and operational efficiency. With a mandate to drive sustainable growth, they sought to modernize their enterprise systems, integrating advanced technologies to streamline operations, improve decision-making, and foster a culture of innovation.



KaarTech

Project Overview

This project aims to address inefficiencies in procurement, approvals, and payments. The P2P solution streamlined RFP creation, committee approvals, and payment workflows, enhancing transparency, compliance, and efficiency while seamlessly integrating with existing systems for end-to-end procurement automation.

Business Pain Points



Business Outcomes



Value Derived

The client achieved substantial time and cost savings with automated procurement processes. The solution improved transparency, compliance, and payment timelines, eliminating manual inefficiencies. Integration with external platforms ensured seamless end-to-end management of procurement, from RFP to vendor payment, delivering significant operational benefits.

KaarTech

AI Expertise- Saudi Aramco



This section showcases some of KaarTech AI expertise and project experience with Saudi Aramco.

Voice enabled Ariva Bot

Project Objective

Entail enabling voice-operated functionality across Aramco's software with Spotfire integration allowing hands-free interactions

Project Highlights

- Speech to text model
- Python middleware
- Integration with SpotFire SDK



Asphalt Quota optimization

Project Objective

Enhance the Quota allocation and distribution process due to excessive manual work and subjective judgement

Project Highlights

- Prediction model using IBM watson
- Enhanced Quota allocation to customers
- Reduced manual work and subjective judgement



MPS (Miscellaneous Payment System)

Project Objective

Develop a mobile application that simplifies and automates the invoice request process

Project Highlights

- CR to scan the invoice
- ABAP Based Naive Bayes Classification Model
- Invoice type prediction
- Mobile app




Gen AI powered Chatbot

Project Objective

To develop a chatbot that understand complex enterprise documents and answer user queries

Project Highlights

- Enterprise documents understanding
- RAG based generative AI training
- Human like chat bot interaction on enterprise documents
- Open source LLM models



AI Expertise- MOTIVA

Meeting Minutes generator with GenAI



Understanding the Customer's Struggles

- Lack of clear and efficient way of summarizing meetings
- Dependence on manual notes taking, summarizing and sharing
- Lack of action tracking and collaboration



Addressing the Customer's Needs

- The entire meeting audio file is summarized to give well-documented MOM
- Interface that users can access, get the summary, action items, attendees and details in one place



Transforming the Customer Experience

- Automate the task of making meeting minutes in order to save time and resources
- Capture the summary, easy tracking of actions in a more accurate and efficient manner
- A User-Friendly Digital Interface to facilitate post-meeting analysis

Founded: 1998

Houston, Texas, US

MOTIVA

Motiva Enterprises, LLC is an American company that operates as a wholly owned US subsidiary of Saudi Aramco. Motiva operates as a distributor of Shell and 76 branded gasolines within its operating territory.

Technology:

NEXT.js

OpenAI



Meta AI
Llama-3



AI Expertise- Reckitt

Demand Forecasting



Understanding the Customer's Struggles

- Uncertain Inventory Management and Inefficient Resource Allocation.
- Reduced Customer Satisfaction.
- Missed Marketing Opportunities, Difficulty in Competing and reduced ROI.



Addressing the Customer's Needs

- Harness the art of sales forecasting to predict market trends and plan for future demand.
- Embrace demand forecasting using demand signals to optimize inventory levels
- Identify the right time to make an order in market for raw materials using commodity nerve centre application



Transforming the Customer Experience

- Enhanced Confidence in Decision-Making and Streamlined Marketing Operations.
- Enhanced Resource Allocation and Optimized Sales and Marketing Strategies.
- Better Inventory Management, Effective Marketing and Promotions.

Founded: 1999

Slough, Berkshire

reckitt

Reckitt Benckiser Group PLC is a global consumer goods company that produces health, hygiene, and nutrition products.

Technology:

XGBoost

LightGBM



databricks

Demand Forecasting




Optimizing Media & Promo Spends



Understanding the Customer's Struggles

- Inability to Measure the Separate and Combined Influence of Advertisements and Promotional Offers on Online Sales, In-Store Sales and ROI
- Inefficient Allocation of Media Advertising and Promotional Budgets.



Addressing the Customer's Needs

- Measuring the influence on Sales & ROI by leveraging 30 different Promotional offers data collected from various streams.
- Draw efficient approach to share and split investment between different Ad Platform and Discounts or Promos



Transforming the Customer Experience

- Improved decision-making on media ads and promo offers by optimizing timing and placement.
- Maximized ROI by managing multiple product groups.
- Centralized diverse investments

Optimizing Media & Promo Spends



Understanding the Customer's Struggles

- Struggling with inefficient sales data management and enduring repetitive data processing tasks for disparate downstream applications.
- Unable to sustain a unified source of truth for critical company data like Sales and Media.



Addressing the Customer's Needs

- Successfully implemented a unified source of truth for multiple data sources, bolstering existing and forthcoming internal data products
- Thorough data quality checks and fixes are consistently performed across all available data sources, with ongoing monitoring & support using AI & ML.



Transforming the Customer Experience

- Enhanced Database Management, Reduce cost and Time of Data Processing.
- Centralized database location and data for all data and other use cases.
- Improved overall Data Quality & Governance for all organization's data.

Founded: 1999
Slough, Berkshire



Reckitt Benckiser Group PLC, a global consumer goods company that produces health, hygiene, & nutrition products.

Technology:



Founded: 1999
Slough, Berkshire



Reckitt Benckiser Group PLC, a global consumer goods company that produces health, hygiene, & nutrition products.

Technology:




3.11 Experience in Similar Geography

This Section highlights KaarTech Tech's expertise in similar geographies like SWA and to meet their requirements.




3.12 Experience in Similar Integrations

KaarTech is the only Partner who has done massive integrations with all public sector applications such as SADAD, SIMAH, SAMA, BAYAN, GSB. KaarTech brings unmatched experience of deep understanding and knowledge of such integrations.

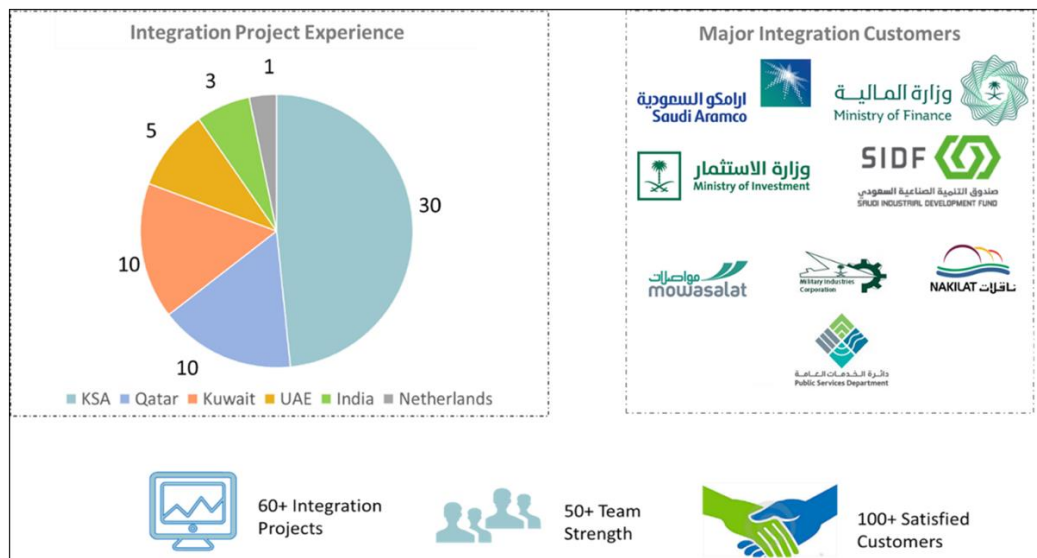

The diagram below shows the High Complex Technical Integration delivered in a record time.

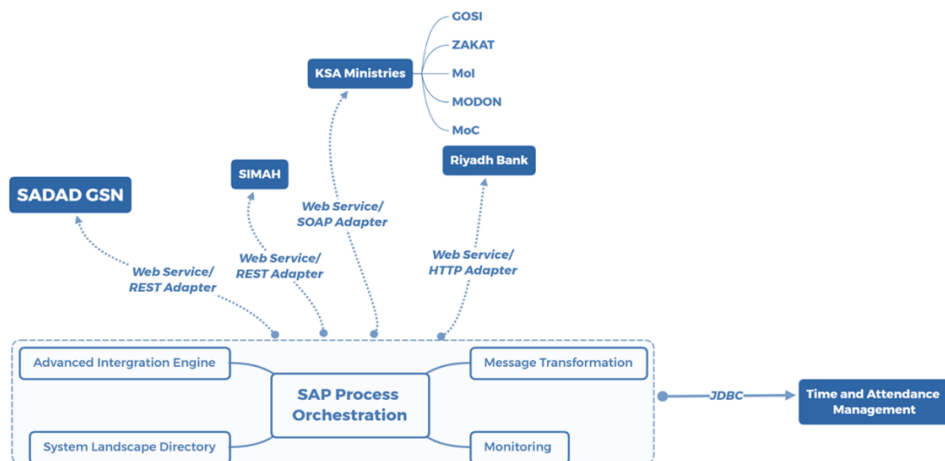

- First Partner to Integrate SADAD successfully 4 years ago.

About the client				
 Public Sector	 Financial and Industrial Service	 Kingdom of Saudi Arabia	 10,000+ Employees	 SAP – SADAD Integration

Key Business Challenges	Value-Driven Results
- File processing was not possible during Ramadan and Hajj vacations (non-working days) - Duplication and incorrect transactions were common due to heavy work loads - Business users were not happy with the transaction delay between SADAD and SAP - Difficulty with manual uploads/downloads from the SADAD portal	- Failures will be handled automatically - System will remain functional and in synchronization during non-working days - Processing time will be reduced from hours to seconds - The Error Handling mechanism will take care of failures - Availability of an Automated System for monitoring and handling transactions

Key Highlights			
 500+ successful transactions were observed on the first day	 24/7 Active System without any interruptions or delays	 Highly secure SSL communication using Server and Client digital certificates	 First successful integration between SAP and SADAD in the KSA

- Below are other Integrations in Public Sector delivered by KaarTech



Name: MIC (Ministry of Commerce)

Reason for Integration: To collect information on Saudi Companies (Registrations, Product and Shareholder Details)

Benefits:

- Accurate Information about Saudi registered companies
- Validity of the companies can be checked



Name: SIMAH (Saudi Credit Bureau)

Reason for Integration: To check the credibility of clients.

Benefits:

- Immediate Credibility Analysis of clients
- Easy decision making process



Name: AMER (National Contact Center)

Reason for Integration: Easy processing of customer queries.

Benefits:

- Statistic Report from Amer for frequent queries Raised.
- Integration with Saudi National Contact Center Agent



Name: GSB (Government Service Bus)

Reason for Integration: Transfer of information from SIDF to other government entities.

Benefits:

- Business to Business interaction
- Easy transfer of data/information



Name: ABSHER (Ministry of Commerce)

Reason for Integration: E-Signing of documents.

Benefits:

- Faster processing of loan approvals
- Zero paperwork
- Corrections can be made easily on the system



|| 4. Proposed Solution

KaarTech is proposing the below indicative solution to cater the business requirement of SWA & has depicted the same for SWA's understanding.

4.1 Overview

KaarTech proposes the implementation of a custom-built RFP Lifecycle Add-On integrated with SAP S/4HANA to fully digitize and streamline the end-to-end procurement lifecycle at SWA. The P2P solution bridges the current procurement process gaps from Request for Proposal (RFP) through to Certificate of Completion (COC). The Add-On will support internal workflows, integrate with internal and external systems including SAP Ariba, TARASUL (Document Management System), and Thiqa, and ensure procurement processes are efficient, traceable, and compliant.

The solution encompasses:

- RFP Process
- Committee Process
- Contract Generation Process
- Contract Management Process
- Certificate of Completion Process
- Centralized repository for RFP documents
- Proposed AI Use Cases

4.2 Business Process

KaarTech's P2P (Procure-to-Pay) solution is a streamlined and efficient approach designed to bridge the gap in the existing SWA procurement process from the initial Request for Proposal (RFP) to the Certificate of Completion (COC) Process.


The solution is structured into four main stages:

- Request for Proposal (RFP) Process
- Committee Process
- Contract Generation Process
- Certification of Completion (COC) Process

Below is a step-by-step explanation of the entire process, meticulously detailed to ensure accuracy and compliance to showcase the below,



- Blue – Refers to steps that will be automated by the newly developed P2P Solution
- Red – Refers to steps that are currently automated and available in SWA SAP Landscape
- Purple – Refers to Approvals available as standard in P2P & SAP Solution
- Orange – Refers to steps that shall be manually performed by the End User

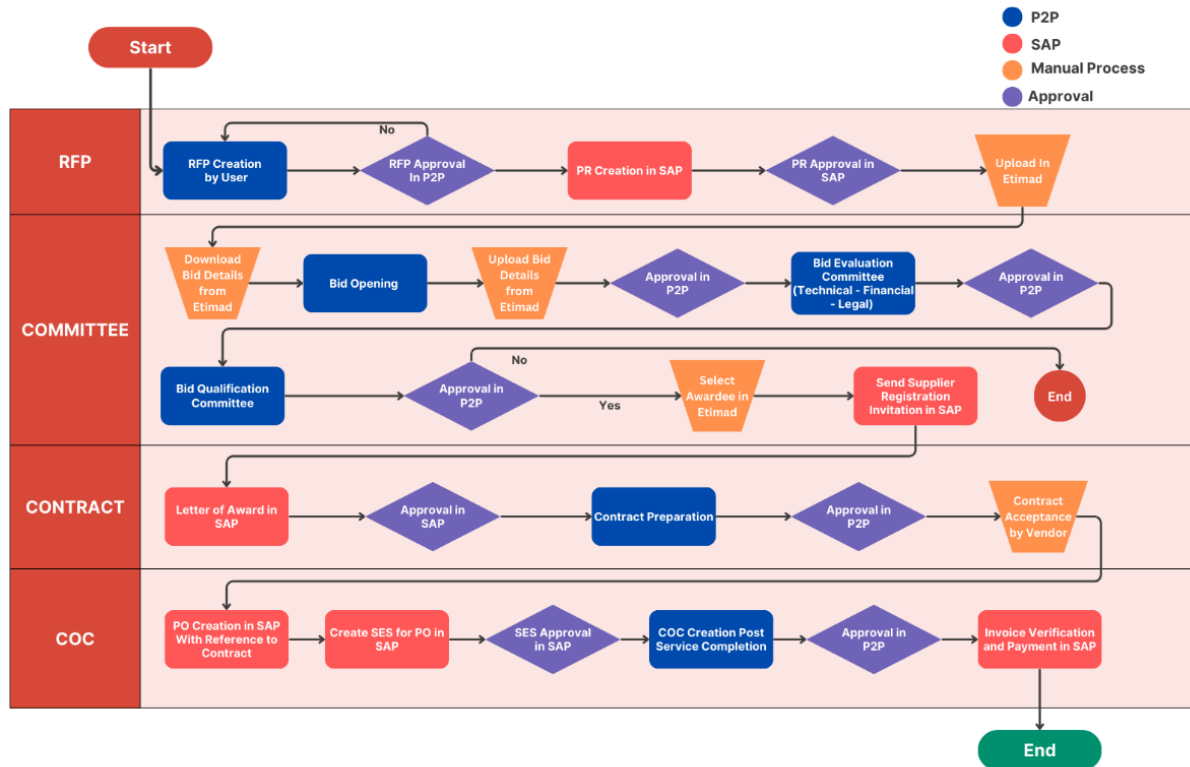

In alignment to the vision of SWA digitally improving the Supply Chain Process, KaarTech also proposes the below features sets to be developed,


- Contract Management Process
- Centralized Repository to store RFPs
- Reports

4.2.1 Scope 1: Complete Procurement Lifecycle Enablement

This scope covers the full procurement lifecycle including RFP creation, evaluation, award, PO generation, and contract creation.

4.2.1 RFP Process

The process is mapped to the proposed P2P solution as follows:

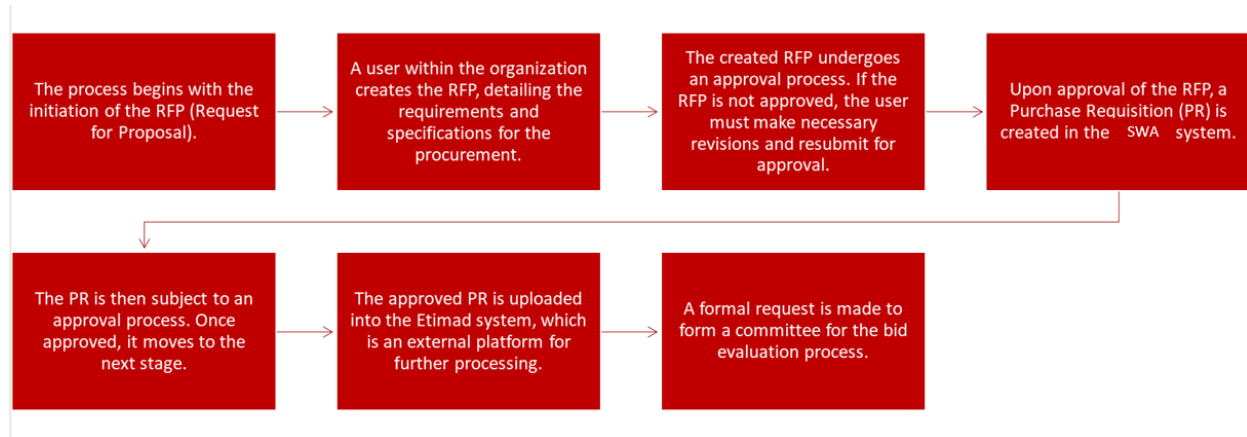

RFP Creation & Structuring

- Role-based interface for RFP initiation
- Structured forms to define procurement category, project scope, and BOQ
- Automated committee assignment (Technical, Evaluation, Qualification)
- Scoring criteria and timeline control
- Auto PR creation in SAP upon RFP approval
- Configurable workflow for change requests or scope extensions

Requirement	Description	Compliance (Yes/No)	Solution & Remarks
Role-based access	Configurable roles to allow requesters to initiate RFPs	Yes	Role-based access is implemented in Add-On, with user permissions defined per role, ensuring secure and appropriate access control for different user types.
Guided Interface	Interface to define project requirements, procurement category, and Bill of Quantity (BOQ)	Yes	Customizable guided form with dropdowns and input fields for procurement details. Simplifies RFP creation with pre-defined templates for project types.

Requirement	Description	Compliance (Yes/No)	Solution & Remarks
Committee Assignment	Assign roles to Technical, Evaluation, and Qualification Committees	Yes	Committee assignment is done through the system interface, with assignment functionality based on RFP requirements, streamlining the RFP review process.
Scoring Criteria & Timeline Control	Define scoring criteria and control timeline	Yes	Configurable scoring matrix with predefined ranges. This ensures that proposals are evaluated based on predefined criteria within the agreed timeline.
Project Estimated Price	Specify estimated project price in RFP	Yes	Price input field with validation for estimated cost. This enables clear budget expectations for vendors.
Approval Workflow	Approval workflow based on the nature of the project	Yes	Multi-step approval flow with configurable rules for each project type. Ensures the correct stakeholders approve the RFP before publication.
Automatic PR Creation	Upon RFP approval, create PR in SAP S/4HANA	Yes	API-based integration with SAP S/4HANA to automatically generate PR based on RFP details, efficiently moving RFP to the procurement stage, reducing manual effort.
Scope Change/Extension Request Workflow	Option for modifying RFP scope with approval flow	Yes	Workflow for scope change requests, including approval steps and documentation. Handles any scope changes or extension requests with appropriate oversight.
PR with Header & BOQ Items	PR to include header and items (BOQ) details	Yes	The PR schema supports itemized entry for detailed BOQ information, ensuring that the PR is




Requirement	Description	Compliance (Yes/No)	Solution & Remarks
			complete with all necessary line-item details.

Purchasing Officer Dashboard

- Dedicated UI for RFP intake, extension tracking, and modifications
- Event update interface to log Etimad publication, vendor invites, and documentation

Requirement	Description	Compliance (Yes/No)	Solution & Remarks
RFP Request Receiving UI	UI for purchasing officer to manage received PRs and RFP events	Yes	Dedicated dashboard for the purchasing officer with action buttons for each task. Provides streamlined access to RFP requests and related updates.
Publication Confirmation	Record publication date and reference number after posting on government portal	Yes	Field to input confirmation details, upload screenshot/documentation. Ensures compliance with government procurement requirements.
Invited Vendors Log	Track vendors invited to RFP	Yes	Log of vendor invitations stored with timestamps. This enables transparency and traceability of vendor invitations.

Vendor Clarification Workflow

- Manual intake of queries from Etimad
- Internal routing via Add-On to Technical Committee
- Timestamped, secure clarification log and documentation tracking




Requirement	Description	Compliance (Yes/No)	Solution & Remarks
Vendor Clarification Log	Record vendor clarifications with details	Yes	Vendor name, clarification reference, date received, and attached docs stored. Provides a complete audit trail for all vendor interactions during the RFP process.
Internal Routing	Clarifications routed to Technical Committee and Purchasing Officer	Yes	Workflow ensures routing to proper stakeholders based on RFP stage, streamlining clarification handling and ensuring timely responses.
Clarification Status Tracking	Track clarification status (Pending, Responded, Reviewed)	Yes	Status indicators for each clarification in the log, providing clear visibility on the status of all clarifications.

4.2.1.1 Committee Process

The Committee Process involves 3 stages as described below,

1. Bid Opening Committee (BOC) Process
2. Bid Evaluation Committee (BEC) Process
3. Bid Qualification Committee (BQC) Process

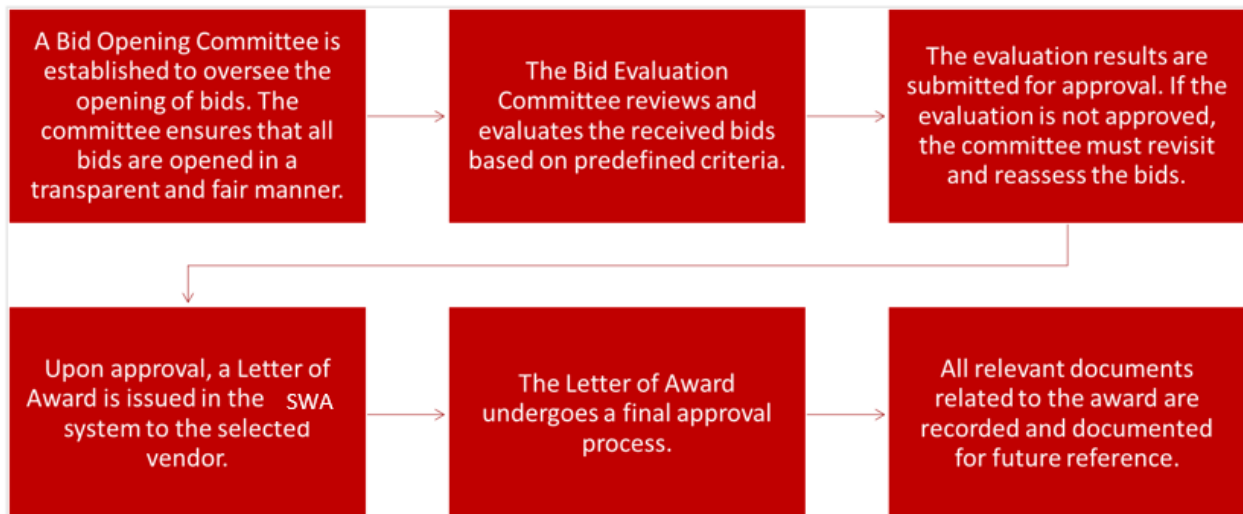


Bid Opening and Proposal Intake

- Manual upload of vendor bids from shared location (RPA-enabled)
- Review and comparison of Etimad and submitted offers
- Digital approval of bid opening records

Requirement	Description	Compliance (Yes/No)	Solution & Remarks
Bid Opening on Government Portal	Bid opening handled on government portal by official committee	Yes	Integration with Etimad portal for bid opening process ensures compliance with government regulations and ensures transparency.
Offer Upload	Coordinator uploads offers into RFP lifecycle	Yes	File upload feature with version control, centralizing bid management and ensuring traceability of offers.
Committee Review	Committee reviews submitted offers and compares with Etimad offers	Yes	Integrated review interface to compare uploaded offers with Etimad records, supporting accurate and compliant evaluation.
Approval and Submission	Approval and submission to Technical Evaluation Committee	Yes	Workflow routing for sign-off and submission for technical evaluation, streamlining the approval process and ensuring all committee members sign off.

Technical Evaluation

- Predefined scoring forms
- Coordinator consolidation and managerial review workflows



Requirement	Description	Compliance (Yes/No)	Solution & Remarks
Predefined Scoring Criteria	Use predefined scoring criteria for evaluations	Yes	Scoring templates based on project category can be customized to ensure evaluations are standardized and compliant.
Evaluator Input & Consolidation	Evaluators input scores, coordinator consolidates, and manager reviews	Yes	Scoring form for evaluators, automated consolidation for coordinator. Simplifies the evaluation process, reducing errors and time.
Internal Routing	Routed to Technical Evaluation Committee for input	Yes	Configurable routing of evaluation tasks ensures that all evaluators have proper access and visibility.

Evaluation Committee Review

- Commercial/technical evaluation by the Evaluation Committee
- Digital preparation and approval of award letters

Requirement	Description	Compliance (Yes/No)	Solution & Remarks
Handles Technical and Commercial Evaluations	Committee evaluates both technical and commercial proposals	Yes	Dual-stage evaluation process separates technical and commercial evaluations to enforce a transparent and unbiased evaluation process.




Award Recommendation	Secretary prepares award letter, with digital signatures required	Yes	Automated award letter generation with integrated digital signature feature streamlines the contract award process.
-----------------------------	---	-----	---

Qualification Committee

- Role-based evaluation panel
- Document-based scoring with justification
- Final decision recording in P2P system

Requirement	Description	Compliance (Yes/No)	Solution & Remarks
Committee Assignment	Assign roles to the qualification committee	Yes	User role management to assign members to the qualification committee, simplifying committee management.
Evaluation Criteria Setup	Define criteria for qualification evaluation	Yes	Configurable evaluation templates allow flexibility based on project type.
Document Review & Score Entry	Document review workflow with score entry and justification	Yes	Integrated document upload with review process and scoring form for evaluators, ensuring comprehensive and transparent evaluation.

Award Approval & SAP PO Creation


- Automatic PO creation upon final award approval
- PO linked to the RFP record in SAP
- Capability to invite non-registered suppliers



Requirement	Description	Compliance (Yes/No)	Solution & Remarks
Non-registered Supplier Invitation	Invitation to non-registered suppliers	Yes	The system allows inviting unregistered vendors, ensuring inclusivity in the procurement process.
Automatic PO Creation in SAP	PO creation upon award approval, linked to PR	Yes	Integration with SAP S/4HANA automatically generates a PO, eliminating manual data entry and reducing errors.
PO Linked to RFP Record	Link PO to the original RFP record	Yes	PO and RFP records are connected for traceability, maintaining a clear audit trail.

4.2.1.2 Contract Generation Process

Letter of Award & Contract Generation Process

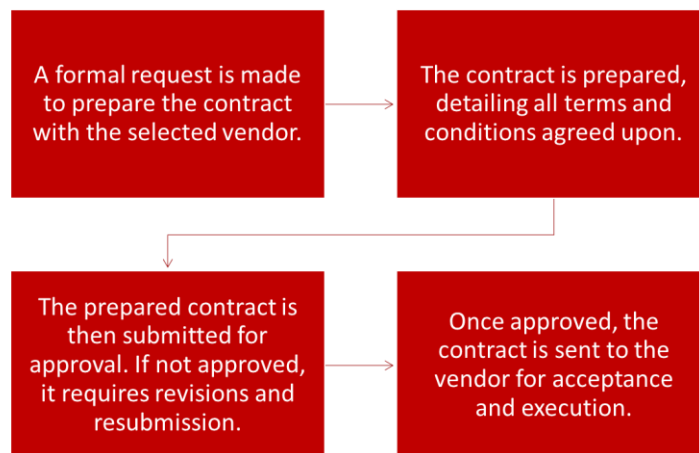

- Auto-generation of Letter of Award and contracts based on pre-approved templates
- Digital signature and archival linked with PO
- Integration with SAP Ariba for LOA and contract exchange



Requirement	Description	Compliance (Yes/No)	Solution & Remarks
Letter of Award Generation	Generate letter of award from system	Yes	Template-driven LOA generation with approval routing ensures a standardized LOA creation process.
Contract Creation from Template	Generate contracts from predefined templates	Yes	Template library with 8 contract types ensures uniformity and compliance in contract creation.
Digital Signature and Approval	Internal approvals with digital signature	Yes	Digital signature integration for contract finalization complies with electronic signature standards.
LOA and Contract Archiving	Archive LOA and contracts, link to PO	Yes	Document storage system with secure archiving and linkage to PO ensures compliance and easy retrieval of contracts.

4.2.2 Scope 2: Contract Management & Certificate of Completion

4.2.2.1 Contract Management Process

KaarTech agrees to provide Contract Management Feature In Contract Process as part of the P2P Solution. This feature shall allow the purchasing officer to monitor the Contract/PO, its services along with the service line item values, its Consumption, its delivery period & its delivery status. Also, it shall allow the purchasing officer to rate the vendor against the contract.


KaarTech agrees to provide Change Request Feature In Contract Process as part of the P2P Solution. This feature shall allow the user to initiate a Change Request (modification of scope or contract value against a Contract/PR to the Vendor.

Requirement	Description	Compliance (Yes/No)	Solution & Remarks
-------------	-------------	---------------------	--------------------




Change Order Request Workflow	Enable creation, approval, and processing of contract change orders	Yes	The solution supports configurable change order workflows allowing users to initiate changes with proper justifications, routing them for approval and implementation. All changes are tracked with audit logs for governance.
Milestone & SLA Tracking	Track contract execution milestones and service-level agreements	Yes	Built-in milestone tracking with alerts and SLA monitoring dashboard. Allow project owners to proactively manage deadlines, deliverables, and vendor performance.

4.2.2.2 Certificate of Completion Process

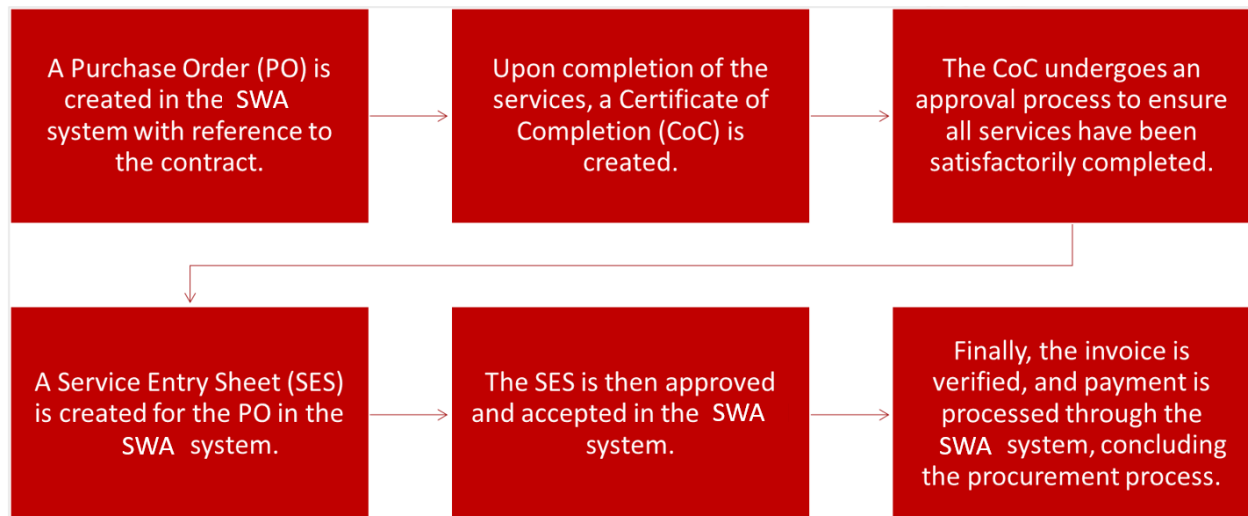


- COC generation with approval workflows and digital signature
- COC record archival and linkage to original contract/PO

Requirement	Description	Compliance (Yes/No)	Solution & Remarks
-------------	-------------	---------------------	--------------------



Certificate of Completion Automation	Generate partial or complete completion certificates with workflow and signatures	Yes	Certificate templates auto-generated based on project completion status. Integrated with approval workflows and digital signatures and archived in the system. SAP Ariba integration enables seamless certificate sharing with vendors.
---	---	-----	---

4.2.3 Scope 3: Centralized RFP Repository in SAP S/4HANA

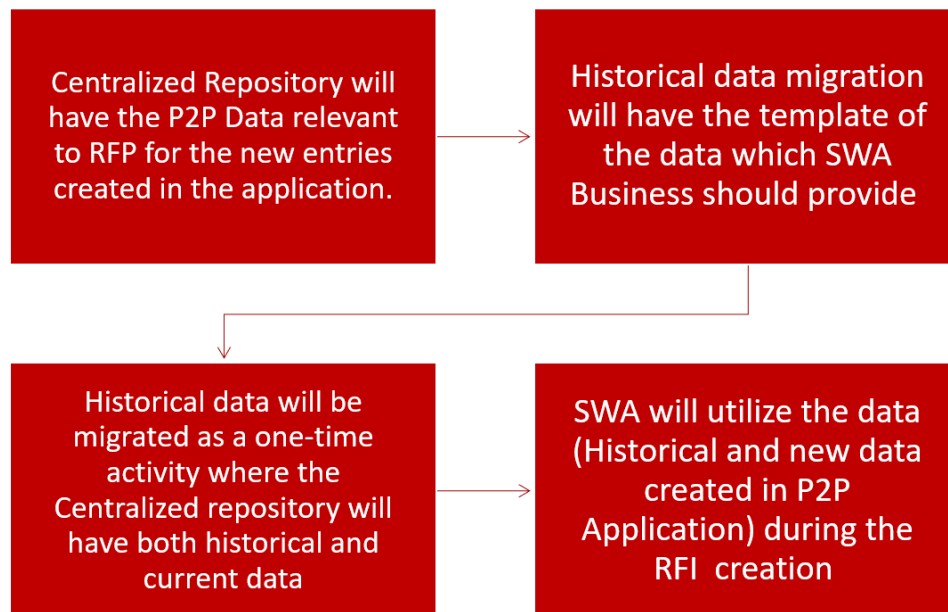

- Historical and new RFP storage in SAP S/4HANA
- Keyword, tag, and metadata-based search
- Live reuse of past templates, scopes, and scoring structures

Requirement	Description	Compliance (Yes/No)	Solution & Remarks
Store Historical & New RFPs	Maintain both newly created	Yes	All RFPs, including metadata, documents, and approvals, are archived in a centralized SAP S/4HANA repository. This enables




	and past RFPs in SAP S/4HANA		long-term storage, traceability, and audit readiness.
Search & Filter Interface	Provide searchable interface using tags, keywords, and filters	Yes	Powerful search interface with filtering by project name, committee, status, scoring criteria, or tags. Enables quick retrieval of relevant RFPs for reference or reuse.
Reuse of Scopes, Criteria & Templates	Reuse scopes, scoring criteria, templates during new RFP creation	Yes	Template engine allows reuse of prior RFP components (e.g., technical scope, evaluation matrix), ensuring consistency and faster preparation of new RFPs. Promote standardization and efficiency.

4.2.4 Scope 4: AI Service Provision

As part of the RFP Lifecycle Add-On initiative, KaarTech proposes an integrated AI-Powered Smart Evaluation Layer fully embedded within the existing P2P framework, designed to deliver intelligent automation, quality enhancement, and predictive insights throughout the tendering and evaluation lifecycle.

The AI service provision comprises a suite of capabilities built using industry-leading machine learning (ML), Large language models (LLMs), natural language processing (NLP), and intelligent automation frameworks, while ensuring seamless integration with SAP S/4HANA, SAP Ariba, and the RFP Lifecycle Add-On.

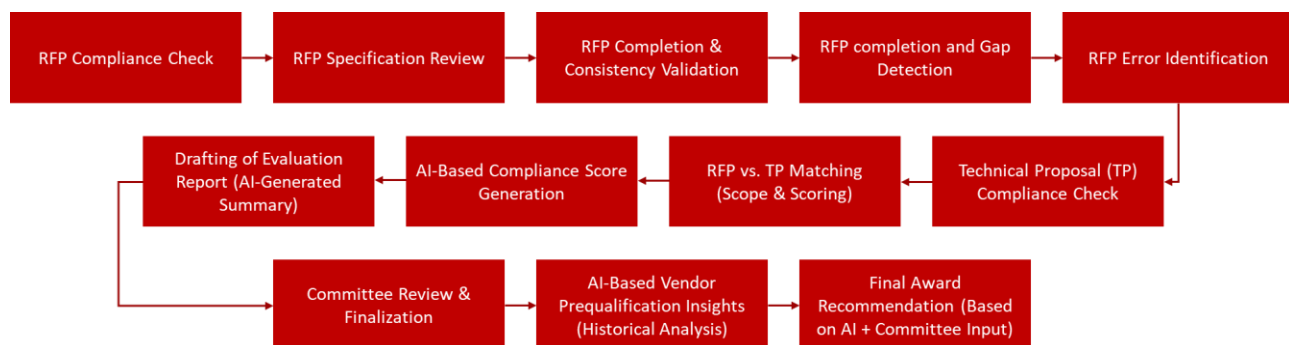

Key AI Use Cases and Proposed Solutions



AI Use case ID	Use Case	AI-Driven Feature	Solution Description
UC-01	Tender Content Review (Review tender specifications and content before issuance, analyze and propose)	TenderGuard – Automated Tender Review	AI-driven solution that reviews tender specifications and content prior to issuance. TenderGuard analyzes documents for completeness and relevance, proposing additions or modifications by referencing the project scope and past tender histories. This ensures tenders are robust and aligned with both organizational and regulatory standards.
UC-02	Document Validation (Validate completeness and correctness of tender documents before release, and detect gaps, duplication, or potential inconsistencies)	DocuSure – Intelligent Document Validator	DocuSure validates the completeness and correctness of tender documents before their release. It automatically detects gaps, duplicates, and inconsistencies, using predefined templates and compliance checklists. This reduces manual oversight, eliminates errors, and guarantees that all required elements are present for successful tendering.
UC-03	Proposal-Tender Matching (Analyze technical proposals and compare them with the tender	TechCompare – AI Proposal Analyzer	TechCompare analyzes technical proposals received from vendors and compares them against the tender specifications. By leveraging AI analytics, it identifies discrepancies, evaluates compliance, and highlights deviations. This streamlines the evaluation process,



	specifications to assess compliance)		ensuring only proposals meeting all requirements proceed to the next stage.
UC-04	Intelligent Evaluation Report Drafting (Prepare and draft bid evaluation reports intelligently and accurately based on committee outputs)	EvalDraft – Smart Report Generator	EvalDraft prepares and drafts bid evaluation reports by synthesizing committee feedback and assessment scores. Using AI, it structures the reports to capture critical evaluation insights accurately and objectively, minimizing manual intervention and ensuring consistency and transparency in reporting.
UC-05	Vendor Prequalification Analysis (Support vendor prequalification by analyzing historical data linked to performance evaluation and compliance models)	PreQualytics – Vendor Prequalification AI	PreQualitics supports vendor prequalification by analyzing historical data related to vendor performance and linking it with compliance models. Leveraging machine learning, it objectively scores vendors, surfaces risk factors, and enhances the selection process, ensuring qualified and reliable vendors are shortlisted for the RFP process.

Integration Architecture

System	Integration Purpose	Integration Mode
--------	---------------------	------------------




RFP Lifecycle Add-On	Embed AI insights within the tender lifecycle UI (RFP creation, evaluation, award)	Embedded APIs & inline widgets
SAP S/4HANA	Sync vendor master, PRs, POs, project details, budget data	REST APIs via SAP BTP CF Integration Suite
SAP Ariba	Exchange of contract, LOA, and evaluation outcome	REST APIs via SAP BTP CF Integration Suite
Centralized RFP Repository	Use historical RFPs as training corpus and reference	REST APIs via SAP BTP CF Integration Suite
THIQAH (Vendor Registry)	Pull qualification status and vendor categorization for training the AI model	REST APIs via SAP BTP CF Integration Suite

Specifications

Layer	Platform / Framework	Purpose
Cloud Platform	Google Cloud Platform (GCP)	Primary hosting for all AI workloads; ensures regional data residency and SWA, Saudi, and NCA data security compliance
AI/ML Platform	Vertex AI (GCP)	Unified model development, training, deployment; supports LLMs, NLP, OCR, MLOps, in Arabic and English
Large Language Models (LLM)	Vertex AI LLMs, Gemini, or Arabic-specific LLMs (hosted on GCP)	Advanced document understanding, proposal summarization, compliance checks, all with Arabic support
OCR & Image Text Extraction	Google Vision AI / Vertex AI OCR (Arabic support), Tesseract OCR	Extracts Arabic text from PDFs, images,




		handwritten documents, and scanned files
Text Analytics (Arabic NLP)	Vertex AI NLP APIs, spaCy/arNLP, fine-tuned BERT models for Arabic	Automated extraction, validation, clustering, and comparison of Arabic-language tenders/proposals
Machine Learning Frameworks	TensorFlow, PyTorch (within Vertex AI)	Custom and pre-trained models for Arabic data: vendor scoring, anomaly, gap, and risk analysis
Integration / Data Exchange	REST/OData APIs, SAP BTP Integration Suite	Secure workflow integration with SAP S/4HANA/Ariba and RFP Add-On
Reporting / Workflow Automation	Vertex AI Pipelines, GCP Workflows, SAP Business Workflow	Automates analytics, evaluation report creation, multi-lingual report outputs in Arabic
Storage / Data Lake	Google BigQuery, Cloud Storage	Stores and analyzes historic RFP/proposal data in Arabic for AI model training, validation, and audit
Security & Compliance	GCP IAM, Google Cloud DLP, Encryption, SAP Security, TLS 1.2+/AES-256	Data protection in line with SWA, National Cybersecurity Authority (NCA), and KSA law; audit logs, alerts
Monitoring / Validation	Google Cloud Monitoring, Vertex AI Model Monitoring, Custom Dashboards	Tracks performance, usage, retraining needs, compliance—including Arabic-language flow and audit trails

AI Governance and Explainability




- **Explainable AI (XAI):** All AI outputs (e.g., recommendation on evaluation or document gaps) will be accompanied by rationale and confidence score to aid human-in-the-loop decisions.
- **Human Override:** Users retain full control to override AI suggestions. AI acts as an assistive layer, not a decision enforcer.
- **Auditability:** All AI-based suggestions and outputs will be logged and stored with version tracking for compliance.

Benefits to SWA

- 40% reduction in tender review cycle time.
- 30% fewer errors or reworks in tender documentation.
- Delivers data-driven, objective evaluations and transparent reporting.
- Improves vendor selection quality and mitigates procurement risks by leveraging historical and performance data.
- Streamlines end-to-end RFP lifecycle management for greater operational efficiency.

Compliance and Deployment Readiness

Requirement	Compliance	Remarks
Seamless Integration with RFP Lifecycle Add-On	Yes	AI layer built as microservices and exposed via REST APIs to integrate with Angular-based frontend
SAP S/4HANA & Ariba Integration	Yes	Through SAP BTP Integration Suite
Data Sovereignty and Privacy	Yes	AI models trained and hosted within SWA's SAP BTP environment; no external data transfer
Multilingual Support	Yes	NLP models trained to support both English and Arabic tender documents



Model Transparency & Audit Trail	Yes	All AI-generated suggestions are timestamped, versioned, and auditable
No Lock-In	Yes	AI models built using open ML frameworks with retrainable pipelines

4.3 Standard Features

Epic	Feature
RFP	RFP Create
RFP	RFP Change/Edit
RFP	RFP Inbox
RFP	RFP - My Requests
RFP	RFP Dashboard
RFP	Budget Allocation Creation
RFP	Budget Allocation - My Requests
Committee	Bid Opening Committee Form
Committee	Bid Evaluation Committee Form
Committee	Technical Evaluation Committee Form
Committee	Bid Qualification Committee Form
Committee	Inbox - Tender list
Committee	Committee Dashboard
Committee	Signature Upload
Contract	My Inbox - Contract
Contract	Contract Preparation Form
Contract	Initial Contract assignment screen
Contract	Signature upload
Contract	Contract Dashboard




COC	COC Preparation and approval Form
COC	COC Dashboard
COC	COC Creation - PO/contract selection screen
Admin	Committee Maintenance
Admin	SLA Maintenance

Note: Above listed are the standard available features as part of the P2P Solution. This shall be discussed and re-validated during the Explore Phase of the Project.

4.4 Additional Features

4.4.1 Official Forms Configuration and Automation

Requirement	Description	Compliance	Solution & Remarks
Form Automation	Generate, populate and store official forms	Yes	Supports forms auto-filled using transaction data, digitally signed, and securely archived.

4.4.2 Internal and External Communication Policy

Requirement	Description	Compliance	Solution & Remarks
Centralized Communication	Internal and committee communications	Yes	All messages and file exchanges occur within the Add-On ensuring traceability, versioning, and security. No external emails are needed.

4.4.3 Committees Maintenance Module

Requirement	Description	Compliance	Solution & Remarks
Manage Committees	Create, update, deactivate roles	Yes	Committee structure maintenance tool validates roles against SAP and



			controls access per role configuration.
--	--	--	---

4.4.4 Committee Delegation Capability

Requirement	Description	Compliance	Solution & Remarks
Task Delegation	Delegate tasks to alternates	Yes	Delegation UI supports delegation of tasks

4.4.5 Tracking System and Dashboards

Requirement	Description	Compliance	Solution & Remarks
Real-Time Dashboards	Visualize status, workload, performance	Yes	Role-specific dashboards display workflow progress, pending items, delays, and performance KPIs in real time.

4.4.6 Notifications and Centralized Inbox

Requirement	Description	Compliance	Solution & Remarks
Centralized Inbox	Task list with filters and actions	Yes	Consolidated inbox with filters by ID, task type, status, and due date.
Automated Notifications	Triggers and email alerts	Yes	Notification engine sends real-time updates by email with deep links to actions. Examples: deadlines, approvals,.

4.4.7 RFP & PR Search and Progress Tracking

Requirement	Description	Compliance	Solution & Remarks
-------------	-------------	------------	--------------------

Search & Progress Tracker	Find records and track status visually	Yes	Allows PR/RFP search by ID, requester, or category. Shows progress bar, pending steps, and ownership visibility for all users.
--------------------------------------	--	-----	--

4.4.8 Full Lifecycle Workflow Integration

Requirement	Description	Compliance	Solution & Remarks
End-to-End Workflow	Integrated object lifecycle from PR to payment	Yes	All stages are linked automatically. Example: PR feeds RFP > Award feeds PO > Contract > CoC > Payment. Fully traceable with history.

4.4.9 Draft Saving and Resumption Feature

Requirement	Description	Compliance	Solution & Remarks
Draft Saving	Save and resume activities	Yes	Users can save work-in-progress drafts across modules. Drafts are tagged, versioned, and resume from dashboard.

4.5 Integrations

4.5.1 With SAP Modules

P2P Applications integrate data from MM, FI and HCM available in the S/4 Environment. Data integrations from the modules are listed below:

- SAP S/4HANA Material Management (MM) – P2P pulls data from the Material Master, vendor, Purchase order, Contract and Service Entry Sheet
- SAP S/4HANA Finance (FI) – Budget details, Cost Centers data integration for RFP Process.
- SAP S/4HANA HCM – Notification emails of the employees, workflow details based on the org structure

4.5.2 With Thiqah System

KaarTech shall integrate P2P Solution with THIQA System based on the below understanding received from SWA,



1. THIQA system shall provide list of qualified vendors for specific services.
2. This qualification based on specific services shall be evaluated in THIQA System.
3. The P2P-THIQA Integration scope is to get the list of qualified vendors from THIQA System based on the specific services in the RFP created in P2P Solution.

4.5.3 With Tarasul System

KaarTech confirms that the P2P Solution provides the option for digital signoff. However, the User should upload the Signature to the P2P Solution as pre-requisite. Also, if required, P2P solution can be planned to integrate with Tarasul to fetch Signature Information based on UID, if the respective API is provided by Tarasul during the Explore Phase of the Project which is planned in M2 of the project timeline.

4.5.4 With Contracts Platform (In-house platform for Contract Management)

KaarTech confirms that the P2P Solution APIs can be consumed by Contracts Platform to fetch required data, if recorded in P2P Solution.

4.6 Workflows

P2P Application supports flexible workflow. Departments with different levels can be configured based on the process of achieving flexibility in adapting the workflow to the respective business.

	LEVEL 1	LEVEL 2	LEVEL 3	LEVEL 4	LEVEL 5
Requestor	Assigner/Approver (ASAP1)	Reviewer (REVV1)	Approver/Return (APRT1)		
Cyber Sec	Assigner 1 (ASGN1)	Assigner/Approver (ASAP1)	Reviewer (REVV1)	Approver/Return (APRT1)	
Op Enterprise Risk	Assigner 1 (ASGN1)	Assigner 2 (ASGN2)	Assigner/Approver (ASAP1)	Reviewer (REVV1)	Approver/Return (APRT1)
Enterprise Architecture	Assigner/Approver 1 (ASAP1)	Assigner 1 (ASGN1)	Reviewer (REVV1)	Approver/Return (APRT1)	
Legal	Assigner 1 (ASGN1)	Assigner 2 (ASGN2)	Assigner/Approver (ASAP1)	Reviewer (REVV1)	Approver/Return (APRT1)
Purchasing	Assigner/Returner & Change RFP (ASRTED1)	Assigner/Approver (ASAP1)	Reviewer (REVV1)	Assigner/Approver/Returner (ASAPRT1)	
Requestor Coordinator	Assigner/Approver (ASAPDS1)	Approver (APRV1)			
	Assign	Assign/Approve	Review	Approve/Return	Special Permissions

Note: Above displayed is to showcase the workflow capability of the P2P Solution. This workflow matrix shall be discussed and finalized during the Explore Phase of the Project.



4.6.1 Workflow Requirements for Approval

Requirement	Description	Compliance	Solution & Remarks
Configurable Workflow Engine	Multi-level approvals, segregation of duties, traceability	Yes	The Add-On features a dynamic workflow engine that supports configurable steps, role-based approvals, escalation paths, and full audit trails to ensure governance and traceability.

4.7 Security

4.7.1 System Administration Requirements

Requirement	Description	Compliance	Solution & Remarks
Multi-Factor Authentication	2FA for all administrative accounts	Yes	Supports integration with identity providers enforcing 2FA (e.g., OTP + Password) for all privileged users.
User Management	Create, modify, deactivate, assign roles	Yes	Admin console provides user access controls through SAP roles
Audit Trail	Immutable logs of all actions	Yes	Every user's action, workflow step, and data change are logged, timestamped, and exportable for audit compliance. Sensitive or confidential data will not be logged
Configuration Management	Adjust workflows and rules without coding	Yes	Admins can modify workflows, notifications, and committees via no-code UI and will be reflected immediately to the system.

Error & Exception Handling	Error logs and auto-alerts	Yes	System error logs accessible with alerts to IT support team for exception handling.
Backup & Recovery	DR-compliant backup schedule	Yes	Supports daily backups, restore points, and compliance with SWA SAP disaster recovery guidelines.
Monitoring Dashboard	Real-time monitoring of activities and health	Yes	Includes a visual dashboard showing system status, RFP progress, pending tasks, and user activity summaries.
Security Compliance	Compliant with national cybersecurity and SWA IT policies	Yes	Regular audits, encryption, access controls, and vulnerability patching mechanisms ensure full compliance.

4.7.2 Solution Hosting and Data Protection Responsibilities

The SAP P2P Application shall be deployed in SWA's SAP BTP Multi Cloud Tenant through Build Work Zone Services. The Consumed Services are SAP Build Work Zone, SAP Integration Suite, SAP Cloud Foundry Runtime.

4.7.2.1 Hosting Requirements

Requirement	Description	Compliance	Solution & Remarks
Containerized Deployment	Host the solution as containerized application on SWA Cloud	Yes	Solution will be deployed using Docker containers in SWA's secure cloud environment with Kubernetes orchestration.
3-Tier Architecture	Ensure separation of presentation, application, and database tiers	Yes	Designed with 3 tiered architecture to comply with enterprise security segmentation standards.

Data Residency Compliance	Must comply with national data laws and regulations	Yes	All data is stored and processed within the country as per regulatory requirements.
Certifications	Cloud provider must have ISO 27001, SOC 2 Type II, GDPR-equivalent	Yes	SWA BTP Cloud tenant is compliant with ISO/IEC 27001, SOC 2 Type II, and local GDPR-equivalent standards.

4.7.2.2 Data Protection and Confidentiality

Requirement	Description	Compliance	Solution & Remarks
Encryption Standards	AES-256 for data at rest; TLS 1.2+ for data in transit	Yes	All storage and communication channels use industry-standard encryption.
Application-Level Readability	Only readable at application level with secure APIs	Yes	Encrypted data is decrypted only within application layer; APIs secured with OAuth and role filtering.
Sensitive Data Protection	Protect RFPs, scores, evaluations	Yes	All classified data tagged and access restricted. Logs and audit trails ensure traceability.
Role-Based Access	Based on least privilege, integrated with SAP IDM	Yes	Role assignments strictly enforced through SAP Identity & Access Management and SAML integration.

4.7.2.3 Information Leakage Prevention

Requirement	Description	Compliance	Solution & Remarks
Audit Logging	Track all access and admin operations	Yes	Immutable logs of all system access, available for audit review and compliance reporting.
Real-time Monitoring	IDS/IPS and monitoring systems in place	Yes	Leverages existing SWA security tooling (e.g., SAP Alert Notification, IDS/IPS) for




			monitoring.
Role-Based Access	Restrict access to sensitive data and admin functions	Yes	Fine-grained RBAC implemented with policy-based controls.
Security Testing	Penetration tests and assessments required	Yes	Security testing conducted at realize phase; findings reported to SWA.

4.7.2.4 Data Ownership and Sovereignty

Requirement	Description	Compliance	Solution & Remarks
SWA Ownership	SWA retains sole ownership of all data	Yes	Contractual and architectural design ensures SWA exclusive data control.
End-of-Contract Procedure	Secure handover and certified deletion	Yes	Contractor provides certified evidence of full data deletion and secure data export during offboarding.

4.7.2.5 Incident Response and Reporting

Requirement	Description	Compliance	Solution & Remarks
SLA Compliance	Follow SWA SLA guidelines	Yes	Fully aligned with SWA's incident response timeframes and escalation matrix.
Breach Reporting	Notify SWA of breaches with impact report	Yes	Defined response plan includes initial report within working hours and formal RCA submission.

4.7.3 System Stability Assurance

Requirement	Description	Compliance	Solution & Remarks
Performance Testing	Simulate high-volume RFP transactions	Yes	Load testing simulates real-life peak conditions for validation.
Redundancy	Failover	Yes	Implemented via container



	mechanisms for workflow and storage		orchestration with replication and autoscaling.
Uptime	Minimum 99.5% uptime commitment	Yes	Ensured through SLA-backed monitoring and cloud service redundancy.
Real-time Error Alerts	Alerts for any disruptions	Yes	Integrated with SWA's monitoring tools for real-time alerts and notifications.
Backup & Recovery	Schedule backups for all data	Yes	Backup strategy includes daily snapshots and weekly full backups.
Technical Monitoring	Dashboard for system resource and health	Yes	Dashboards show CPU, memory, RFP progress, and task queues.
SLA for Issue Resolution	Critical: 1 day; Major: 3 days; Minor: 7 days	Yes	Support model and ticketing tool adhere to these SLA windows.

4.7.4 System Performance and Scalability Requirements

4.7.4.1 Performance Requirements

Requirement	Description	Compliance	Solution & Remarks
Concurrent Users	Support up to 5,000 users	Yes	Infrastructure scales elastically; tested with 5000+ users under concurrent load.
Response Times	≤ 2s normal, ≤ 5s peak	Yes	UI and backend optimized for low latency and fast interaction.
Workflow Efficiency	Optimize background processes	Yes	Background jobs scheduled and monitored to avoid impact on user performance.

4.7.4.2 Scalability Requirements

Requirement	Description	Compliance	Solution & Remarks
Horizontal &	Scale compute as	Yes	Kubernetes enables seamless scaling

Vertical Scaling	needed		without code modifications.
Multi-Environment Deployment	Deploy to Dev/QA/Prod with ease	Yes	Configuration-as-Code approach ensures consistent multi-env deployments.

4.7.4.3 Technical Optimization

Requirement	Description	Compliance	Solution & Remarks
SAP Best Practices	Use efficient ABAP, indexing, etc.	Yes	Development aligned with RAP model standards.
Caching & Encryption	Cache encrypted static/frequent data	Yes	Smart caching implemented with respect to data classification policies.
UI Optimization	Avoid excessive DB round-trips	Yes	Uses frontend data caching and optimized APIs for minimal backend load.

4.7.4.4 Load Testing

Requirement	Description	Compliance	Solution & Remarks
Load Testing	Test under normal and peak loads	Yes	Load test results shared during UAT phase, covering performance and scalability KPIs.

4.7.4.5 Monitoring & Maintenance


Requirement	Description	Compliance	Solution & Remarks
Real-time Monitoring	Use SAP Solution Manager	Yes	Solution Manager shall be used
Alerts & Logs	Detect workflow, transaction delays	Yes	Alerts on workflow bottlenecks, long jobs, and abnormal transaction durations.

4.7.4.6 Infrastructure Compatibility

Requirement	Description	Compliance	Solution & Remarks
-------------	-------------	------------	--------------------

SAP S/4HANA Compatibility	Must work with HANA DB and BTP	Yes	Designed for SAP HANA in-memory DB and BTP
---------------------------	--------------------------------	-----	--

4.8 Solution Architecture

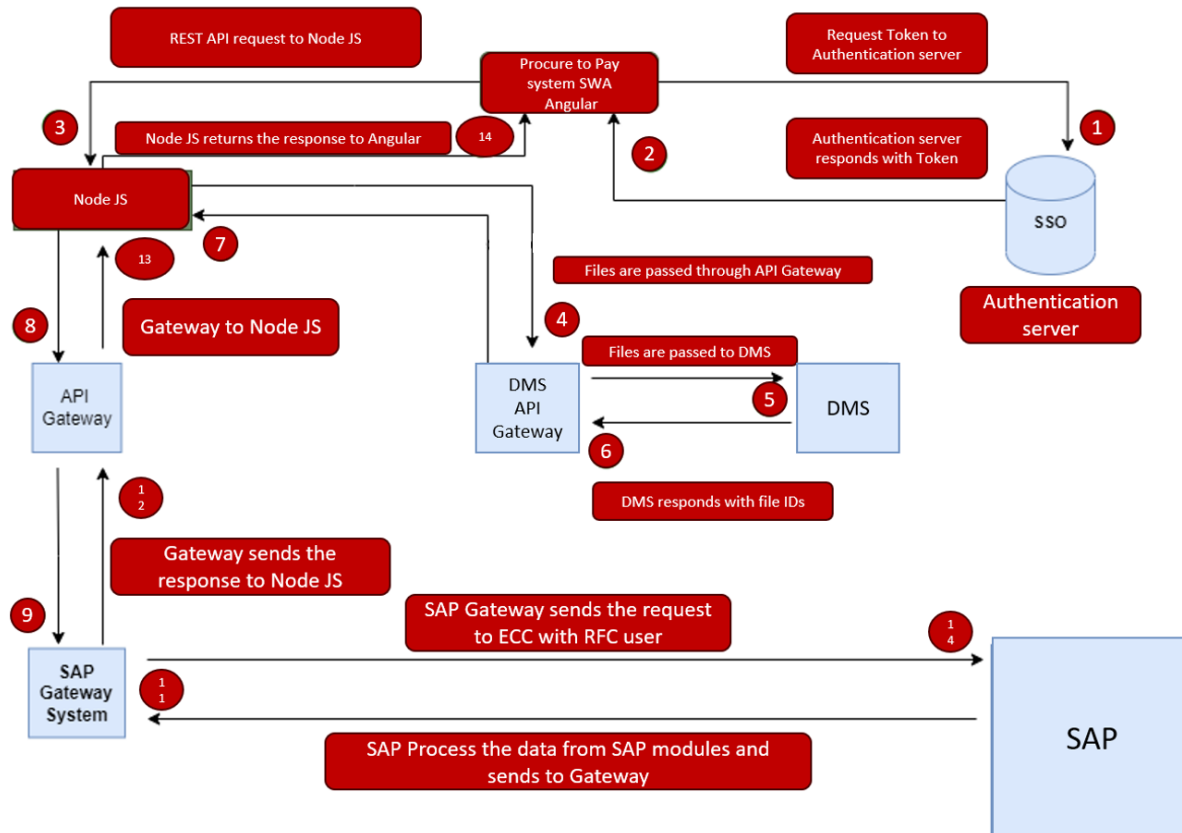

*An Angular-based web application, served via a Node.js runtime, will be deployed on SAP BTP using the Cloud Foundry environment

Overview

The solution architecture for KaarTech Tech's Procure to Pay process is designed to integrate various systems and components seamlessly. This architecture leverages REST APIs, Node JS, Angular, SWA systems, and an authentication server to ensure an efficient and secure procurement workflow.

Technical Components and Their Roles

This architecture leverages various technical components, each playing a critical role in the process. The Angular application serves as the front-end interface for users, while the authentication server manages user authentication. The SSO service provides seamless access across applications, and the Node JS server handles incoming REST API requests. The API Gateway manages and routes requests, the DMS handles file storage, and the proposed gateway system and SAP system shall facilitate data processing and transaction management. This comprehensive and integrated approach ensures robust, secure, and efficient procure to pay process for SWA.

Authentication and Token Request

The process initiates with the Angular application, which sends a request to the authentication server to obtain an authentication token. This step is crucial for securing access to subsequent services, ensuring that only authorized users can proceed. The authentication server validates the credentials provided and responds with an authentication token. Following this, the token is passed to the Single Sign-On (SSO) service, enabling users to access multiple applications without the need to log in repeatedly, thus enhancing user experience and security.

REST API Request to Node JS

Subsequently, the Angular application sends a REST API request to the Node JS server. This request marks the beginning of the procure to pay process. The Node JS server processes this request and forwards it to the API Gateway. The API Gateway plays a pivotal role in this architecture, acting as an intermediary that routes requests to the appropriate service endpoints. It ensures that traffic is managed efficiently and securely, maintaining the integrity and performance of the system.

File Management

The API Gateway then sends files to the SAP system. The system is responsible for the storage and management of these files. The files are passed through the API Gateway, which ensures they are correctly stored and can be retrieved when needed. The SAP system responds with file IDs, which are crucial for tracking and managing the files throughout the process, ensuring that all documents are accounted for and easily accessible.

Communication with SWA Gateway System



In parallel, the SWA Gateway system sends a request to the SWA system using an RFC (Remote Function Call) user. This integration with the SWA system is essential for processing data from various SWA modules relevant to the procurement process. The SWA system then processes the data it receives. This involves executing business logic, updating records, and performing necessary transactions within the SWA modules, ensuring that all procurement activities are accurately recorded and managed.

Final Response to Angular

Finally, the Node JS server returns the processed response to the Angular application. This marks the completion of the procure to pay process. The Angular application can now display the results to the user or take further action based on the processed data, ensuring that the entire procurement workflow is completed efficiently and securely.

4.9 Technical Specifications

Backend Specifications

Requirement	Description	Compliance	Solution & Remarks
Security Best Practices	Consider OWASP Top 10 vulnerabilities	Yes	Application backend is designed to prevent OWASP Top 10 risks, including input validation, access control, and secure session management.
Design Patterns	Use standard design patterns (e.g., Layered, Microservices)	Yes	Layered architecture implemented for separation of concerns; microservices used where needed for modular integration.
SAP-Native Development	Use ABAP, BAIs, User Exits, CDS Views, OData	Yes	All custom logic developed using SAP's recommended S/4HANA extension frameworks, fully aligned with SAP clean core principles.
Business Logic	Compliant with SAP Clean Core	Yes	Customizations are non-intrusive; extensions follow clean core and upgrade-safe guidelines.
SAP Module Integration	Integrate with SAP Finance, HCM, Material Master	Yes	Uses standard APIs and BAPIs to integrate seamlessly with key SAP modules.
SAP Ariba Sync	Sync via REST APIs or	Yes	Uses SAP BTP Integration Suite for secure



	SAP Integration Suite		and scalable data exchange with SAP Ariba.
Authorization Control	Comply with SAP authorization objects	Yes	Role checks and object-level permissions enforced using SAP standard authorization framework.

Frontend Specifications

Requirement	Description	Compliance	Solution & Remarks
UI Framework	Use SAP Fiori, SAPUI5, or Angular	Yes	An Angular-based web application, served via a Node.js runtime, will be deployed on SAP BTP using the Cloud Foundry environment
Responsive Design	Support desktop and tablet	Yes	Frontend built with responsive layouts using standard design guidelines to ensure device flexibility.
Role-Based UI	Navigation and tiles based on user roles	Yes	Customizable Launchpad with dynamic tiles and routing based on SAP roles assigned to users.

Database Specifications

Requirement	Description	Compliance	Solution & Remarks
SAP DB Usage	Use SAP S/4HANA DB or separate DB on SAP Cloud	Yes	By default, transactional data resides in custom/extended S/4HANA tables; fall back to SAP Cloud-hosted DB in specific scenarios.
Historical Data Management	Import, index, and tag legacy RFPs	Yes	Legacy RFPs imported, tagged with metadata, and indexed using CDS Views for fast retrieval.




Document Storage	Use SAP ArchiveLink or SAP DMS	Yes	Can be Integrated with SAP DMS for secure document storage and retrieval with metadata mapping.
Logging and Audit Trail	Log all user and process actions	Yes	All system events, changes, and approvals logged in dedicated audit tables for traceability.
Data Archival Strategy	Align with data retention policies	Yes	Archival procedures adhere to SWA's data lifecycle governance using SAP ILM (Information Lifecycle Management).

4.10 User Interface

Requirement	Description	Compliance	Solution & Remarks
UI Screen Count	A detailed list of the total number of UI screens/modules that will be developed as part of the RFP Lifecycle Add-On.	Yes	Refer Section Development Scope
UI Screen Previews	- Navigation flow -Clear identification of each screen's purpose and functional role within the workflow. - Wireframes or visual mockups (if available) to support the evaluation of user experience and interface consistency. - Classification of the screens based on user roles (e.g., requester, committee member, approver, administrator).	Yes	Snapshots of Sample Screens are provided in the below section.

Below furnished are the snapshots of the User Interface available as part of the standard P2P Solution.




RFP

ADMIN

RFP - REQUESTER

Create

My Request

RFP - APPROVER

BID OPENING COMMITTEE

Project Details

Project Name Arabic*

Department*

Cost Center*

تمسقين

إدارة الحوكمة والمخاطر والالتزام المؤسسي

0001000501-إدارة الحوكمة والمخاطر

Purchase Group*

P06-الأمن السيبراني

Bill of Quantity

SI No.*

Material Group*

Item Name*

2

Quantity*

UOM*

Item Description

Estimated Unit Price (Without VAT)*

Delivery Date*

2024/12/30

SI No.

Material Group

Item Name

Quantity

UOM

Action

1

GEN1-استهلاك الكهرباء

Item 1

1,000

ONE-One

RFP Estimated Price (Without VAT)*

VAT Amount*

RFP Estimated Price (With VAT)*

100,000.00

15,000

115,000.00

Technology RFP*

No

Scope Of Work

Contract Duration*

Duration Type*

2

Week

Technical Member Name*

Abdulahman AlFawaz × Aref O. AlShamari Aref O. AlShamari ×

Technical Member's Manager Name*

Mohammed Alomar

Justification(300 Characters)*

[Handwritten Signature]



ADMIN
RFP - REQUESTER
Create
My Request
RFP - APPROVER
BID OPENING COMMITTEE

Procurement Checklist

Technical Requirements

SI No.*
Description (2)*

2

+

SI No.	Description	Action
1	req 1	

Technical Evaluation Criteria

Technical evaluation passing percentage*
70
Save
Edit

SI No.*	Headline*	Weightage*	Sub Criteria*
2	headline 2	20	Yes

Add Sub Criteria

	SI No.	Headline	Weightage	Action
	1	headline 1 Description	80	

Vendor Evaluation Weightage

Technical Evaluation Weightage*
0
Financial Evaluation Weightage*
0

Man Power

Attachments

© 2024 Copyright. All Rights Reserved
Version - 1.1.0

BID OPENING COMMITTEE

RFP - APPROVER
BID OPENING COMMITTEE
Bid Opening Form
Bids List (70)

Bid Opening Form

RFP Number*
1000000109 - امتحان

Tender Name
امتحان

Reference Number (PR number)
122022360

Type of Purchase
RFP for tendering

Method of Submission*
Select Type Of Tendering

Purchase method*

Etimad Number*
Etimad Number

Etimad Submission Date*
Select Date

Department
إدارة الجودة والمخاطر والالتزام المؤسسي

SUBMIT



RFP - APPROVER

CERTIFICATE OF COMPLETION

BID OPENING COMMITTEE

Go To Bid Opening (5)

Go To Received Offer (5)

Go Live (5)

Bid Opening Committee Form

Tender Name

Technical offer opening date

Financial offer opening date

Reference Number (PR number)

Type of Purchase

Method of Submission

Estimate Number

Estimate Submission Date

Committee head

Department

Date for submitting quotation*

Number of vendors

Number of buyers

Purchase method*

Committee Head Comments

Committee Members

Fixed Members *

Department	Members
Committee Member	☒ Abdulghani Alami
Committee Member	☒ Mustafa Hassan Mustafa Hassan
Committee Member	☒ Abdulaziz Alakim Abdulaziz Alakim
Committee Member	☐ Abdulrahman AlFawaz

RFP - APPROVER

CERTIFICATE OF COMPLETION

BID OPENING COMMITTEE

Go To Bid Opening (5)

Go To Received Offer (5)

Go Live (5)

Add Vendors

Add Vendors

SI No.*

Vendor*

Commercial Number*

Price

Initial Guarantee Value*

Comment History

Add Comments

Certificates *

Attachments *

Content Of Offer *

Committee Comments

Attachments

Note

- Maximum file size is 40 MB

Drag and drop file here

OR



RFP - APPROVER
CERTIFICATE OF COMPLETION
BID OFFERING COMMITTEE
Bids To Be Evaluated (1)
Bids For Financial Offer (1)
Bids For Offer (1)

Certificates

Sl. Number	Certificates	Status	Attachments
1	Financial Offer	Not attached	Attachments
2	Technical Offer	Not attached	Attachments
3	Proof of the establishments affiliation with the local small and medium enterprises category, if applicable	Not attached	Attachments
4	Bank Guarantee	Not attached	Attachments
5	Commercial register or statutory business	Not attached	Attachments
6	Certificate of payment of tax or fee or both	Not attached	Attachments
7	Certificate from the General Organization for Insurance	Not attached	Attachments
8	Certificate of affiliation with the Chamber of Commerce	Not attached	Attachments
9	Certificate of achieving the required percentage for Saudization of jobs	Not attached	Attachments
10	Others	Not attached	Attachments

Attachments
Content Of Offer

© 2024 Copyright, All Rights Reserved
Version - 1.1.0

BID EVALUATION COMMITTEE

RFP - REQUESTER
RFP - APPROVER
CONTRACT
BID EVALUATION COMMITTEE
Bids To Be Evaluated (1)
Bids List (18)
Signature Upload

Vendor Selection
LCU
Small and medium enterprises

Committee Members

Vendors

Sl No.	Vendor	Price	Price Ranking	Technical Result	Technical Weightage	Financial Weightage	Total weightage	Comments	Add Comments	Documents Checklists
1	test	122,222.00	1	Pass	70.00	30.00	100.00			

Committee Recommendations

Attachments

Comment History
Add Comments

Submit to Procurement Member

Calculate Financial Weightage

© 2024 Copyright, All Rights Reserved
Version - 1.1.0

[Handwritten Signature]



ADMIN ▼

RFP - APPROVER ▼

DIRECT PURCHASE EVALUATION ▲

Bids To Be Opened (1)

Bids To Be Evaluated(0)

✔ **Bids To Be Approved (1)**

Bids List (56)

Final Approval (1)

From Qualification (0)

Signature Upload

Committee Members ▼

Vendors ▲

Sl No.	Vendor	Price	Technical Result (Pass / Fail)	Applicable / Not Applicable	Price Ranking	Technical Weightage	Financial Weightage	Total weightage	VendorSelected	Comments	Add Comments	Documents Checklists
1	test vendor	23,000.00	Pass	Not Applicable	2	79.00	20.20	99.20	Selected			
2	test vendor 2	22,121.00	Pass	Applicable	1	70.00	21.00	91.00	Not			

Attachments ▼

Download MOM ▼

Bill Of Quantity

Comment History

Add Comments

© 2024 Copyright, All Rights Reserved
Version - 1.1.0

Cancel Tender

ADMIN
RFP - APPROVER
DIRECT PURCHASE EVALUATION
Bids To Be Opened (1)
Bids To Be Evaluated(0)
Bids To Be Approved (1)
Bids List (56)
Final Approval (1)
From Qualification (0)
Signature Upload

RFP Number	Tender Name	Tender Number	Etamad Number	Status	Opening Date	Method of Submission	Purchase method	Type of purchase	Pending with	Download MoM	SLA
1000000111	امتحان	5000000069	1625431423	Submitted	26/12/2024	One Envelope	Limited	RFP For Tendering		Download	
1000000063	امتحان	5000000068	1232122332	Submitted	26/12/2024	One Envelope		Direct Purchase	Turki Alateeq		
1000000088	امتحان	5000000067	9876543210	Submitted	26/12/2024	Two Envelope	Limited	RFP For Tendering	Abdulghani Alami	Download	
1000000076	امتحان	5000000061	1234567890	Submitted	18/12/2024	One Envelope	Limited	RFP For Tendering	Saleh Alqantani	Download	
1000000064	امتحان	5000000060	7654543329	Submitted	18/12/2024	One Envelope		Direct Purchase	Waheed Suliman		

1 2 3 4 5 ... 12 > 5 / page

© 2024 Copyright, All Rights Reserved
Version - 1.1.0

TECHNICAL EVALUATION COMMITTEE

RFP - REQUESTER
TECHNICAL EVALUATION COMMITTEE
Bids To Be Evaluated (1)
Bids List (15)
Signature Upload

Vendors

Sl No.	Vendor	Action	Comments	Add Comments	Documents Checklists
1	vendor 1	Action			

Technical Requirement

Sl No	Description	Applicable / Not Applicable *
001	tech req 1	Select Applicable Not Applicable
Justification *		
Sl No	Description	Applicable / Not Applicable *
002	tech req 2	Select
Justification *		

© 2024 Copyright, All Rights Reserved
Version - 1.1.0

[Handwritten Signature]



RFP - REQUESTER

TECHNICAL EVALUATION COMMITTEE

Bids To Be Evaluated (1)

Bids List (15)

Signature Upload

Technical Evaluation
vendor 1
Technical evaluation passing percentage
66.00 %

SI No	Headline	Weightage	Actual *	Page No *
001	Headline 1	50	0	
Comment * 				
Sub Criteria				
002	Headline 2	10	0	
Comment * 				
003	Headline 3	40	0	

© 2024 Copyright, All Rights Reserved
Version - 1.1.0

ADMIN

RFP - APPROVER

TECHNICAL EVALUATION COMMITTEE

Bids To Be Evaluated (2)

Bids From Technical Members (1)

Bids List (14)

Signature Upload

Technical Evaluation Result

Vendor
A

Technical Member
Mohammed Alghamdi

SI No.	Technical evaluation passing percentage	Total
1	66 %	79 %

Technical Requirements

Technical Requirement
tech req 2

Applicable / Not Applicable
Applicable

Justification
122

Technical Requirement
Technical Evaluation Criteria

Comments
122

Attachments

Return

Calculate Weightage

Comment History

Add Comments

© 2024 Copyright, All Rights Reserved
Version - 1.1.0

BID QUALIFICATION COMMITTEE



QUALIFICATION COMMITTEE
Bids To Be Evaluated (0)
Bids List (19)

Bid Qualification Committee Form

Tender Details

Tender Name

التميز

Opening Date

12/12/2024

Reference Number (PR number)

122022343

Type of Purchase

RFP For Tendering

Method of Submission

One Envelope

Etamad Number

1234567890

Date for submitting quotation

12/12/2024

Purchase method

Public

Committee head

Mosleh Alshamrani

Number of Qualification Invitation

fsdf

Invitation Publish Date

03/12/2024

Qualification Document Receiving Date

Select date

Qualification Document Inspection Date

Select date

Number of vendors involved in Qualification

0000

Passing rate

Committee Members

© 2024 Copyright, All Rights Reserved
Version - 1.1.0

QUALIFICATION COMMITTEE
Bids To Be Evaluated (0)
Bids List (19)

Technical Evaluation

Evaluation standard	Technical Capabilities (Technical Member)	Weightage (%)	Score
Previous experience		100 50	50
Number of years of experience		100 30	30
Number of projects implemented during the last three years		20	20
Total value of projects during the last three years		50	50
Existing contractual obligations		100 20	18
Number of existing projects		100 10	10
The value of existing projects		90	80
HR		100 30	21
Number of Employees		100 ..	50

© 2024 Copyright, All Rights Reserved
<https://procurementtest.mwan.sa:3000>



QUALIFICATION COMMITTEE

Bids To Be Evaluated (0)

Bids List (15)

Number of Employees

100

80

50

Percentage of Saudi employees

20

20

Total

89

Technical Capabilities (60 %)

53.4

Financial Evaluation

Weightage (%)

Points

Total

60

Financial Capabilities (40 %)

24

Vendor Passed

Vendor Passed *

Yes No

© 2024 Copyright. All Rights Reserved

CONTRACT PREPERATION PROCESS

ADMIN

RFP - APPROVER

CERTIFICATE OF COMPLETION

CONTRACT

List Of Contract To Be Created

Return From Rm

Return From Approval

Contract List

BID EVALUATION COMMITTEE

Contract Details

Project Details

Project Name

Type of Project

Award Number

Award Date

Vendor Name

Contract Start Date *

Date(Calendar)

Project Duration:

Duration Type

PR Number

Award Letter(Printable) *

Award Date(Printable) *

Select Registration Type *

Number

Brief Description of the process: *

description of the prcs

Total Amount

Total Amount In Words

© 2024 Copyright. All Rights Reserved
Version - 1.1.0

[Handwritten Signature]



ADMIN

RFP - APPROVER

CERTIFICATE OF COMPLETION

CONTRACT

List Of Contract To Be Created

Return From RFP

Return From Approval

Contract List

BID EVALUATION COMMITTEE

Bank Guarantee

Bank Guarantee Number *

Final guarantee percentage *

Amount *

1

12

Enter Guarantee amount

Currency *

Issued By: *

Select Date Type *

SAR

Bank 1

Hijri Date

Date Of Issue *

Valid Till *

1446-06-23

1446-06-30

Delegate's Details

Authorization

Signing Authorization: *

Authorized to sign

Select Signing Authorization

Authorized to sign

Delegated to sign

ADMIN

RFP - APPROVER

CERTIFICATE OF COMPLETION

CONTRACT

List Of Contract To Be Created

Return From RFP

Return From Approval

Contract List

BID EVALUATION COMMITTEE

Contractor Details

Downpayment

☒ Downpayment

Maximum Advance Percentage Allowed *

Rate of Downpayment (In %) *

Downpayment Amount *

10

1

Enter downpayment amount

Copy of Contract

Insurance

Penalties

Penalty Percentage (%) *

Enter penalty percentage

Fines for violating the provisions of the local content preference regulation

Enter penalties

ADMIN

RFP - APPROVER

CERTIFICATE OF COMPLETION

CONTRACT

List Of Contract To Be Created

Return From RFP

Return From Approval

Contract List

BID EVALUATION COMMITTEE

Scope of Work

Payment Schedule

Specifications

☒ Specification

☒ Team Specification

☒ Quality Specification

Static

Static

Local Content Requirement

☒ Local Content Requirement

☒ Mandatory Terms

☒ National Products Share

Static

Static



CERTIFICATION OF COMPLETION

CERTIFICATE OF COMPLETION

Create

Coc Action

Certificate Of Completion List

CONTRACT

BID EVALUATION COMMITTEE

Create COC

Back

Department Name : المركز الوطني لإدارة النفايات

Project Name :

Contract Number :

SI No	Vendor Name	Contract Item Number	PO Number	PO ItemNo	SES Number	SES Amount	SES Remaining Amount	PO Amount	PO Remaining Amount	COC Amount
1	شركة الزامل العالمية لخدمات المعلوم	00000	4000000067	00010	1000000498	2,568,617.94	2,568,617.94	--	--	23,000

1 5 / page

Continue

CERTIFICATE OF COMPLETION

Create

Coc Action

Certificate Of Completion List

CONTRACT

BID EVALUATION COMMITTEE

Create COC

Project Name

COC Number

Vendor Name

Phase Name*

Invoice Number*

Invoice Issue Date*

Invoice Amount(VAT included)

Retention(%)

Advance Payment Deduction

Penalties(Amount)

COC Amount

SI No	PO Number	PO ItemNo	PO Issue Date	PO Amount	SES Number	SES Amount	COC Amount	SES Document
1	4000000067	00010	2023-10-16	0.00	1000000498	2,568,617.94	23,000	SES Document

CERTIFICATE OF COMPLETION

Create

Coc Action

Certificate Of Completion List

CONTRACT

BID EVALUATION COMMITTEE

Certificate Of Completion List

SI No	COC Number	Department Name	Project Name	Vendor Name	Contract Number	PO Number	Invoice Number	CreatedBy	CreatedOn	Status	Pending with	SLA	Action
1	3000000010		تقديم خدمات استشارية للرقابة الداخلية للمركز	مؤسسة وقت ال	4600000063	4000000000	1234567890	Majed M. AIO	2024-12-18	PENDING WITH PROJECT MANAGER	Mohammed Alomar	11 Days 20 Hours	
2	3000000009		تقديم خدمات استشارية للرقابة الداخلية للمركز	مؤسسة وقت ال	4600000063	4000000000	1020304050	Majed M. AIO	2024-12-05	PENDING WITH DIRECTOR	Nasser Ahmed Nasser Mshai	19 Days 22 Hours	
3	3000000008		تقديم خدمات استشارية للرقابة الداخلية للمركز	مؤسسة وقت ال	4600000063	4000000000	1112221212	Majed M. AIO	2024-12-04	PENDING WITH FINANCE OFFICER	Majed M. AIOtaibi Majed M. AIOtaibi	21 Days 23 Hours	
			تقديم										



4.11 Conclusion

KaarTech's P2P solution ensures a structured and transparent procurement process, from the creation of the RFP to the final payment and certification of completion. By leveraging P2P Solution & Etimad Systems, KaarTech Tech provides a robust framework for efficient procurement management.



5. Project Scope of Work

In line with RFP requirements, KaarTech understands that SWA requirements are as below.

- KaarTech's solution presented below outlines the "Project to Create an Electronic Platform for Managing the Competition Lifecycle in Integration with Corporate Systems and Artificial Intelligence Technologies" initiative tailored for SWA. This initiative is focused on establishing the automation of Procure to Pay process at SWA.
- With this understanding we have provided the detailed scope of work that is considered for this engagement.

5.1 Language

- The solution will display available information in English and Arabic only if such is provided as part of the standard software.
- Furthermore, the default version of Arabic used in such standard software is fixed and cannot be edited.
- All required system configuration will be done in the English version of the application only.
- The Project language will be in English. All Project communications, workshops and project deliverables will be delivered in English.

5.2 Geography

The work related to this engagement will be performed as per the following:

Onsite Project Location	Offshore Project Location
SWA Office in Riyadh, KSA.	KaarTech Offshore Delivery Centre, India

5.3 Service Window

- KaarTech will follow the below Calendar days and business hours of SWA:
- Working Days: KSA – Sunday to Thursday (5 days)
- Working Hours: 8.00 AM to 4.00 PM KSA time (8 hours/working day)

5.4 Currency

- Local currency or book currency will be Saudi Riyal (SAR).



- Business transactions can be executed in any currency as per the standards.

5.5 Legal Entity

KaarTech is considering engaging with only One (1) Entity of SWA in KSA for the SWA's "Establishing an auxiliary electronic system to organize and facilitate purchases" initiative.

5.6 Development Scope

Below are the developments considered as part of project scope,

Row Labels	Low	Medium	High	Total
User Interface (Screens)		22	9	31
Workflows		4	4	8
Reports	3	5	2	10
Interfaces	2	6		8
Enhancements		1		1
Forms	3	7	10	20
Custom Tables	108	9		117
OData Services	131	23		154
Bot			1	1
AI Solutions		3	2	5
Total	247	80	28	355

Below are few pre-identified lists of Screens, Workflows, Reports, Interfaces, Enhancements, Forms, Class, Custom Tables & OData Services. The rest of the development items shall be identified based on business requirement during the Explore Phase of the project.

5.6.1 User Interfaces (Screens)

Development Type	Process	Description	Complexity
------------------	---------	-------------	------------

User Interface (Screens)	RFP	RFP Create	High
User Interface (Screens)	RFP	RFP Change/Edit	High
User Interface (Screens)	RFP	RFP Inbox	Medium
User Interface (Screens)	RFP	RFP - My Request	Medium
User Interface (Screens)	RFP	RFP Dashboard	Medium
User Interface (Screens)	RFP	Budget Allocation Creation	Medium
User Interface (Screens)	RFP	Budget Allocation - My Request	Medium
User Interface (Screens)	Committee	Bid Opening Committee Form	High
User Interface (Screens)	Committee	Bid Evaluation Committee Form	High
User Interface (Screens)	Committee	Technical Evaluation Committee Form	High
User Interface (Screens)	Committee	Bid Qualification Committee Form	High
User Interface (Screens)	Committee	Inbox - Tender list	Medium
User Interface (Screens)	Committee	Committee Dashboard	Medium
User Interface (Screens)	Committee	Signature Upload	Medium




User Interface (Screens)	Contract Generation	My inbox – contract	Medium
User Interface (Screens)	Contract Generation	Contract Preparation Form	High
User Interface (Screens)	Contract Generation	Initial Contract assignment screen	Medium
User Interface (Screens)	Contract Generation	Signature upload	Medium
User Interface (Screens)	Contract Generation	Contract Dashboard	Medium
User Interface (Screens)	Contract Management	Contract Change Request Form	Medium
User Interface (Screens)	COC	COC Preparation and approval Form	Medium
User Interface (Screens)	COC	COC Dashboard	Medium
User Interface (Screens)	COC	COC Creation - PO/contract selection screen	Medium
User Interface (Screens)	General	RFP Maintenance	Medium
User Interface (Screens)	General	SLA Maintenance	Medium
User Interface (Screens)	General	Committee Maintenance	Medium

5.6.2 Workflows

Development Type	Process	Description	Complexity
Workflows	Committee	1 Envelope Normal Scenario Workflow	High




Workflows	Committee	2 Envelope Normal Scenario Workflow	High
Workflows	Committee	Direct Purchase - 1 envelope Scenario workflow	High
Workflows	Committee	Direct Purchase - 2 envelope Scenario workflow	High
Workflows	Contract	Contract form Preparation and form approval workflow	Medium
Workflows	COC	COC form preparation and form approval workflow	Medium

5.6.3 Reports

Development Type	Process	Description	Complexity
Reports	RFP	RFP SLA Breach Report	Medium
Reports	Committee	Committee SLA Breach Report	Medium
Reports	Contract	Contract SLA Breach Report	Medium
Reports	COC	COC SLA Breach Report	Medium

5.6.4 Interfaces

Development Type	Process	Description	Complexity
Interfaces	RFP	Estimated Price Interface	Low
Interfaces	Committee	BOC Interface	Medium
Interfaces	Committee	BEC Interface	Medium
Interfaces	Committee	Technical Evaluation Interface	Medium
Interfaces	Committee	BQC Interface	Medium
Interfaces	Contract	Contract Interface	Medium




Interfaces	COC	Certificate of Completion Interface	Medium
Interfaces	COC	SES Interface	Low

5.6.5 Enhancements

Development Type	Process	Description	Complexity
Enhancements	Contract	Enhancement in include program ZXM06U43 (User Exit to save Purchase Document) to integrate the SAP Contract to P2P Contract Preparation process	Medium

5.6.6 Forms

Development Type	Process	Description	Complexity
Forms	RFP	Estimated Price Form	Low
Forms	Committee	BOC 1 Envelope MOM	Medium
Forms	Committee	BOC 2 Envelope MOM - Public	Medium
Forms	Committee	BOC 2 Envelope MOM - Limited	Medium
Forms	Committee	BEC MOM	Medium
Forms	Committee	Technical Evaluation Report	Medium
Forms	Committee	BQC MOM	Medium
Forms	Contract	General Supply	High




Forms	Contract	Public Services	High
Forms	Contract	Information Technology	High
Forms	Contract	Consulting Services	High
Forms	Contract	Operating and Maintenance	High
Forms	Contract	Engineering Services - Supervision	High
Forms	Contract	Engineering Services - Design	High
Forms	Contract	Framework Supply Agreement Template	High
Forms	Contract	Framework Consulting Services Agreement Form	High
Forms	Contract	Framework Service Agreement Form - General	High
Forms	COC	Certificate of Completion Form	Medium
Forms	COC	SES Form	Low

5.6.7 Custom Tables

Development Type	Process	Description	Complexity
Custom Tables	RFP	Commitment Item and Document Type Mapping Config.	Low
Custom Tables	RFP	RFP BA Attachments	Low
Custom Tables	RFP	Workflow Rule Table 1 (Process Flow)	Low
Custom Tables	RFP	Workflow Rule Table 1 (Process Flow)	Low
Custom Tables	RFP	RFP Attachments	Low
Custom Tables	RFP	RFP Budget Allocation	Low
Custom Tables	RFP	RFP Budget Controller	Low
Custom Tables	RFP	RFP Bill of Quantity	Low




Custom Tables	RFP	RFP Checklist ID Master	Low
Custom Tables	RFP	RFP Checklist Configuration	Low
Custom Tables	RFP	RFP Checklist Value Option Dts	Low
Custom Tables	RFP	RFP Approver Comments	Low
Custom Tables	RFP	RFP Comment	Low
Custom Tables	RFP	RFP Constants	Low
Custom Tables	RFP	RFP possible values for finance evaluation	Low
Custom Tables	RFP	RFP Finance Evaluations	Low
Custom Tables	RFP	RFP IT Checklist	Low
Custom Tables	RFP	RFP possible values for material groups	Low
Custom Tables	RFP	RFP Manpower	Low
Custom Tables	RFP	RFP Payment Terms	Low
Custom Tables	RFP	PUD/FIN approver details for IT / Non	Low
Custom Tables	RFP	RFP Procurement Checklist	Low
Custom Tables	RFP	RFP Purchase group mapping	Low
Custom Tables	RFP	RFP Qualification Details	Low
Custom Tables	RFP	RFP Request Headers	Low
Custom Tables	RFP	RFP Role Access	Low
Custom Tables	RFP	User signature	Low
Custom Tables	RFP	RFP SLA	Low
Custom Tables	RFP	RFP Technical Evaluations	Low
Custom Tables	RFP	RFP technical members	Low
Custom Tables	RFP	RFP Technical Requirements	Low




Custom Tables	RFP	RFP User list	Low
Custom Tables	RFP	RFP Workflow Header	Low
Custom Tables	RFP	Workflow Log	Low
Custom Tables	RFP	RFP Consultancy of Work	Low
Custom Tables	RFP	Project and Budget Maintenance	Medium
Custom Tables	Contract	Contract Attachments	Low
Custom Tables	Contract	Contract Manpower	Low
Custom Tables	Contract	Z Table for P2P contract processes	Medium
Custom Tables	Contract	P2P Contract Role with SAP Role Master Table	Low
Custom Tables	Contract	Contract SLA Configuration Maintenance	Low
Custom Tables	Contract	Contract Comments Table	Low
Custom Tables	Contract	Z Table for Con Contract	Low
Custom Tables	Contract	MM: Contract Department	Low
Custom Tables	Contract	Z Table for P2P Contract - Evaluation Period	Low
Custom Tables	Contract	Contract form View	Low
Custom Tables	Contract	Contract Process log Table	Low
Custom Tables	Contract	P2P Contract Log Header	Low
Custom Tables	Contract	CON Payment Schedule	Low
Custom Tables	Contract	Contract Workflow Rule Configuration	Medium
Custom Tables	Contract	P2P Contract User Signature	Low
Custom Tables	Contract	MM: Contract Process Department	Low
Custom Tables	Committee	Committee vendors Check List Attachments	Low




Custom Tables	Committee	Committee Bid Members Assigned	Low
Custom Tables	Committee	Committee SLA Calendar and Working time Config.	Low
Custom Tables	Committee	Committee vendors Check List	Low
Custom Tables	Committee	Committee Comments	Low
Custom Tables	Committee	Competition Type	Low
Custom Tables	Committee	Committee Constants	Low
Custom Tables	Committee	Committee and Department Identifier Config.	Low
Custom Tables	Committee	Eval.Committee Legal Evaluation Criteria Dts.	Low
Custom Tables	Committee	Eval.Committee Technical Evaluation Criteria Dts	Medium
Custom Tables	Committee	Eval.Committee Technical Requirements Criteria Dts	Medium
Custom Tables	Committee	Qual.Committee Financial. Statements Criteria Values	Low
Custom Tables	Committee	Legal/Technical Team Committee Comments	Low
Custom Tables	Committee	Committee Log Header	Low
Custom Tables	Committee	Committee Limited Vendor Details	Low




Custom Tables	Committee	Committee Members	Low
Custom Tables	Committee	Committee MOM Details	Low
Custom Tables	Committee	P2P CMT Mom viability	Low
Custom Tables	Committee	Qual.Committee Financial. Evaluation Criteria Dts	Low
Custom Tables	Committee	Qual.Committee Financial. Statements	Low
Custom Tables	Committee	Qual.Committee Qualification Level Master Values	Low
Custom Tables	Committee	Qual.Committee Tech. Evaluation Criteria Dts	Medium
Custom Tables	Committee	Committee Role Definer	Low
Custom Tables	Committee	Committee Tender Request	Medium
Custom Tables	Committee	Committee WF Rule Configuration	Medium
Custom Tables	Committee	Committee WF Rule Header	Medium
Custom Tables	Committee	Committee User Digital Signature	Low
Custom Tables	Committee	Committee SLA Configuration Maintenance	Low
Custom Tables	Committee	Committee Substitute User Maintenance	Low




Custom Tables	Committee	Committee vendors	Low
Custom Tables	Committee	Committee vendors and tech members	Low
Custom Tables	Committee	Committee Workflow Header	Low
Custom Tables	Committee	Committee Workflow Item	Low
Custom Tables	Committee	Committee WF Final Approval Rule Table	Low
Custom Tables	Committee	Committee MOM Approver Dts	Low
Custom Tables	Committee	Committee MOM User Signature Configuration	Low
Custom Tables	Committee	Committee MOM User Menu Configurations	Low
Custom Tables	COC	COC Attachments MANDT MANDT	Low
Custom Tables	COC	P2P COC: Workflow Table	Low
Custom Tables	COC	COC Comments	Low
Custom Tables	COC	COC Department Table	Low
Custom Tables	COC	Coc item details	Low
Custom Tables	COC	Log Table for COC	Low
Custom Tables	COC	P2P COC Log Header	Low
Custom Tables	COC	COC Payment Schedule	Low
Custom Tables	COC	Request Table MANDT MANDT	Low
Custom Tables	COC	P2P COC Role with SAP Role Master Table	Low




Custom Tables	COC	Coc Role Definer	Low
Custom Tables	COC	CoC Workflow Rule Configuration	Low
Custom Tables	COC	COC SLA Configuration Maintenance	Low
Custom Tables	COC	COC Workflow Approval Signature	Low
Custom Tables	COC	P2P COC Workflow Log Table	Low
Custom Tables	COC	Service Entry Sheet Response	Low
Custom Tables	COC	Service Entry Sheet Approver list	Low
Custom Tables	General	Admin Access Information	Low
Custom Tables	General	P2P Attachments	Low
Custom Tables	General	P2P Application Domain Whitelist	Low
Custom Tables	General	P2P File Table	Low

5.6.8 OData Services

Development Type	Process	Description	Complexity
OData Services	RFP	Cost Center Lookup Data	Low
OData Services	RFP	Department Lookup data	Low
OData Services	RFP	Department Manager Lookup Data	Low
OData Services	RFP	Estimating available budget amount using Project	Low
OData Services	RFP	Financial Evaluation Lookup data	Low
OData Services	RFP	Material Group Lookup data	Low
OData Services	RFP	Project Lookup data	Low
OData Services	RFP	Purchase group lookup data	Low
OData Services	RFP	Qualification Criteria lookup data	Low




OData Services	RFP	Unit of Measurement lookup data	Low
OData Services	RFP	Employee User list lookup data	Low
OData Services	RFP	RFP File Attachment	Medium
OData Services	RFP	RFP Budget Allocation Attachment	Medium
OData Services	RFP	RFP Budget Allocation Header entity	Medium
OData Services	RFP	RFP Bill of Quantity	Medium
OData Services	RFP	RFP comments	Low
OData Services	RFP	RFP Estimated Price	Medium
OData Services	RFP	Qualification Financial Criteria	Low
OData Services	RFP	RFP Header entity	Medium
OData Services	RFP	RFP IT checklist	Low
OData Services	RFP	Manpower	Low
OData Services	RFP	Internal Order - Finance	Low
OData Services	RFP	RFP Payment schedule	Low
OData Services	RFP	RFP Procurement checklist	Low
OData Services	RFP	RFP Procurement edit	Low
OData Services	RFP	Qualification Criteria	Low
OData Services	RFP	Technical Criteria	Medium
OData Services	RFP	Technical sub criteria	Medium
OData Services	RFP	Technical members	Medium
OData Services	RFP	Technical Requirement	Medium
OData Services	RFP	Commitment Item	Low
OData Services	RFP	RFP workflow users list	Low
OData Services	RFP	RFP User signature	Medium




OData Services	RFP	RFP Budget Type Lookup data	Low
OData Services	RFP	RFP checklist lookup data	Low
OData Services	RFP	RFP Commitment item lookup data	Low
OData Services	RFP	RFP Commitment Item and material group mapping lookup data	Low
OData Services	RFP	Internal Order lookup data	Low
OData Services	RFP	RFP manpower qualification lookup data	Low
OData Services	RFP	RFP IT checklist	Low
OData Services	RFP	RFP Procurement Checklist	Low
OData Services	RFP	RFP checklist	Low
OData Services	Committee	Get Technical members	Medium
OData Services	Committee	Get Technical and Financial weightage	Low
OData Services	Committee	Committee MOM download	Medium
OData Services	Committee	Committee GUID generator	Low
OData Services	Committee	Committee Users	Low
OData Services	Committee	Committee signature	Low
OData Services	Committee	Tender details in committee	Medium
OData Services	Committee	Committee buttons	Low




OData Services	Committee	Committee constants	Low
OData Services	Committee	Committee certificate checklist	Low
OData Services	Committee	Committee competition Type	Low
OData Services	Committee	Committee Type	Low
OData Services	Committee	Committee Financial Statement Criteria	Low
OData Services	Committee	Committee user list	Low
OData Services	Committee	Qualification committee Financial List	Low
OData Services	Committee	RFP Purchase Type in Committee	Low
OData Services	Committee	Get RFP details from Committee	Low
OData Services	Committee	Committee tender type lookup data	Low
OData Services	Committee	Selected committee User list from RFP	Low
OData Services	Committee	Limited vendor list	Low
OData Services	Committee	MOM visibility	Low
OData Services	Committee	Qualification Financial Evaluation Criteria	Low




OData Services	Committee	Qualification Finance Statement	Low
OData Services	Committee	Qualification Technical Evaluation Criteria	Low
OData Services	Committee	Committee Certificate Attachments	Low
OData Services	Committee	Committee certificate checklist	Low
OData Services	Committee	Committee Vendors	Low
OData Services	Committee	Committee Vendor Technical requirement	Low
OData Services	Committee	Committee Request header	Medium
OData Services	Committee	Get RFP BOQ list	Low
OData Services	Committee	Get RFP Qualification Financial Evaluation and it's weightage	Low
OData Services	Committee	Get committee substitute user list	Medium
OData Services	Committee	Committee Technical Requirement evaluation type	Low
OData Services	Committee	Committee Technica Requirement Status type	Low
OData Services	Committee	Committee User role details	Low
OData Services	Committee	Committee User role CSS Parameter	Low




OData Services	Committee	Committee User role CSS Type	Low
OData Services	Committee	Committee User list	Low
OData Services	Committee	Committee Users and their roles	Low
OData Services	Committee	Committee Final Approval list	Low
OData Services	Committee	Committee Legal Evaluations	Low
OData Services	Committee	Committee Local Content	Low
OData Services	Committee	Committee Comments	Low
OData Services	Committee	Committee Request Members	Low
OData Services	Committee	RFP Qualification criteria list	Low
OData Services	Committee	RFP Technical Requirements list	Low
OData Services	Committee	RFP Technical Criteria list	Low
OData Services	Committee	RFP Technical Evaluation Item	Medium
OData Services	Committee	RFP Technical Evaluation Header	Medium
OData Services	Committee	RFP Technical Evaluation Sub-criteria	Medium
OData Services	Contract	Contract Project lookup data	Low




OData Services	Contract	Contract role lookup data	Low
OData Services	Contract	Contract Status lookup data	Low
OData Services	Contract	Contract section - static/dynamic indicator	Low
OData Services	Contract	Contract Evaluation Period Item	Low
OData Services	Contract	Contract Evaluation Period Head	Low
OData Services	Contract	Contract Manpower item	Low
OData Services	Contract	Contract Manpower header	Low
OData Services	Contract	Contract Attachment	Low
OData Services	Contract	Contract comments	Low
OData Services	Contract	Contract Form Preparation - section visibility	Low
OData Services	Contract	Contract Header Entity	Low
OData Services	Contract	Contract Header Entity - Status level	Low
OData Services	Contract	Contract Payment schedule item	Low
OData Services	Contract	Contract Payment schedule header	Low
OData Services	Contract	Contract - Copy to departments item	Low
OData Services	Contract	Contract - Copy to department header	Low
OData Services	Contract	Contract section - text object CRUD	Low
OData Services	Contract	Master department	Low
OData Services	Contract	List of country lookup data	Low
OData Services	Contract	Department lookup data	Low
OData Services	Contract	Usernames lookup data	Low
OData Services	Contract	Contract Log in authorisation check	Low




OData Services	Contract	Contract Sign and signature	Low
OData Services	COC	COC Attachments	Low
OData Services	COC	COC Comments	Low
OData Services	COC	COC workflow completion	Medium
OData Services	COC	COC Create	Medium
OData Services	COC	COC Dashboard	Low
OData Services	COC	COC Dashboard - Item	Low
OData Services	COC	COC departments	Low
OData Services	COC	COC Form - Header	Medium
OData Services	COC	COC Form - Item	Medium
OData Services	COC	COC Login	Low
OData Services	COC	Open Contract Items	Low
OData Services	COC	Open PO with and without Contract	Low
OData Services	COC	Open PO Header	Low
OData Services	COC	Open PO Items	Low
OData Services	COC	COC PDF	Low
OData Services	COC	COC Process History	Low
OData Services	COC	Project Coordinator	Low
OData Services	COC	Purchase Order Project Owner	Low
OData Services	COC	COC Project Owner	Low
OData Services	COC	SES PDF	Low
OData Services	General	Committee SLA Maintenance	Low
OData Services	General	Contract SLA Maintenance	Low
OData Services	General	RFP SLA Maintenance	Low




OData Services	General	RFP list	Low
OData Services	General	RFP User list lookup	Low
OData Services	General	Admin User Role Parameter	Low
OData Services	General	Admin User Role Type	Low
OData Services	General	COC Role lookup data	Low
OData Services	General	COC SLA Maintenance	Low
OData Services	General	COC User Action Lookup data	Low
OData Services	General	SLA unit lookup data	Low
OData Services	General	P2P Common File Attachment	Low

5.6.9 AI Use cases complexity

Development Type	AI Use case ID	Process	Use Case	Complexity
Artificial Intelligence	UC-01	RFP	UC-01-Review tender specifications and content	Medium
Artificial Intelligence	UC-02	RFP	UC-02-Validate completeness and correctness of tender documents	Medium
Artificial Intelligence	UC-03	Committee	UC-03-Analyse technical proposals for compliance	High
Artificial Intelligence	UC-04	Committee	UC-04-Draft bid evaluation reports	Medium
Artificial Intelligence	UC-05	Committee	UC-05-Support vendor prequalification with historical data analysis	High




5.7 Training Scope

- As part of the project, KaarTech shall provide a virtual training sessions (up to 16 Hours planned as 8 sessions in 1 week) along with KaarTech specific training documentations and user manuals.
- Training will be provided based on 'Train the Trainer' model for BPOs & key users identified in Stakeholder Authority Matrix signed by both the parties and detailed plan shall be finalized during execution of the project. This model has been suggested to ensure that SWA's draws maximum benefit from within a minimum duration. The training will cover all the detailed functionalities of the respective modules finalized during the Analyse phase.
- Classroom Training for the End Users will be carried out by SWA.
- End user training manual will be the deliverable provided by KaarTech under the training scope.
- End-user documentation (Limited to End-User Manuals, UAT Scripts), will be in English.

5.7.1 Training Assumptions

- Training will be provided to all the nominated BPOs / key users in the Stakeholder Matrix.
- BPOs/key users are subject matter experts in their respective departments.
- BPOs & Key users identified by SWA should have a thorough understanding of the business processes of their respective departments.
- Only the Stakeholders who were actively involved as "Responsible" as well as "Accountable" in finalization of Requirement gatherings during Explore phase are eligible to be the training participants (Champions) for key user training.
- IT team must attend the training
- Training Coordinator will be assigned by SWA.
- Infrastructure facilities required for training must be provided by SWA.
- Mobilization of the key users and core team will be the responsibility of SWA.
- The user engagement calendar will be published during the Planning phase of the project. SWA shall adhere as per the given target date in the calendar published by KaarTech well in advance.



- If there are any additional days required for training, will be considered as change request.

5.7.2 Training Exclusion

- Any training other than the listed scope of work



5.8 Testing Scope

The objectives of testing are:

- Ensuring that the system meets all the business requirements defined in the service scope.
- Ensuring that the system meets technical requirements and service levels for application.
- Response time, throughput, and infrastructure performance at typical production loads
- The purpose of the test plan is to provide a central document that outlines what needs to be tested to complete the business process flow agreed upon as per the Test script.
- KaarTech has showcased a tentative testing methodology, which shall be mutually discussed and agreed based on the mutual discussions between KaarTech and SWA, planned during the preparation phase of the project.

5.8.1 Test Cycles

The table below shows the test cycles for business process in the scope of the project:

Test Type	Description	Environment
Unit Testing	Validates those individual functions are configured and/or developed to appropriately translate technical and functional requirements. This would include testing of individual configuration elements, process steps associated with business transactions, and custom development objects. Unit testing includes: • Positive testing – confirms that the test functions correctly by entering a value that is known to be correct and verifying that the returned data/view is as expected. • Negative testing – confirms that the test fails by entering a value that is known to be incorrect and verifying that the component or test case fails. This enables you to understand and identify failures and verify that the target application is operating	Development



	correctly by displaying the appropriate warning message. Unit test data – Fabricated or SWA-specific master data is entered manually as required for unit testing and used by other teams, where appropriate.	
Scenario (Integration) Testing	Validates a set of business processes that define a business scenario in a comprehensive and self-contained manner on a macro level. - Integration testing is recommended to be performed in multiple iterations. - The initial iteration of integration testing concentrates on testing all-important business processes within the components of the migrated solution, starting with touchpoint scenarios and ending with end-to-end scenarios. - The final iteration of integration testing focuses on cross-functional business scenarios with systems and applications, custom development objects, converted data, and solution security	Development
User Acceptance Testing (UAT)	Users test the complete, end-to-end business processes to verify that the migrated solution performs the intended functions and satisfies the business requirements	Quality
Load Testing	Conduct Load testing to evaluate how a system behaves under expected or peak user loads	Non-PRD
Penetration Testing	Conduct Penetration testing to identify security weaknesses & system vulnerabilities	Non-PRD

5.8.2 Test Roles and Responsibilities

- SWA will provide user roles and responsibility before executing the testing phase.
- KaarTech will execute Unit Testing in the development landscape of the activated solution.




- Integration Testing will be executed by KaarTech. Integration Testing will be carried out with standard authorizations.
- User Acceptance Testing will be executed by SWA's Key Users to validate the end-to-end business processes.
- KaarTech will provide Unit Testing test plans and test scripts for Unit Testing.
- SWA will provide the Integration and User acceptance Test scenarios whereas KaarTech will provide the Integration and User acceptance Test scripts.
- SWA will validate and sign off UAT Scenarios and testing outcomes.

5.8.3 Roles & Responsibilities

The table below shows the different responsibilities per test cycle:

S. No	Activities	Responsibility	
		Primary	Secondary
1	Preparing the UAT script & UAT Plan	KaarTech Consultant	KaarTech Project Manager
2	Circulating the UAT script to SWA Business Process Owner's	SWA Project Manager	N/A
3	Finalizing the Test script and business scenario for UAT	SWA BPO	SWA Project Manager
4	Circulating the UAT Plan to Business Process Owner's	SWA Project Manager	N/A
5	Approving the UAT Plan	SWA Project Manager	SWA PMO
6	Ensuring 100% Business Process Owner's availability for UAT	SWA Project Manager	N/A
7	Test execution only based on approved Test script	SWA Business Process Owner's	SWA Project Manager
8	Recording the issues log of UAT	SWA Business Process Owner's	SWA Project Manager



9	Prioritising the issues as Backlog where must to have nice to have will be prioritized	SWA Project Manager	SWA Business Process Owner's
10	Fixing the must to have issue for Re-UAT	KaarTech Consultant	KaarTech Project Manager
11	Sign off the UAT	SWA Business Process Owner's	SWA Project Manager

5.8.4 Testing Assumptions

- Unit testing and integration testing must be completed successfully before the commencement of User acceptance Testing.
- Training must be delivered successfully before the commencement of User Acceptance Testing
- Testing should be done by Key users. The Key users identified during Prepare Phase will be responsible for doing the User Acceptance Testing.
- The UAT invitation will be sent by SWA Project manager based on the UAT plan.

5.8.5 Training Exclusions

- Any third-party system development and testing are excluded from the scope.
- 3rd party systems side of testing for integration scenarios which is not mentioned explicitly in scope
- Any other users other than the ones identified during Prepare phase should not perform the User Acceptance testing.

5.9 Technical Assumptions

- The latest version of the proposed solutions, available as of the date of the project kick-off shall only be deployed.
- All the requirements compliance is subject to product compatibility. Hence KaarTech is not liable to consider the product non-compatible items in the scope of work.
- The components mentioned in the high-level solution diagram shall be subjected to change based on SWA's actual landscape.



- KaarTech shall implement the exact standard P2P process in alignment to Development Scope as per the project's timeline without any customizations. Any additional customizations apart from the listed in Development Scope shall have an impact on the timeline and subsequently commercials shall be realigned.
- KaarTech will follow standard UX guidelines.
- KaarTech assumes OData gateway server is established and activated.
- KaarTech assumes Windows/Linux server is available for node and angular application deployment.
- If SWA does not have a Document Management System (DMS). Consequently, SWA shall benefit from employing manual upload and download functionalities for document handling, which shall be stored in SAP S/4HANA Application Layer.
- SWA has access to high-quality, structured historical tender, proposal, and vendor performance data for effective AI model training and validation.
- Integration APIs or middleware are available for seamless data exchange between the AI solution, the RFP Lifecycle Add-On system, and enterprise platforms like SAP S/4HANA or SAP Ariba.
- It is assumed that SWA will take full ownership and responsibility for all platform-related costs, including but not limited to:
 - Subscription fees
 - Licensing
 - Usage-based billing
 - Any infrastructure or service costs associated with Google Cloud Platform (GCP), Vertex AI, Gemini, or any other third-party platforms/services utilized as part of the proposed solution.
- Kaar Technologies will be responsible solely for the service delivery costs as outlined in this proposal.

5.10 Technical Exclusions

- Transaction entry on behalf of SWA business users
- Re-organizing, modifying, simplifying, and standardizing of the organizational processes and procedures shall be the responsibility of SWA and is out of scope for this engagement.
- Any Modification of existing functional scope or application in SWA
- Any Hardware & Licenses procurement.



- Any activities related to third party systems will be taken care by SWA and it will not be considered in KaarTech scope.
- Any further development apart from the mentioned Scope of Work.
- Any components related to hardware's, servers & licenses shall be procured by SWA separately and it is not a part of this project & commercials.
- For any requirements not outlined in Scope of Work, a separate change request (CR) shall be initiated by SWA.
- Implementation of Document Management System.
- The AI solution will not handle manual data entry or correction of legacy data errors; responsibility for data cleansing and preparation remains with the SWA.
- Support for proprietary or non-standard document formats outside of supported templates (such as uncommon file types or handwritten submissions) is not included in the implementation scope.
- Any other AI use case apart from the mentioned scope.



|| 6. Support Scope

6.1 Support Period

The Hypercare Support Period planned under this project is 4 Months post completion of go-live followed by 8 months of technical support.

6.2 Service Window

KaarTech will follow SWA's calendar (Sunday to Thursday) and Business working hours (max 8 hours a day)

6.3 Support Tool

SAP Solution Manager (SOLMAN) shall be utilized as Ticketing Tool during the Hypercare Support Period and all tickets shall be recorded, dispatched, resolved & communicated through SOLMAN.

6.4 Classification of Calls and Procedures

Calls are classified based on their criticality into various categories as follows:

| L1 issues

- Basic navigational issues
- Master data – (such as extension of SWA master records)
- Issues involving basis transactional steps
- Normally resolved by power users

| L2 issues

- Authorization issues, any analysis issue
- Business knowledge / training
- Debugging (for Problem Tracking)
- Integration / Interface issues (Independent Assignment)
- Master data (without customization)
- System bug / transactional error (Requires Less Effort)



L3 issues

- Authorization issues (incl. creation of new roles / role modifications)
- Debugging (for solution)
- Integration / Interface issues (Dependent Assignment)
- Master data (with customization)
- System bug / transactional error (Requires More Effort)
- Analysis issue involving other modules
- Application of note(s)

6.5 Service Level Parameters for Incident Management

Severity	Description
S1 – High	Defect has a critical impact on the overall system / deliverable and the current activity cannot proceed further until the defect is addressed. There are no workarounds, and the impact is on the majority or the entire users. The quantum of the impact is very high for business financially. Only System Unavailability shall be treated as High.
S2 – Medium	Defect has a high impact on the overall system / deliverable, but the current activity can proceed further. Workarounds exist and the impact of using a workaround is internal to the system / deliverable. Defects will not have major impact on other work streams / deliverables.
S3 – Low	Defect does not have a high impact on the system / deliverable. The defect can be addressed internally within the system / deliverable. A process affected by the Defect can be managed through a work around or can be on hold till the resolution is achieved. The impact on other work streams / deliverables is negligible or zero. Suggestion to enhance deliverable in solution – where the suggestion does not have an impact on deliverable / system, could also be cosmetic defects.

6.6 Exceptions in SLA

The above SLA is not valid in case of:




- Any problems in OEM's Datacentre
- Issues with operating system, servers, storage area network and connectivity (VPN, Router String)
- Failure of end-users Local Area Network
- Any other outage due to reasons that are out of KaarTech 's direct control.
- If any clarification sought by KaarTech and it is pending with SWA, SLA hours will not be counted.

6.7 Incident Response and Resolution Time

S. No	Category	Avg. Response Time	Avg. Resolution Time
1	S1 – High	4 hours	8 hours
2	S2 – Medium	8 hours	3 days
3	S3 – Low	16 hours	7 days

Note

- The above-mentioned Service Level Parameters are applicable only for incidents and are not valid for service request, any enhancement / development activities.
- The above-mentioned Service Level Parameters are applicable only for "Onsite Dedicated Support Services".
- The above-mentioned response/resolution time are business hours.

Definition

- Average Response Time: This is the time taken by KaarTech consultants to respond to an incident raised by SWA's end users. It can also be referred as Initial Response Time (IRT).
- Average Resolution Time: This is the time taken by KaarTech consultants to close an incident raised by SWA's end users. It can also be referred as Maximum Processing Time (MPT).
- 8 Hours = 1 Working Day



6.8 Support Assumptions

- SWA to ensure the presence of a support coordinator/ support SPOC to be available throughout the support period.
- KaarTech has considered Hybrid (Onsite/Offshore) Execution Model for Hypercare Support Period & Remote Execution Model for Technical Support Period.
- KaarTech has considered only Incident Management under the Support Scope.
- Additional developments in will be considered as a change request to ensure regular support activities are not disturbed.
- A ticket will be closed when there is no response from SWA after 3 remainders from KaarTech.

6.9 Support Exclusions

The following are not considered as part of scope for this support model:

- Technical and Functional upgrades and migration.
- Any new module supports other than the ones listed in the scope of work.

6.10 Knowledge Transfer

KaarTech strongly believes that knowledge transfer to the new support vendor is important.

The following approach will be used for a smooth transition from the existing support team to KaarTech Support team.

KT Process

During Knowledge Transfer, the new vendor's transition team will make all necessary efforts to gather necessary business knowledge from KaarTech by means of collaborating with KaarTech team.

KaarTech's consultants will provide detailed walkthroughs of the applications to the new vendor's team. The most used functionalities, major developments, user profiles, authorizations, roles, and security will be covered as part of this activity. Based on this, the KaarTech team will develop a transition checklist to ensure completeness of transition to the new vendor's support team.

Below is the process followed:



1. KT Giver to publish the KT Status Tracker with Topics, Schedule & Supporting Document Name (Attached Template)
2. KT Giver to provide KT per the schedule & post KT Status Tracker (Updated) with updated status post completion of each session
3. KT Receiver to prepare KT Understanding Document (Attached Template)
4. KT Giver to signoff/approve the KT Understanding Document

This would help to have streamlined Knowledge Transfer (KT) and acceptance from New Team Member on receipt of KT.

Documents

SWA shall provide necessary access to KaarTech personnel for the document repository for further maintenance and update. This will help KaarTech consultants to provide storage of documents in centralized repository. As part of this transition process, KaarTech consultants will provide the below documents:

- Business Process Documentation
 - Solution design document
 - Testing scripts
 - User Manuals
 - User Acceptance documents of SWA to get a clear idea about the process SWA follows for their business
- Implementation Documents
- Technical Documents
 - System Landscape and Hardware Infrastructure and implications
 - Inventory of Customized Transactions and its usage
 - Inventory of Report Variants
 - Inventory of Interfaces
 - Inventory of third-party system integration
 - Inventory of Background Jobs (Batch jobs)
 - Inventory of Data extracts and uploads

Validation

The new vendor team will validate the acquired knowledge with the KaarTech through reverse knowledge transfer process. This will help in updating relevant documents based on our understanding and as per best practices.



7. Project Execution & Approach

7.1 Project Delivery Methodology

The project shall be executed in alignment to KaarTech's Delivery Methodology (KDM).

KaarTech's Delivery Methodology (KDM) is a refined evolution from the SAP Activate Methodology, presenting a robust framework tailored for successful implementations. KDM lays the groundwork and ensures alignment before project initiation in the Prepare phase. Through value driver sessions, KDM facilitates profound understanding and stakeholder alignment. KDM offers self-enablement opportunities for non-SAP tools, empowering teams with diverse skills. Augmented Organizational Change Management (OCM) activities address the human element of transformation, guaranteeing stakeholder buy-in and seamless transitions. By incorporating multiple solution walkthroughs, mock cutovers, and customer touchpoints, KDM emphasizes collaboration, feedback, and continual enhancement. Its comprehensive data migration plan and stringent Go-Live acceptance criteria illustrate how KDM will help businesses grow and prosper.

Prepare

The Prepare phase is the foundational stage for initial planning and preparation across the project. In this phase, the project is initiated, plans are finalized, project teams are assigned, and work begins to ensure the project starts optimally. This pivotal phase lays the groundwork for seamless execution across the project, setting the stage for success from the outset. The primary focus during this phase is to ensure everything is in place, including finalizing plans, assigning teams, and initiating work to work to ensure the wave begins optimally.

Explore

The Explore phase aims to craft comprehensive plans across all implementation workstreams, encompassing scoping, testing, end-user enablement, operations, and solution configuration, to guide execution during the Realize phase.

Realize

The Realize phase focuses on executing plans formulated in the Explore phase, configuring the solution based on approved backlogs, preparing users for transition, conducting end-user training, and readying the productive environment for cutover.



Deploy


The purpose of the Deploy phase is to cut over to the production system. After confirming organization readiness, the business and the operations are switched to the new system.

Run/Hypercare

The Hypercare phase encompasses the deployed solution's ongoing operational management and optimization, focusing on monitoring, maintenance, support, and continuous improvement to ensure sustained functionality and alignment with business objectives.

7.2 Project Plan

KaarTech has furnished the below indicative L1 project plan for SWA's Procure to Pay Automation solution to meet the business requirements of SWA.

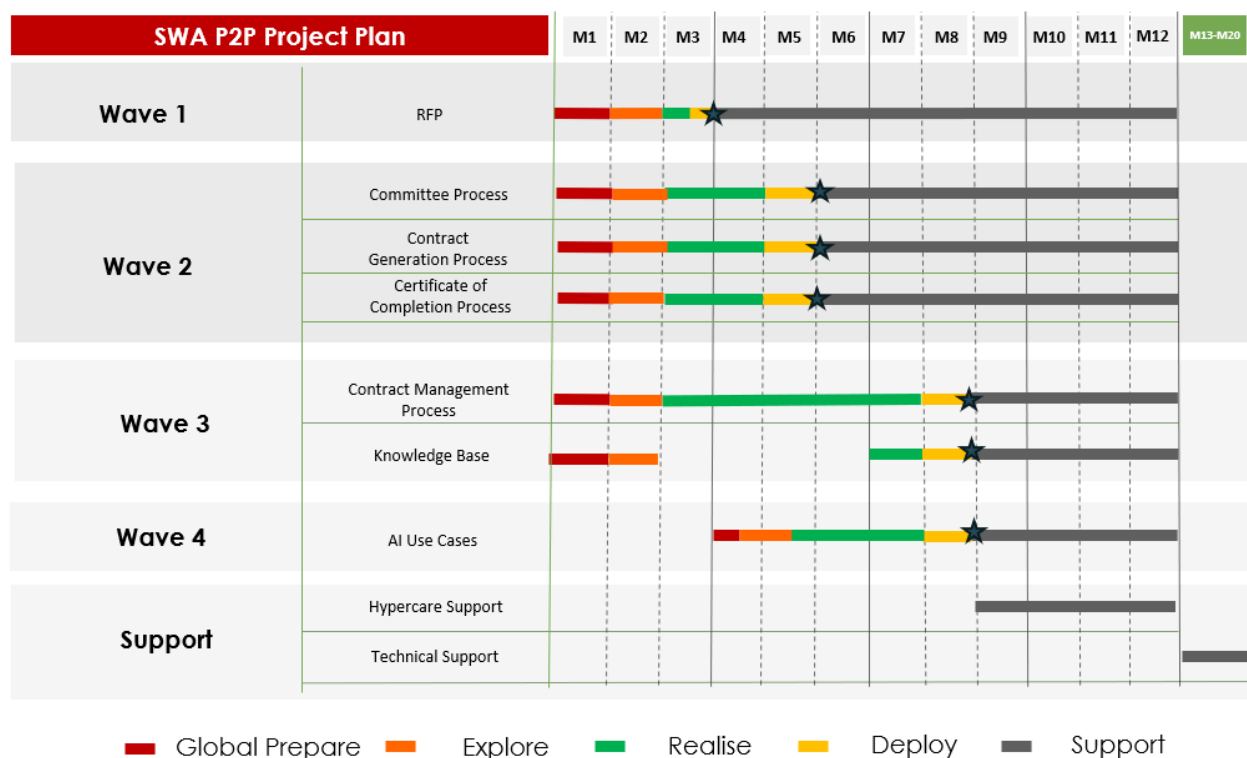

Note: KaarTech has provided a L2 Project Plan as additional supporting document as part of the bid package in the file "KaarTech_SWA_Project Plan_ 250739015178_ Project to Create an Electronic Platform for Managing the Competition Lifecycle in Integration with Corporate Systems and Artificial Intelligence Technologies _V1.0_08082025"



7.3 Release Plan

S. No	RFP Line Item	Description	Process	Wave	Release Plan
1	Automated order management processes from purchase order to purchase order	Automation of order management processes from the purchase order stage to the creation of the contract	RFP Process	Wave 1	M3
			Committee Process	Wave 2	M5
			Contract Generation Process	Wave 2	M5
2	Automation of contract management processes	Automation of contract management processes	Certificate of Completion Process	Wave 2	M5
			Contract Management Process	Wave 3	M8
3	Providing Artificial Intelligence Services	According to the AI use cases mentioned in the brochure	AI Service Provision	Wave 4	M4-M8
4	Creating a Knowledge base	Creating a unified database that includes all previous and new projects	Knowledge Base	Wave 3	M8
5	Technical Support	Integrated technical support for the system	Hypercare Support	N/A	M9-M12
			Technical Support	N/A	M13-M20

7.4 Project Deliverables

The deliverables listed below are the standard set of deliverables as part of the proposed approach. The final deliverables will be finalized during the initial phase of the project.



S N O	Phases	Deliverables	Task Owner	Document Type
1	Prepare	Stakeholder Identification & Analysis	Customer Success Manager	Document
		Approval of Authority Matrix & Project Progress Metrics	Customer Success Manager	Document
		SAP Agile/ Activate Methodology and KTERN Enablement	Customer Success Manager	Mail confirmation
		Project Charter sign off	Customer Success Manager	Document
		Project Management Plan	Customer Success Manager	Document
		Project Plan - L3 Project Plan	Customer Success Manager	Document
		Prepare - Training Strategy	Customer Success Manager	Document
		Prepare - Testing Strategy	Customer Success Manager	Document
		Data Migration Approach and Strategy	Customer Success Manager	Document
		Conduct Project Quality	Customer Success Manager	Mail confirmation




		Phase Steering Committee	Customer Success Manager	Attendance & MoM
2	Explore	Fit-to-Standard Analysis and Workshop	Customer Success Manager, Functional & Technical Consultants	Mail confirmation
		Configuration Definition	Functional Consultants	Document
		User Access and Security (Role Matrix)	Functional Consultants	Document
		Integration Preparation	Functional Consultants	Mail confirmation
		Backlog Workshop (FRICEW)	Functional Consultants	Document
		Data Load Preparation	Functional Consultants	Document
		Solution Design Document Sign off	Functional Consultants	Document
		Functional Requirement Specification/ TDS	Functional Consultants	Document
		UI/UX Screens Sign off	Technical Consultant	Mail confirmation




		Conduct Project Quality Gate	Customer Success Manager	Mail confirmation
		Conduct Steering Committee	Customer Success Manager	Attendance & MoM
3	Realize	Solution Extension Development	Functional Consultants	Mail confirmation
		Integration Setup in the Test Environments	Functional & Technical Consultants	Mail confirmation
		End User Training Strategy and Plan	Functional & Technical Consultants	Document
		End-User Training Materials and Resources	Functional & Technical Consultants	Document and Mail confirmation
		User Acceptance Testing Script Execution (L5 and L4)	Functional & Technical Consultants	Mail confirmation
4	Deploy	Solution Extension Deployment on Production	Functional Consultants	Mail confirmation
		End User Training	Functional Consultants	Mail confirmation
		Go-Live Approval Document Sign off	Customer Success Manager	Document




		Establish Hyper care and Support Strategy & Plan	Customer Success Manager	Document
		Go Live Readiness Acceptance from BPO's	Customer Success Manager	Mail confirmation
		Establish Acceptance Criteria Plan for Go/No-Go Decision Moment	Customer Success Manager	Mail confirmation
		Conduct Q Gate review with Practice Leads & PMO	Customer Success Manager	Mail confirmation
		Publish Phase Closure Criteria	Customer Success Manager	Document
5	Run (Hypercare Support)	Post Go-Live Support	Customer Success Manager	Mail confirmation
		Complete Documents Handover	Customer Success Manager	Mail confirmation
		Complete Lessons Learned Document	Customer Success Manager	Document
		Obtain Project Closure	Customer Success Manager	Mail confirmation

Below AI Deliverables are listed in alignment to delivery of the P2P Add-On Solution,

AI Deliverables

Deliverable ID	Deliverable Name	Description	SWA RFP Defined Phase	KaarTech Proposed
----------------	------------------	-------------	-----------------------	-------------------



				Phase (in alignment to P2P Add-On Solution Implementation)
AI-D1	AI Use Case Design Document	Definitions and expected behaviors for each use case (e.g., tender review, bid analysis, prequalification analysis)	Design	Prepare
AI-D2	Tools & Platform Specification	List of AI/ML tools (e.g., NLP, OCR, LLMs), platforms (e.g., GCP services), and integration components	Design	Explore
AI-D3	AI PoC / Live Demonstration	Working prototype for at least one-use case (e.g., auto-review of tender content or bid comparison)	Development	Realize
AI-D4	Integrated AI Services	AI modules connected to RFP Add-On and SAP S/4HANA / Ariba for live data use	Integration	Realize
AI-D5	AI Workflow Automation	Automated workflows for proposal review, extraction, and evaluation with committee input	Integration	Realize
AI-D6	AI Testing & Validation Reports	Functional and performance testing results of AI components with accuracy metrics and edge-case handling	Testing	Realize
AI-D7	AI Security Compliance Checklist	Documentation proving alignment with SWA cybersecurity, data protection, and GCP IAM/security policies	Support Phase	Realize




AI-D8	AI Monitoring & Optimization Report (Post-Go-Live)	Monthly performance reviews, retraining logs, feedback integration	Support Phase	Support
AI-D9	AI User Guide & Admin Manual	Documentation for using and managing AI features — how to run, monitor, retrain, and interpret results	Project Closure	Project Closure

AI BOQ

Item No.	Description	Quantity	Unit	SWA RFP Defined Phase	KaarTech Proposed Phase (in alignment to P2P Add-On Solution Implementation)	Remarks
1	Design and definition of AI use cases	1	Lot	Phase 1 – Planning	Prepare	Includes scope alignment and mapping cases to RFP workflow
2	GCP access setup and cloud environment configuration	1	Lot	Phase 1 – Setup	Explore	Includes account provisioning, IAM, security setup
3	Development of MVP use cases (UC-01, UC-02)	2	Use Cases	Phase 2 – MVP	Realize	Tender review & completeness validation
4	Proof of Concept (PoC) demonstration of MVP use cases	1	Lot	Phase 2 – MVP	Realize	Required for initial acceptance before further development
5	Development of	2	Use	Phase 3	Realize	Vendor




	core use cases (UC-03, UC-04)		Cases	– Core		prequalification and financial comparison
6	Development of full use cases (UC-05)	2	Use Cases	Phase 4 – Full	Realize	Technical compliance check and report generation
7	Integration with RFP Lifecycle Add-On and SAP systems	1	Lot	Cross-phase	Realize	Covers API setup between AI services, SAP S/4HANA, and Ariba
8	Training and onboarding for AI features	1	Lot	Phase 4 – Training	Realize	Covers end-user and admin training
9	Documentation of AI features, configurations, and operating procedures	1	Lot	Phase 4 – Closure	Deploy	Final manuals, guides, and handover docs
10	Support and maintenance for AI services	12	Months	Phase 5 – Support	Support	Ongoing tuning, fixes, and GCP environment support post-go-live

7.5 Project Organization Structure

KaarTech has incorporated the below indicative Project organization structure for this project:



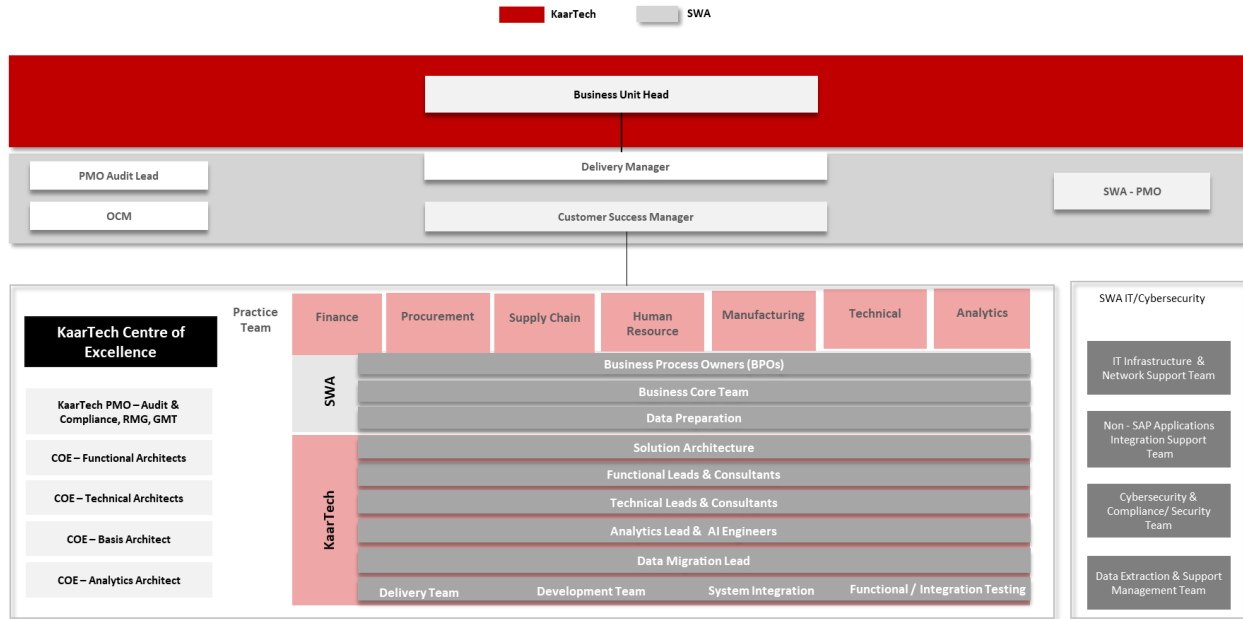

7.6 Project Governance

KaarTech recognizes the importance of effective governance and proposes the following governance model to ensure the success of the engagement. Engagement with SWA will be governed at 4 levels as follows and the same is depicted in the following diagram:

- Strategic Committee
- Tactical Level
- Project Management Level
- Delivery Level



	ROLE	FREQUENCY & CADENCE	OBJECTIVES	ATTENDEES	OUTPUTS
Strategic	PROJECT STEERING COMMITTEE	Monthly (1st Sunday)	✓ Review progress of the overall project, including benefits and realization scope and progress against the budget ✓ Align on cross-functional topics ✓ Provide direction for issue resolution	✓ Steering Committee Members	✓ Review high level project status ✓ Resolution of escalated issues
Operational	PROJECT STATUS MEETING	Weekly/ Fortnightly (Thursday)	✓ Align on the progresses of each stream ✓ Identify risk and relevant mitigation actions ✓ Define detailed activities plan ✓ Review and validate deliverables ✓ Address performance issues to tactical resolution tier	✓ Business Process Owner Head(BPO) ✓ SWA PMO ✓ KaarTech PMO	✓ Tasks priority list ✓ Issue list & resolution plan ✓ Deliverables validation
Advisory	SCOPE CHANGE ADVISORY Committee / Project Sub Committee(s)	Fortnightly/ (on demand)	✓ Review, estimate, validate, prioritize, and escalate scope change requests & review urgent matter to avoid delays	✓ Business Process Owner Head (BPO) ✓ SWA PMO ✓ KaarTech PMO	✓ Change request & costs ✓ Issue Log
Workgroup	PROJECT TEAMS	Daily	✓ Team / workgroup daily alignment, along project activities execution	✓ Project Team members	✓ Deliverable

****Above model will be refined based on mutual discussions and agreement.**

- A Project Manager will be on board from commencement who will be leading the project as well as being focal point of contact for the complete project deliverables.
- The project agenda will be guided at the highest level by a steering committee peopled by top management representatives from SWA and KT. It will also have a representative from the KT Account Management team setup specifically for this engagement.
- The Project Manager would be responsible for creating the detailed project plan in close consultation with SWA Project Manager / Owner. The Plans would cover all aspects of the project including identifying stakeholders, communication & escalation processes, Detailed Transition Plan with Dependencies & assumptions & Milestones.
- The Project Manager will support in the actual Project Execution & Delivery, ensuring the project continues to function smoothly and delivery & milestones are reached on schedule. Also, Issue Resolution & Relationship Management would remain the key responsibilities of the Project Manager .
- During the entire engagement, KT will have the Delivery Manager, who is based onshore, aligned with the project. He would be visiting the SWA office on regular intervals and on a needy basis.
- Besides, the KT Quality team would help in continuous process improvement which would ensure quality deliverables.



7.7 Project Roles & Responsibilities

7.7.1 KT - Roles and Responsibilities

Given below are the roles and responsibilities of KT Project Stakeholders:

Role	Responsibilities
Project Manager	• Project planning • Status reporting of the project • Manages project risk and track to closure
SAP Functional Consultant	• Drives business requirement understanding, specification, and analysis. • Creation of High-level design • Mapping of to be business processes flows with SAP functionalities and performing fit gap analysis. • Configuration and prepare detailed design document • Designs the custom development needs. • Develops custom reports. • Provides key subject matter inputs to the team. • Validates the application being implemented. • Prepares/validates test cases and test results. • Support in UAT • Provides functional Early Life Support • Tests the application to ensure proper functionality
SAP Basis Consultant	• System Administration • Support for SSO Configuration
SAP Technical Consultant	• Develops code for technical objects • Designs the custom development needs. • Develops interfaces between SAP and SFSF • Tests the application to ensure proper functionality. • Develops custom reports
SAP Integration Consultant	• Integrates between SAP and other third-party application. • Integrates between SAP S/4HANA and other cloud solutions.

UI/UX Designer	• Convert UI/UX designs into responsive, interactive web/app interfaces using HTML, CSS, JavaScript, and frameworks like React or Angular. • Collaborate with back-end teams to integrate APIs and ensure seamless functionality. • Optimize interfaces for performance, usability, and cross-browser compatibility.
UI Developer	• Create visually appealing and user-centric designs for websites, apps, or software. • Develop wireframes, mock-ups, and prototypes using tools like Figma, Sketch, or Adobe XD. • Collaborate with UX designers and developers to ensure design consistency and usability.
AI Engineers	• Build and deploy AI models for automation, analytics, and insights. • Integrate AI with SAP and other systems. • Train, test, and fine-tune models using relevant data. • Ensure transparency, accuracy, and performance in AI outputs.

7.7.2 SWA - Roles and Responsibilities

Given below are the roles and responsibilities of SWA Project Stakeholders:

Resource	Role Description	Duration
Project Manager	Reporting to the steering committee and parallel responsibility for Project execution.	Entire duration of the project
Core Team Members	Subject Matter Experts are involved in the full implementation cycle and should be available full-time, throughout the project duration. Should bring to the project authentic details of Business process in their respective field.	Entire duration of the project

Business Process Owner	For Decision-making on approving the Business Process Blueprint.	Entire duration of the project
Subject Matter Experts	Subject Matter Experts in specific business process and would supplement the core team members when process-specific specialized inputs are required.	During phase Explore
Key Users	Senior process experts who do the day-to-day transactions in the system. The Key users will be given the first round of training by the core team members. They will support the core team members when training the end-users.	During phase Deploy
End Users	User experts who do the day-to-day transactions in the system. They are the final level of transactional users who will have to be trained in SAP processes only in their area of function. They will have to attend the end-user training as part of the implementation	During phase Deploy
Technical AI SPOC	Acts as the main liaison for all AI-related project activities, ensuring alignment between SWA's technical requirements and the solution. Coordinates with AI engineers, functional teams, and vendors to oversee AI integration, testing, and performance validation.	Entire duration of the project
Cybersecurity SPOC	Serves as the primary contact for cybersecurity matters, ensuring that all project activities comply with SWA's security policies and regulatory standards. Oversees security reviews, risk assessments, and incident response coordination during the project lifecycle.	Entire duration of the project




7.7.3 RACI Matrix

S No	Phases	Deliverables	RACI Matrix
1	Prepare	Stakeholder Identification & Analysis	R- CSM A- PMO C- BU I- Customer PM
		Approval of Authority Matrix & Project Progress Metrics	R- CSM A- PMO C- BU I- Customer PM
		SAP Agile/ Activate Methodology and KTERN Enablement	R- CSM A- PMO C- BU I- Customer PM
		Project Charter sign off	R- CSM A- PMO C- BU I- Customer PM
		Project Management Plan	R- CSM A- PMO C- BU I- Customer PM
		Project Plan - L3 Project Plan	R- CSM A- PMO C- BU I- Customer PM
		Prepare - Training Strategy	R- CSM A- PMO C- BU I- Customer PM
		Prepare - Testing Strategy	R- CSM A- PMO C- BU I- Customer PM
		Data Migration Approach and Strategy	R- CSM A- PMO C- BU I- Customer PM




		Conduct Project Quality	R- CSM A- PMO C- BU I- Customer PM
		Phase Steering Committee	R- CSM A- PMO C- BU I- Customer PM
2	Explore	Fit-to-Standard Analysis and Workshop	R- CSM A- PMO C- BU I- Customer PM
		Configuration Definition	R- CSM A- PMO C- BU I- Customer PM
		User Access and Security (Role Matrix)	R- CSM A- PMO C- BU I- Customer PM
		Integration Preparation	R- CSM A- PMO C- BU I- Customer PM
		Backlog Workshop (FRICEW)	R- CSM A- PMO C- BU I- Customer PM
		Data Load Preparation	R- CSM A- PMO C- BU I- Customer PM
		Solution Design Document Sign off	R- CSM A- PMO C- BU I- Customer PM
		Functional Requirement Specification/ TDS	R- CSM A- PMO C- BU I- Customer PM




		UI/UX Screens Sign off	R- CSM A- PMO C- BU I- Customer PM
		Conduct Project Quality Gate	R- CSM A- PMO C- BU I- Customer PM
		Conduct Steering Committee	R- CSM A- PMO C- BU I- Customer PM
3	Realize	Solution Extension Development	R- CSM A- PMO C- BU I- Customer PM
		Integration Setup in the Test Environments	R- CSM A- PMO C- BU I- Customer PM
		End User Training Strategy and Plan	R- CSM A- PMO C- BU I- Customer PM
		End-User Training Materials and Resources	R- CSM A- PMO C- BU I- Customer PM
		User Acceptance Testing Script Execution (L5 and L4)	R- CSM A- PMO C- BU I- Customer PM
4	Deploy	Solution Extension Deployment on Production	R- CSM A- PMO C- BU I- Customer PM
		End User Training	R- CSM A- PMO C- BU I- Customer PM




		Go-Live Approval Document Sign off	R- CSM A- PMO C- BU I- Customer PM
		Establish Hyper care and Support Strategy & Plan	R- CSM A- PMO C- BU I- Customer PM
		Go Live Readiness Acceptance from BPO's	R- CSM A- PMO C- BU I- Customer PM
		Establish Acceptance Criteria Plan for Go/No-Go Decision Moment	R- CSM A- PMO C- BU I- Customer PM
		Conduct Q Gate review with Practice Leads & PMO	R- CSM A- PMO C- BU I- Customer PM
		Publish Phase Closure Criteria	R- CSM A- PMO C- BU I- Customer PM
5	Run (Hypercare Support)	Post Go-Live Support	R- CSM A- PMO C- BU I- Customer PM
		Complete Documents Handover	R- CSM A- PMO C- BU I- Customer PM
		Complete Lessons Learned Document	R- CSM A- PMO C- BU I- Customer PM
		Obtain Project Closure	R- CSM A- PMO C- BU I- Customer PM

7.8 Communication Mechanism

Communication will be carried out between SWA and KT through the following means:



- Status reporting
- Progress reviews
- Issue resolution
- Project communication

KT focuses on building strong transparent communication channels. Joint regular steering meetings ensure overall engagement focus while effectively resolving issues & problems on the way.

Listed is the communication mechanism that will be implemented for SWA Engagement.

S No.	Report Name	Frequency	Purpose
1	Status reports	Weekly	For recording/tracking the status of project activities with respect to the project plan
2	Risk register	Bi-Weekly	For better risk tracking and quicker resolution
3	Issue Log	Weekly	For better Issue tracking and quicker resolution
4	Change Log	Monthly	For better change tracking and quicker resolution
5	Steering committee presentation	Quarterly	Status reporting of the project along with the issues faced, process improvement activities, resources etc. Steering committee frequency will be decided during the preparation phase.

Note: This is an indicative list, and the actual number and types of reports will be discussed and agreed upon during the start of the engagement. Any emergency meeting shall be scheduled based on the decision taken by Steering Committee.



7.9 Escalation Mechanism

We have a well-defined organizational structure and work with a well-defined framework and project structure comprising of a steering committee and account management to take care of any issues and escalations.

Levels	Escalation Type	SWA Responsible Person	KT Responsible person
Level 3	Strategic	Project Sponsor	Delivery Manager
Level 2	Tactical	Project Manager	Project Manager / CSM
Level 1	Operational	BPOs	Module Leads

Listed is the escalation mechanism that will be implemented for SWA engagement.


Note: As outlined in the clarification response sheet, the final escalation matrix will be mutually discussed and agreed upon between SWA and KT during the Prepare Phase.

7.10 Risk Management

KT's Risk Management Strategy will cover and address the below processes:

- Risk Identification
- Risk Analysis
- Risk Planning (Mitigation and Contingency Planning)
- Risk Implementation
- Risk Tracking & Control
- Communication



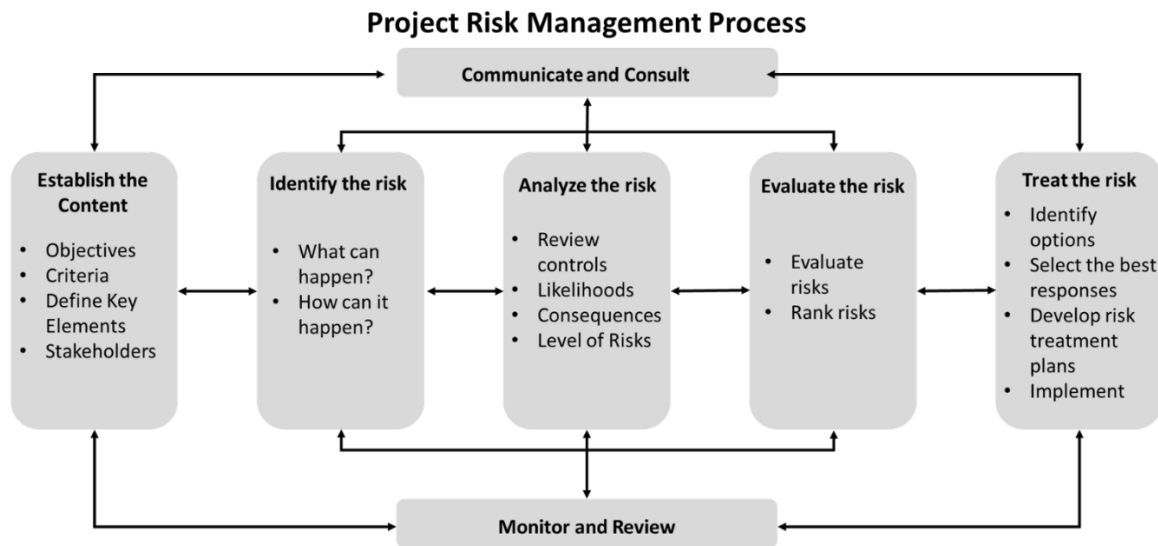

7.10.1 Potential Risk Matrix

From our experiences of managing projects, we have a fair understanding of the associated risks. We have tabled below some of the risks and mitigation plans for such risks.

Risk & Description	Risk Probability	Risk Impact	Mitigation Plan
Non-availability of SMEs, especially during Business requirements phase, due to business commitments.	Medium	High	KT shall notify at least a week in advance; SWA to ensure the availability of key SMEs
Non-availability of Servers/ Systems/ Software/ User Licenses	Medium	High	KT to plan and organize the availability of required hardware, software and licenses
Inadequate Hardware Sizing for Optimizers	Medium	High	KT shall assist SWA with advance planning for procurement of hardware with suitable parameters
Non-availability of appropriate consultants for the project	Medium	Medium	KT Project Manager and Project manager to ensure availability and back-ups

Inter-dependent processes affected due to member absence	Low	Medium	Project Managers to formulate reasonable leave policies for the project
Lack of clear project scope, unrealistic timelines, or insufficient resources can lead to project delays and cost overruns.	Medium	High	Conduct a thorough readiness assessment before starting the project. Establish a clear roadmap with defined milestones. Allocate resources based on realistic project needs. Regularly review and update the project plan as needed.
Migrating data from legacy systems to S/4HANA is complex and can lead to data inconsistencies, loss, or quality issues.	High	High	Perform a detailed data quality check prior to migration. Implement data validation processes at every stage of migration. Ensure that backup plans are in place in case of migration failure
Excessive customization of the S/4HANA system can increase complexity, leading to higher costs and difficulties in maintenance.	Medium	Medium	Stick to standard functionalities whenever possible. Avoid over-customization unless absolutely necessary. Perform a fit-gap analysis to assess which customizations are essential. Focus on business process reengineering rather than altering the system.
Employees may resist changes, particularly when transitioning from familiar systems to S/4HANA.	Medium	Medium	Implement a robust change management strategy that involves communication, training, and stakeholder engagement. Regularly conduct training programs to familiarize users with the new system. Have key users or champions




			lead the adoption process within departments
--	--	--	--


7.11 Change Request Management

7.11.1 Why Change Request?

The scope of the project is normally defined during the 'Explore' phase (business blueprint) of the project and duly signed off by the SWA Project Stakeholders.

As the project progresses, there may be a necessity to change the scope of the project to meet any unique and specific requirements of SWA such as new Company Code creation, business process change, new developments, delay in provisioning master/open data and so on. Any change will be governed by strict scope control procedures in order to reduce the impact of the additional work on the project teams and overrun the project schedule and costs. Hence, any deviation from the agreed scope will be treated as Change Request (CR) which will be estimated and mutually agreed before taking to Realization (Development), as it involves additional timeline and costs.

7.11.2 CR Process Flow

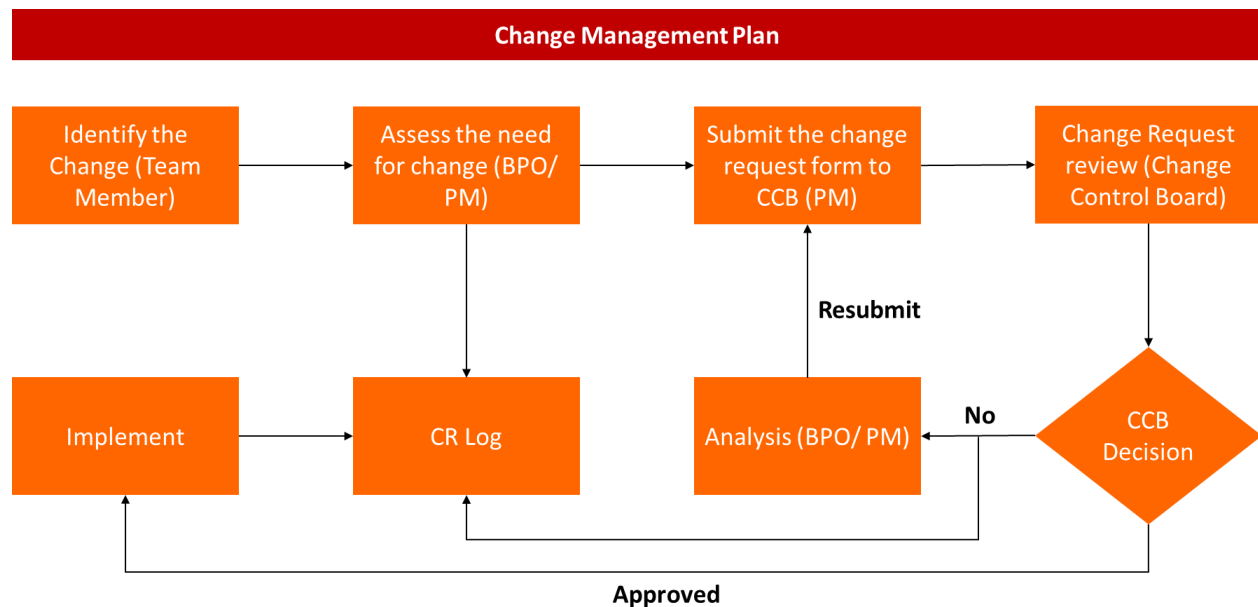

Following are the two key elements used for Change Management and Control.

- Change Request Form

- Change Request Tracker
- If any change is identified, it shall be processed through Change Request Form (CRF).
- Every Change will have a unique Change Request ID (CR ID). CR ID shall be obtained from registering Change Request in Change Request Tracker.
- Change Request Tracker should be the single repository for Registering, Monitoring, Control and Closing of any Change.
- This shall be updated by KT Project Manager throughout the project life cycle and report to SWA Project Manager regarding the progress of Change Requests.
- The sample change request forms and **change register documents have been attached as a separate file along with the technical proposal document.**

7.12 Quality Management

KT will deploy Project Quality Gate process which is a formal way of monitoring the implementation of the solution by specifying and recording the transition between critical stages in the project lifecycle. Each Project Quality Gate verifies that acceptance is met for the deliverables required and actions to be completed for the associated critical stage.

7.12.1 Objectives

- Assure quality at the milestones of the project.
- Assure you that all key deliverables and actions have been completed in compliance with best practices.
- Enable Project Managers to continuously communicate and build quality into the project.

7.12.2 Benefits

- Enhance project quality.
- Minimize project risk exposure.
- Manage expectations and monitor customer satisfaction.
- Improve transparency of the project.
- Reduce cycle time: get it done right the first time.



7.12.3 Approach

Q-Gates	
Project Quality Gates	
Executed at the end of each deliverable, it is a formal way of specifying and recording the transition between critical stages in the project lifecycle.	
Scope	- Evaluate quality of each deliverable based on the questionnaire and actual deliverable - Formal approval of the quality gate - Focus on Project Management + Limited coverage of Functional/Technical topics
Delivery Events	Prior to the end of each stage in the project lifecycle, before moving to the next deliverable
Results	Pass/No Pass Status (based on approval from QA Manager and Delivery Manager)
Follow-Up	QA Manager dispatch all follow-up activities and ensure that they have been executed

- Preparation calls to establish pre-requisites.
- Quality Gate Meeting duration half day to full day, owner is Project Manager.
- Project Manager presents overall project status and Team Leads the status of each key deliverable.
- Project Manager and Customer Project Manager review deliverable quality and verify completeness and accuracy.
- Sign off Quality Gate scorecard and Action Items for follow-up are established.
- All address specific project matters for second opinion & follow-up.

7.13 Prerequisites to Start the Project

The below pre-requisites shall be fulfilled by SWA during the starting phase of the project to ensure smooth functioning of the project:

S. No	Project Pre-Requisites
1	Project Room Setup
2	Access cards
3	Gate pass for entry into SWA premises if required.
4	Access to Network / VPN / Printer / Projector
5	SWA's user ID, licenses review, Enterprise Support review
6	Relevant License / Software should be in place before the start of the project



S. No	Project Pre-Requisites
7	Stakeholder Identification (BPO's for each module, Project Sponsor, SWA Project Manager and Steering Committee stakeholders)
8	System availability, license procurement, system partition, and business approval authority matrix to be made available by SWA before Prepare phase.
9	Stakeholder availability, stakeholder leave calendar for complete project timeline, best practice adoption and Change management enablement should be already given by SWA to their internal users & internal project team.
10	Document formats to be agreed between SWA and KaarTech
11	SWA – KSA holiday calendar for all allocated resources
12	Storage of documents
13	Meetings plan to be agreed between SWA and KaarTech
14	Daily meetings are required with all stakeholders on agreed fixed time for the entire project duration
15	SWA will make all project stakeholders available within 2 days upon request from the KaarTech.
16	SWA to have 2 working days at the maximum for any decision making and approval requests from KaarTech.
17	SWA to ensure the IT Team availability and Core team member availability throughout the Project.
18	SWA to ensure VPN connectivity for remote (KaarTech Offshore) consultants and developers. System/network availability not to be disturbed during the entire project duration.
19	SWA shall make the required Business Process Owners (1 BPO per module) and/or Subject Matter Experts (SMEs) available for the project to ensure knowledge sharing, approvals, and validation of processes defined by the project team. The same will be discussed and the schedule will be presented to SWA well in advance so that SWA could plan.
20	KaarTech requires assistance from SWA IT team throughout the project to avoid time delay.



S. No	Project Pre-Requisites
21	Considering the timeline and success of the project, we expect SWA's availability also in weekends if required.
22	Assurance of high-speed internet connectivity to conduct online sessions.
23	Availability of video conferencing facility/ intercom set up for carrying out online / remote sessions.
24	SWA must identify the PMO Team, Project Manager & Project Sponsor and ensure their availability throughout the project duration.
25	Project kick-off should happen with the presence of all stakeholders from SWA.
27	SWA to assign Dedicated SME & BPOs and ensure their availability for the Data migration.
28	SWA Business Owners must be available for any clarifications and assigned activities such as UAT, Training, Data facilitating and validating and all project activities.
29	Any document submitted to SWA for review and approval must be cleared within 2 to 4 business working days.
30	Payment pertaining to all required licenses for the entire scope should be made by SWA in advance before the start of the Project date.
31	Steering committee meetings are required fortnightly till the Go Live
32	SWA Project Sponsor(s) must attend all the Steering Committee meetings.
33	Core Team Member (CTM), BPOs, Key Users and End Users should be available during the entire Project timeline as per the User engagement calendar which will be published by KaarTech during the Prepare phase. SWA need to confirm it and make the resources available accordingly.
34	SWA office rules and regulations review.
35	SWA will be responsible for all requirement of Master data migration and Open transaction data.
36	SWA to ensure user availability for training as per plan, KaarTech is not responsible for any delay due to this.
37	SWA to ensure data quality and consistency in integrating external systems, Contractor is not responsible for any issues and delays caused thereby.




S. No	Project Pre-Requisites
38	In case of any unexpected delay in VISA processing by KSA Embassy or Government, KaarTech will notify SWA about the delay in resource mobilization. To avoid any impact in Project schedule and deliverables, respective consultant(s) shall be working from Offshore till the VISA processing is completed. KaarTech will take responsibility to ensure the delivery as per the Project Timeline from Offshore
39	SWA to ensure no additional scope is introduced during the Realize and Deploy phases of the project and KaarTech is not responsible for any delay caused.
40	SWA to share the current roles before the project start date.
41	Organization structure and proposed Organization structure to be shared by SWA structure.
42	Availability of Decision authority by department, Business approvers by department is necessary who should bring the above said data and their availability to be ensured by SWA.

7.14 Project Assumptions

- KaarTech has considered hybrid (Onsite/Offshore) execution model for implementation & hypercare support period and complete remote execution model for the technical support period.
- The onsite work location for provision of support under scope shall be SWA's Head Office premises in Riyadh and offshore work location shall be KaarTech's Delivery Centre, India. For any travel outside the project location, SWA shall bear the logistics cost (including accommodation, local travel, and conveyance) for associates deployed by KaarTech.
- KaarTech shall mobilize the resources within 4-6 weeks from the date of signing the contract.
- KaarTech has accounted 30 Onsite Man Months for Implementation & Support.
- SWA will provide the required project infrastructure in the form of system hardware, LAN, internet connectivity, communication facility, working desks, meeting rooms for KaarTech's project team members. Also, SWA will provide access to printers and scanners for project team members. VPN and existing access will be given by SWA within 1 day on request.
- SWA will make available all project stakeholders within 2 days upon request from KaarTech. Core Team Member (CTM), BPOs & Key Users should be available during the entire Project timeline as per the User engagement calendar which will be published by KaarTech during the Prepare phase. SWA needs to confirm the availability of project sponsor, project owner



and the responsible business stakeholders intact with the project plan. Any non-availability of SWA's team will be intimated by KaarTech & has to be resolved within 1 working day to avoid any deviations in timeline. In case of any schedule impact due to SWA stakeholder's non-availability due to annual leave, public holiday, etc, KaarTech shall consider the additional timeline and cost for such delayed period and shall be billed accordingly.

- SWA's Business Owners must be available for any clarifications and assigned activities such as UAT, Training, Data facilitating and validating and all project activities.
- Daily meetings are required with all stakeholders at an agreed fixed time for the entire project duration.
- Any delay from SWA's support beyond mutually agreed standard time in resolving issues raised by KaarTech during the project execution will have impact on the project timeline.
- Considering the project timeline, KaarTech expects SWA to have 2 working days at the maximum for any decision making, document signoffs and approval requests from KaarTech.
- KaarTech would ensure all the Document deliverables committed to SWA in this proposal, provided SWA agrees for a separate timeframe dedicated for the same subjected to mutual agreement.
- Required business critical documents will be mutually identified between KaarTech and SWA.
- KaarTech shall adopt train the trainer model for any such training considered
- The BPO's & Key Users who have been involved during the Explore Phase only should represent SWA during the UAT.
- Any UAT observations that are not showstoppers for Go-Live to be agreed by SWA for completion post the Go Live phase.
- KaarTech shall provide the knowledge transfer & handover the solution to SWA IT Support Team as part of project closure activities, at the end of the hypercare support period.
- The scope shall not be swapped without mutual agreement. Any descoping or reduction in the proposed Scope of Work in this Proposal to revise the commercials shall not be feasible during the project.
- Any additional scope, deviation, and activities other than those mentioned in the Scope of work section in alignment to the clauses in assumption & exclusion sections specified in this proposal, such change will be subject to the Change Request (CR) Process to assess its impact and feasibility for inclusion and may incur additional efforts, time and costs.

7.15 Project Exclusions

- Deployment of resources apart from the said location.
- Any new skills (or) resource requirements.



- Any Hardware & Licenses procurement.
- Any activities related to third party systems will be taken care by SWA and it will not be considered in KaarTech scope.
- Any further development apart from the mentioned Scope of Work.



8. Project Team

KaarTech has provided the tentative profiles for the skillsets as per the RFP. However, by taking SWA request into consideration and understanding the value of the resource skills needed for this project, KaarTech would try to retain the same resource for the entire duration. In case of unavailability of the proposed resources, KaarTech will provide alternative resources with equivalent skills and experience and will be onboarded in accordance with the timeline which is agreed between SWA and KaarTech.

S.NO	Skillset	Minimum Years Of Experience	Consultant Name
1	Project manager (SAP Experienced)	7+ years in project management, including at least 3 SAP projects.	Bala Murugan P (or) Venkatesh Y
2	SAP Functional Consultant – Procurement / MM	5+ years in SAP MM with at least two full-cycle implementation/improvement projects.	Aman Kumar Singh
3	SAP Functional Consultant – Cross-Module (FI / HCM)	4+ years across at least two modules with integration experience.	Dinesh Kumar (or) Mustafa (or) Imran Pasha Mohammad
4	SAP Technical Consultant / ABAP Developer	5+ years in ABAP development, including at least two projects in the SAP Procurement module.	Khavya Somasundaram (or) Rohan D
5	SAP Fiori / UI5 Developer or angular	3+ years in Fiori/UI5 development.	Tharachandar (or) Saurab
6	SAP Workflow Consultant	4 years' experience in workflow scenarios within SAP MM/FI/HCM.	Pavithra SE (or) Isravel J




7	SAP Integration Consultant	5+ years in integration, including SAP procurement processes.	Chidambaram K (or) Shreelakshmi A
8	SAP Security & Authorization Specialist	3+ years in SAP security across various modules.	Rajitha (or) Priyaranjan Kumar
9	SAP Test Lead / QA Specialist	4+ years in SAP testing, including User Acceptance Testing (UAT) and integration testing.	Vishal Patil (or) Vinay Kumar Chippa
10	Artificial Intelligence Specialist	Minimum 3 years in AI applications implementation and development.	Anju Shaju
11	AI Applications Specialist	Minimum 2 years in developing and managing AI-based applications.	Gathiravan G (or) Tharun S C (or) Vasanthakumar B

Note: KaarTech has provided a profile tracker as additional supporting document as part of the bid package for the above consultants in the file "KaarTech_SWA_Profile Tracker_ 250739015178_ Project to Create an Electronic Platform for Managing the Competition Lifecycle in Integration with Corporate Systems and AI Technologies _V1.0_08082025"



9. Frequently Asked Questions (FAQs)

9.1 Database

P2P Solution shall leverage the existing HANA Database in SAP S/4HANA Solution and store data in Custom Z Tables.

9.2 Hardware

KaarTech assumes that SWA shall provide either one of the below listed options for the deployment of P2P Solution.

Option 1:

1. Deployed in SAP BTP Multi Cloud Tenant through Build Work Zone Services
2. Consumed Services: SAP Build Work Zone, SAP Integration Suite, SAP Cloud Foundry Runtime

Option 2:

1. Deployed in SWA On-premises Data Centre or SWA Private Cloud
2. Hardware specifications required for deployment of Production Environment
 - VCPU's : 16
 - Memory : 32 GB
 - Storage : 250 GB
3. Hardware specifications required for deployment of Non-Production Environment
 - VCPU's : 8
 - Memory : 16 GB
 - Storage : 250 GB

9.3 Licenses

For Database Layer, P2P Solution does not require any additional licenses as it leverages the existing HANA Database in SAP S/4HANA Solution.

For Application Layer, P2P Solution does not require any additional licenses as the business logics are designed/built with consideration of provisions/limitations of SAP S/4HANA Solution.

For Presentation Layer, P2P Solution does not require any additional licenses as it uses Angular User Interface. However, it has to be hosted/deployed in either one of the listed options above.

9.4 Backend

The backend of P2P Solution is SAP S/4HANA Solution.



9.5 Workflow

The provided workflow matrix table in section [Workflows](#) is to showcase the workflow capability of the P2P Solution. Departments with different levels can be configured based on the process to achieve flexibility in adapting the workflow to the respective business. This workflow matrix shall be discussed and finalized during the Explore Phase (M2) of the Project.

9.6 Ariba

KaarTech will configure the RFI Posting in SAP Ariba System. P2P Solution shall leverage the RFI Posting Feature of SAP Ariba.

P2P Solution shall be integrated with SAP Ariba for the following processes.

1. To initiate RFI Posting to SAP Ariba from P2P Solution
2. To collect the RFI Responses from SAP Ariba to P2P Solution

9.7 Integration with Thiqah System

KaarTech shall integrate P2P Solution with THIQA System based on the below understanding received from SWA,

1. THIQA system shall provide list of qualified vendors for specific services.
2. This qualification based on specific services shall be evaluated in THIQA System.
3. The P2P-THIQA Integration scope is to get the list of qualified vendors from THIQA System based on the specific services in the RFI created in P2P Solution and initiate RFI Process only to those qualified vendors.

9.8 Contract Management Feature

KaarTech agrees to provide Contract Management Feature In Contract Process as part of the P2P Solution.

This feature shall allow the purchasing officer to monitor the Contract/PO, its services along with the service line item values, its Consumption, its delivery period & its delivery status. Also, it shall allow the purchasing officer to rate the vendor against the contract.

9.9 Change Request Feature in Contract Process

KaarTech agrees to provide Change Request Feature In Contract Process as part of the P2P Solution.

This feature shall allow the user to initiate a Change Request (modification of scope or contract value against a Contract/PR to the Vendor.



9.10 Support Period

KaarTech has considered 4 Months of Hypercare Support Period from M9-M12 post Go-Live of the P2P Solution.

Also, KaarTech has considered an additional Technical Support Period of 8 Months from M13-M20 post completion of Hypercare Support Period. In this additional Technical Support Period, KaarTech shall provide remote support services to support Incidents. A Ticket shall be categorized as Incident only if it is an unplanned interruption of a business process which successfully passed the User Acceptance Testing when executed per the Test Script. Change in Business Process is not included in the Technical Support Period.

In total, KaarTech provides 12 months of support (4 Months of Hypercare Support Period + 8 Months of Technical Support Period) post Go-Live of the P2P Solution.

9.11 Once the RFP approved will the purchasing officer will update the information of Etimad publishing information (Ex. Etimad reference number , BOD, Etc)?

Once the RFP is approved in P2P Solution, the purchasing officer shall post the RFP in Etimad and record the Etimad RFP Information (such as Etimad Reference Number, Bid Submission Deadline Date, Bid Opening Date, etc) in the P2P Solution. Based on the recorded Bid Opening Date, the Bid Opening Form shall be triggered to the Purchasing Officer to further carry out the Bid Opening Process.

9.12 In case of auto generated PR in which it is automatic system creation what will be the proposed scenario?

In case of Auto Generated PRs (from SAP Project Systems, SAP Plant Maintenance), the current process shall be modified to trigger RFP Creation instead of PR Creation and then follow the RFP Process flow in the P2P Solution to result in PR Creation in SAP System.

9.13 Will the proposed solution will have the ability for creating contract form in which the purchase order is not at the cycle of this solution.

P2P Solution shall have the capability to generate contract forms. POs/Release Orders can be mapped in relationship to the contract using PR Number as the primary key.

9.14 The mentioned team will be fixed for entire project period in order to avoid any possible disturbance.

KaarTech confirms that the onboarded project team shall remain unchanged during the course of the project unless there are exceptional circumstances, such as serious health issues affecting the individual or their family, personal loss, or employee separation.



- 9.15 The main committees (BOC , BEC , Technical Evaluation committees and BQC) are not fixed since Ex. There are more than 5 BOC and it is periodically changed and for the technical committee is project based committee.**

KaarTech confirms that the P2P Solution shall have the option to maintain/change the Committee Members through a maintenance table provided to SWA with defined roles per Role Matrix signed off during the Explore Phase of the Project which is planned in M2 of the project timeline.

- 9.16 The selection of the above different committees has to be selected on the RFP creation stage.**

KaarTech confirms that the committees are selected during the RFP Creation Stage itself in P2P Solution.

- 9.17 Since your solution designed to meet the client needs for the procure to pay, all related activities will be not limited to what has been mentioned at your offer (Development Scope Section).**

KaarTech has proposed the Development Scope to meet the mentioned timeline of the project and its respective release plan. Also, KaarTech would like emphasize that there shall be no clear definition of completion of project if the scope is open without limitations which shall also be a risk to the project success. However, KaarTech shall support to finalize the development scope along with its User Interfaces Wireframes signed off during the Explore Phase of the Project planned in M2 of the project timeline.

- 9.18 During the hyper care period any necessary changes will be carried out in which it is related to prior going live activities.**

KaarTech shall support to make necessary changes during the 4 months of Hypercare Period planned from M9-M12 of the project timeline, provided that it is identified as backlog from the mutually signed User Interfaces Wireframes & Solution Design Document.

- 9.19 The solution will have internal communications between committees if required.**

KaarTech confirms that a communication space for committee members shall be provided in the P2P Solution.

- 9.20 The solution will have the digital signature approach and it will be integrated with Tarasul if required.**

KaarTech confirms that the P2P Solution provides the option for digital signoff. However, the User should upload the Signature to the P2P Solution as pre-requisite. Also, if required, P2P solution can be planned to integrate with Tarasul to fetch Signature Information based on UID, if the respective



API is provided by Tarasul during the Explore Phase of the Project which is planned in M2 of the project timeline.

9.21 No further renewal will be required for the provided solution.

KaarTech confirms that the P2P Solution is a Custom Application built & hosted in SWA Landscape. Post completion of contract period with KaarTech, P2P Solution can be supported by any Operations Support Team with ABAP Consultant, OData Consultant, Angular Consultant, BTP Front End Consultant, BTP Back End Consultant, MM Consultant & Ariba Consultant.

9.22 Technical Clarifications

1. Development scope compliance with the functional requirements. This includes, but is not limited to: - Purchasing Officer workflows (e.g., Etimad reference update, vendor publication tracking) - Clarification handling processes (technical and commercial) - Committee dashboard views and delegation handling - Notification, alerting, and event tracking dashboards

KaarTech confirms full compliance with the functional requirements stated in the RFP, including but not limited to:

- Purchasing Officer Workflows (**Example:** Etimad reference number updates, vendor publication tracking).
- Clarification Handling process (Technical & Functional)
- Committee Dashboard and Delegation handling
- Notifications, alerting and Event Tracking dashboards:

2. Detailed matrix mapping each UI screen to the corresponding functional requirement. Also identify any screens not currently included in your development scope and confirm your commitment to developing them.

The proposal details each functional requirement and its acceptance to comply under section 4.2. Any additional screens to meet the of process scope items (features) listed in the RFP shall be finalized during Explore phase and it will be developed.

Below is the requested matrix of UI screens with business process as per the functional requirements in the RFP.

Development Type	Process	Description	Complexity	Business Process Section Mapping
User Interface (Screens)	RFP	RFP Create	High	Accounted for the requirements



Development Type	Process	Description	Complexity	Business Process Section Mapping
User Interface (Screens)	RFP	RFP Change/Edit	High	detailed in section 4.2.1.1 of Technical Proposal
User Interface (Screens)	RFP	RFP Inbox	Medium	
User Interface (Screens)	RFP	RFP - My Request	Medium	
User Interface (Screens)	RFP	RFP Dashboard	Medium	
User Interface (Screens)	RFP	Budget Allocation Creation	Medium	
User Interface (Screens)	RFP	Budget Allocation - My Request	Medium	
User Interface (Screens)	General	RFP Maintenance	Medium	
User Interface (Screens)	General	SLA Maintenance	Medium	
User Interface (Screens)	General	Committee Maintenance	Medium	Accounted for the requirements detailed in section 4.2.1.2 of Technical Proposal
User Interface (Screens)	Committee	Bid Opening Committee Form	High	
User Interface (Screens)	Committee	Bid Evaluation Committee Form	High	
User Interface (Screens)	Committee	Technical Evaluation Committee Form	High	
User Interface (Screens)	Committee	Bid Qualification Committee Form	High	




Development Type	Process	Description	Complexity	Business Process Section Mapping
User Interface (Screens)	Committee	Inbox - Tender list	Medium	
User Interface (Screens)	Committee	Committee Dashboard	Medium	
User Interface (Screens)	Committee	Signature Upload	Medium	
User Interface (Screens)	Contract Generation	My inbox – contract	Medium	Accounted for the requirements detailed in section 4.2.1.3 of Technical Proposal
User Interface (Screens)	Contract Generation	Contract Preparation Form	High	
User Interface (Screens)	Contract Generation	Initial Contract assignment screen	Medium	
User Interface (Screens)	Contract Generation	Signature upload	Medium	
User Interface (Screens)	Contract Generation	Contract Dashboard	Medium	
User Interface (Screens)	Contract Management	Contract Change Request Form	Medium	Accounted for the requirements detailed in section 4.2.2.1 of Technical Proposal
User Interface (Screens)	COC	COC Preparation and approval Form	Medium	Accounted for the requirements detailed in section 4.2.2.2 of Technical Proposal
User Interface (Screens)	COC	COC Dashboard	Medium	
User Interface (Screens)	COC	COC Creation - PO/contract selection screen	Medium	





3. UX design walkthroughs and approval checkpoints with SWA will be conducted during the Explore and Realization phases. Explain how SWA feedback will be incorporated before final delivery.

Yes, confirmed. UI design walkthroughs and approval checkpoints shall be scheduled and signed off in explore phase. Feedback/ changes from SWA stakeholders will be captured via KTer.AI and implemented to the solution which will be showcased for validation in UAT during realize phase before deployment.

4. Details on the implementation of Multi-Factor Authentication (MFA) for administrative accounts. In addition, confirm that OWASP Top 10 security practices are followed and whether a third-party vulnerability assessment report will be provided after deployment.

- SWA's SAP S/4HANA Rise Private Cloud Edition Landscape is SAP SSO Enabled which supports Multi-Factor Authentication (MFA) through Microsoft ADFS. SAP SSO Architecture follows the OWASP security guidelines. Kaartech will leverage this SSO Mechanism to access the P2P Application hosted in SAP BTP Cloud Foundry Environment.
- Below diagram shows the SSO architecture

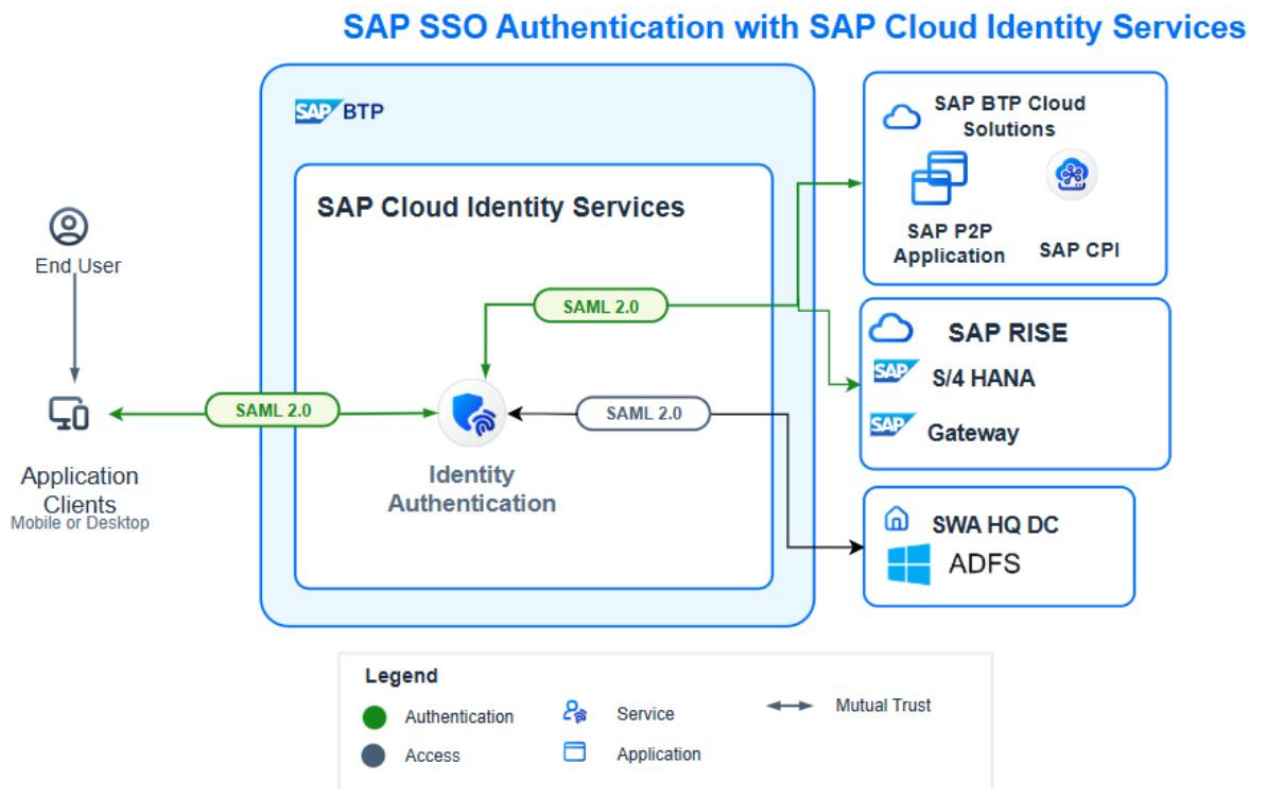

- P2P Application shall be hosted in SAP BTP (Business Technology Platform) Cloud Foundry Environment. As BTP is an PaaS offering by SAP, SOC's Compliance Report Type 1 & Type 2 shall be provided by SAP which includes penetration testing and vulnerability testing.

5. Confirm on the business logic and data processing reside within SAP S/4HANA using native tools (ABAP, BADIs, CDS Views, OData). Clarify the role of Node.js and Angular in your solution and ensure they are used only for UI/middleware layers without affecting SAP-native extensibility.

- All business logic resides in SAP S/4HANA using ABAP, CDS Views, BADIs, and OData.
- Node.js and Angular are exclusively used for UI deployment in SAP BTP. An Angular-based web application, served via a Node.js runtime, will be deployed on SAP BTP using the Cloud Foundry environment.
- Complied with clean core principles of SAP.

6. Licensing and ownership structure for KTern.AI components. Will SWA retain full access post-go-live? Are there any recurring subscription costs associated with KTern.AI?
KTern. AI is a DXaaS tool platform used by KaarTech for its digital transformation projects.

The KTern license for implementation period shall be taken care by KaarTech. However, post go live, all the documents/reports from KTern shall be extracted and handed over to SWA as part of the deliverable "Complete Documents Handover" planned in Hypercare support. Kindly refer to the section – 7.4 Project Deliverables.

In case, if SWA would like to use KTern after the implementation period for other projects. Then, SWA shall request an official quotation from KaarTech on the same.

7. Performance testing simulating up to 5,000 concurrent users will be performed and provide the expected timeline for sharing performance results with SWA (e.g., during UAT).
Yes, confirmed. SAP BTP Cloud Foundry is a PaaS offering in which the environment is scalable in relation to User Load. Load Testing shall be executed in the deployed BTP environment through load runner script for 5,000+ concurrent users and its performance results will be shared with SWA in realize phase.

8. Valid change requests raised during the hypercare and support period that fall within the RFP scope will be implemented at no additional cost.

All valid change requests aligned with process scope items (features) listed in the RFP will be executed at no additional cost during the Hypercare Support Period (4 months).

9. Proposed integration and configuration approach with the SAP PPM (Project Portfolio Management) module. This module is used by SWA to initiate projects and service requests and must be aligned with your proposed procurement lifecycle.
During the Request for Proposal (RFP) creation process within the Procure-to-Pay (P2P) system, integration with the Project Portfolio Management (PPM) module is available to verify the existence of an active project and the availability of sufficient budget corresponding to the RFP value. This ensures that the RFP is aligned with approved financial and project planning parameters.



In cases where no budget has been pre-allocated for the identified project, the system will support ad hoc budget planning. The P2P system will trigger the PPM module to initiate a planning process, allowing for the definition and allocation of the necessary budget. Once the budget has been allocated and confirmed by the PPM module, the RFP preparation process can proceed accordingly.

This integration ensures financial governance, promotes planning accuracy, and facilitates a seamless procurement workflow aligned with organizational budgeting and project execution standards.

10. Committee Role Handling Does the proposed solution support managing multiple procurement committees assigned to the same role or function concurrently? For example, can more than one committee act in the role of "Evaluation Committee" simultaneously across different RFPs within the system?

Yes, Confirmed. The system supports multiple committees concurrently fulfilling the same role (e.g., multiple Evaluation Committees) across different RFPs using a dynamic assignment model. In other words, each RFP can have different committee members.

11. The full integration scope, including both technical and functional aspects, must be executed directly by your ABAP and SAP CPI (Cloud Platform Integration) teams. Please confirm that no third-party resources or subcontractors will be involved in this integration work.

Yes, confirmed. The integration scope shall be completely executed by ABAP and CPI consultant provided by KaarTech. No third-party resources or subcontractors will be involved.

12. SAP CPI is the only accepted middleware for this project. Please confirm that SAP PO (Process Orchestration) or any alternative platforms will not be used.

Yes, confirmed.

13. VPN access will not be granted to any vendor consultants. All connectivity must follow our secure access policies, which will be communicated separately if needed.

Yes, confirmed.

14. Please be aware that our SAP S/4HANA system is currently undergoing an upgrade. Your technical team must be prepared to ensure compatibility with the updated system landscape during implementation.

Yes, confirmed. The technical developments shall be processed through ATC check before deployment which ensures compatibility with SAP S/4HANA upgrades.

9.23 Team Continuity Requirements

1. Key team members (e.g., Project Manager, Technical Lead, Functional Consultant) will remain committed throughout the execution and support period.



KaarTech confirms that the onboard project team shall remain unchanged during the project unless there are exceptional circumstances, such as serious health issues affecting the individual or their family, personal loss, or employee separation.

2. Proposal guarantees the continuity of the same project team members during implementation and post-go-live support.

Yes, confirmed.

3. Process for handling replacements, including how SWA will be notified, what documentation will be provided (e.g., CV, justification), and whether SWA has the right to approve or reject proposed replacements.

In case of exceptional circumstances that consultant has to be replaced, KaarTech shall notify SWA with the identified replacement profile along with the justification for replacement. Since this is a delivery-based engagement and not a T&M resource-based engagement, resources identification shall be at the discretion of KaarTech. However, KaarTech shall take complete accountability on ensuring the deliverables are met in planned timeline.

During this transition, below is the Knowledge Transfer (KT) process followed:

1. KT Giver to publish the KT Status Tracker with Topics, Schedule.
2. KT Giver to provide KT per the schedule & post KT Status Tracker.
3. KT Receiver to prepare KT Understanding Document.
4. KT Giver to signoff/approve the KT Understanding Document

This would help to have streamlined Knowledge Transfer (KT) and acceptance from New Team Member on receipt of KT.

9.24 Training Scope

1. Your training scope focuses only on BPOs and key users, with no specific breakdown for departments such as Procurement, IT, Legal, and Finance.

BPO and Key users shall be identified in stakeholder matrix document as part of prepare phase.

- Key users shall comprise members of IT, Procurement, Legal and Finance.
- Business Process Owner (BPO) shall be the decision maker for the entire P2P process.

2. Please confirm if training sessions will be tailored by user role, including procurement staff, committee members, and system administrators.

Yes, training will be tailored to different user roles, including procurement staff / purchasing officer, committee members, and system administrators.



3. The training delivery appears limited to 8 virtual sessions (16 hours) and documentation in English. Please clarify whether training will include: • Hands-on exercises, sandbox practice, and walkthroughs • Recorded demo sessions and role-specific FAQs.

Yes, Confirmed. Training will include:

- Hands-on sandbox exercises
- Live walkthroughs
- Recorded demo sessions
- Role-specific FAQs

4. Kindly confirm whether refresher training and Q&A support will be provided during the Hypercare phase.

Yes. Refresher training sessions scheduled in batch (E.g., 1 session per week) can be provided during the Hypercare phase to reinforce learning and ensure adoption. Q&A can be raised as tickets by the end users in Solman and shall be resolved by KaarTech consultants.

5. Clarify whether administrator-specific training will be conducted and whether guidebooks or cheat sheets will be delivered.

Administrator-specific training will be conducted, and user guides will be provided.

9.25 Post-Go-Live Support (Hypercare and Standard)

1. The SLA listed in your proposal (4-hour response, 8-hour resolution) does not meet the critical issue resolution requirement defined in the RFP (1-hour acknowledgment, 4-hour resolution for critical incidents). Kindly confirm your ability to comply with this SLA.

KaarTech shall comply to requested SLA for the scope in Section 6.1 of RFP as mentioned below, "Critical issues must be acknowledged within 1 hour and resolved or mitigated within 4 hours".

2. Your proposal does not explicitly confirm that original project developers and consultants will be actively available during the first month of Hypercare.

Project Developers & Consultants identified as Primary in Section 2.6 of the response document shall be actively available during the first month of Hypercare.

3. Please clarify whether the same key technical team members involved in development will support SWA during Hypercare and provide a list of their names and roles.

P2P Solution being KaarTech's Strategic Innovative In-House Solution, KaarTech has a predefined Support Team who shall take over from the Implementation Team. This team has better experience in supporting P2P Application. However, as confirmed in previous statement, original project



developers & consultants identified as Primary in Section 2.6 of the response document shall be actively available during the first month of Hypercare to ensure transition.

4. Your support scope is currently limited to incident handling, with no mention of minor enhancements, patching support, or proactive system monitoring during the support period.

During Hypercare Support Period (4 Months), KaarTech shall support Incident Management, Service Request Management, Minor Enhancements & Monitoring Activities as outlined in scope of the proposal. However, KaarTech has considered only Incident Management as part of Technical Support Period (8 Months) as requested in the RFP Section 6.2.

5. Confirm whether your support team will maintain compatibility with SAP patches and upgrades and continue monitoring integration with SAP Ariba and other modules.

Yes, confirmed.

6. Kindly clarify if you will assign a dedicated Support Manager for the entire support period and provide weekly trend and incident reports as required.

Yes, confirmed.

9.26 Development Scope Flexibility

1. Please be reminded that the scope defined in the RFP represents the minimum baseline required. Your solution must remain flexible to accommodate future functional and workflow extensions.

Yes, Confirmed. The solution is designed with extensibility & scalability in mind.

2. We require confirmation that the development scope will not be limited to the exact list of features mentioned in the proposal.

Yes, Confirmed. The developments shall not be limited to the documented list in the proposal, Such developments aligned with process scope items (features) listed in the RFP in consideration to SAP S/4HANA features, technologies utilized & its license availability with SWA are requested to be identified during the Explore Phase of the project so that it can be accommodated within the project timeline.

3. The proposed solution must support extensibility and configurability to address evolving procurement needs within the Authority.

Yes, Confirmed. The system supports configuration, and extensibility features to adjust to evolving business needs.

9.27 Project Team Allocation

1. Total number of personnel you plan to assign for each role identified in your proposal (e.g., Project Manager, SAP Technical Consultant, Workflow Specialist, Integration Consultant, Support



Manager, etc.). - Your response should indicate the full team structure with roles, number of resources per role, and expected effort (FTE or percentage allocation).

S.No	Project Role	Type	FTE
1	Project Manager / Support Manager	Primary	1.00
2	SAP Functional Consultant – Procurement / MM	Primary	1.00
3	SAP Functional Consultant – Cross-Module (FI / HCM)	Secondary	0.25
4	SAP Technical Consultant / ABAP Developer	Primary	1.00
5	SAP Technical Consultant / ABAP Developer	Secondary	2.00
6	SAP Fiori / UI5 Developer or Angular	Primary	1.00
6	SAP Fiori / UI5 Developer or Angular	Secondary	1.50
7	SAP Workflow Consultant	Secondary	0.50
8	SAP Integration Consultant	Secondary	0.25
9	SAP Security & Authorization Specialist	Secondary	0.25
10	SAP Test Lead / QA Specialist	Secondary	0.75

2. Onsite vs. Offshore Team Distribution Your proposal refers to both onsite and offshore team members. Please provide a clear nomination of which team members will be working onsite (at SWA premises) and which will be working remotely (offshore). For each, kindly explain how offshore team will contribute without VPN Access.

Onsite (SWA Riyadh):

- Project Manager
 - Available Onsite during Prepare, Explore & Deploy Phases
- SAP Functional Consultant (MM)
 - Available Onsite during Explore, Realize, Deploy & Run Phases
- SAP Technical Consultant / ABAP Developer
 - Available Onsite during Realize Phases

Offshore (India):

- Project Manager / Support Manager




- Available Offshore during Realize & Run Phases
- SAP Functional Consultant – Cross-Module (FI / HCM)
 - Available Offshore during Explore Phases
 - Consulting support required to identify Integration Points and does not involve hands-on activity in S/4HANA System.
- SAP Technical Consultant / ABAP Developer
 - Available Offshore during Realize, Deploy & Run Phases
 - The P2P Solution being KaarTech's Strategic Innovative In-House Solution, the ABAP Developments shall be carried out in KaarTech Standard P2P System and shall be transported to SWA through imports through the Onsite Techno-Functional Consultant.
- SAP Fiori / UI5 Developer or Angular
 - Available Offshore during Explore, Realize, Deploy & Run Phases
 - An Angular-based web application, served via a Node.js runtime, will be deployed on SAP BTP using the Cloud Foundry environment. This BTP Cloud Foundry Environment is Cloud Based SaaS Offering by SAP.
- SAP Workflow Consultant
 - Available Offshore during Realize, Deploy & Run Phases
 - The P2P Solution being KaarTech's Strategic Innovative In-House Solution, the Workflow Developments shall be carried out in KaarTech Standard P2P System and shall be transported to SWA through imports through the Onsite Techno-Functional Consultant.
- SAP Integration Consultant
 - Available Offshore during Realize, Deploy & Run Phases
 - Integration is executed using CPI as middleware. This CPI Environment is Cloud Based SaaS Offering by SAP.
- SAP Security & Authorization Specialist
 - Available Offshore during Realize, Deploy & Run Phases
 - For Authentication, SSO is already configured between SAP S/4HANA, SAP CPI & SAP BTP Cloud Foundry. For Authorization, it shall be minimal effort as all roles shall be created in S/4HANA and routed through standard GRC protocols.
- SAP Test Lead / QA Specialist



- Available Offshore during Explore, Realize & Deploy Phases
- All Testing shall be carried out through UI which is hosted in BTP Cloud Foundry. This BTP Cloud Foundry Environment is Cloud Based SaaS Offering by SAP.





Primary

Messrs. Saudi Water Authority
P.O. Box 5968 Riyadh 11432 Al Olaya Prince Mohammed bin Abdulaziz Road
Kingdom of Saudi Arabia

Location Riyadh
TEBCBG563474: Letter of Guarantee No.
Date 08/07/2025

Whereas our clients, Messrs. Car Technologies Saudi Arabia for Information Technology Company, have submitted their bid to implement (or) supply the creation of an electronic platform for managing the life cycle of competitions, integrated with enterprise systems and artificial intelligence technologies. Reference No.: 250739015178, we, the Saudi First Bank, hereby unconditionally and irrevocably pledge to pay you an amount of 60,000.00 Saudi Riyals only (an amount of sixty thousand Saudi Riyals only), equivalent to 1% of the value of their bid submitted under the terms of the tender, as follows:

(a) We will pay you immediately, upon your written request, and regardless of any objection from the Contractor or any other party, this amount or any amounts you request to be paid, provided that they do not exceed in total the above-mentioned amount of 60,000 Saudi Riyals only (an amount of sixty thousand Saudi Riyals only), by transfer to your account with any bank in the Kingdom of Saudi Arabia or by any other method acceptable to you.

(b) Any payments made upon your request will be net and free from and without any current or future deduction for the purpose of settling any taxes, executions, fees, expenses, charges, deductions, or seizures of any nature or by the party imposing them.

(c) The representations contained in this guarantee constitute our direct, unconditional, and irrevocable obligations. We will not be relieved of all or part of these obligations for any reason of any nature or source, such as a change in the terms of the contract, its extension, a change in the extent or nature of the work required to be performed, or any default or act or action by you or a third party that would relieve or release us from our obligations and liabilities under this guarantee.

(d) This guarantee shall remain in force and effect until the end of the 8th day of December 2025.

(e) We will promptly respond to your request to extend this guarantee. If the work is awarded and you provide us with written and signed notice on or before the stated expiry date of this guarantee or any subsequent extensions to extend the guarantee, we will (i) automatically extend this guarantee for the requested period, provided that it does not exceed 365 days from the original expiry date of the guarantee or from the expiry date of subsequent extensions, as specified in the extension request, or (ii) pay you the value of the guarantee.

(f) We acknowledge and confirm that the value of this guarantee does not exceed 20 percent of the bank's total paid-up capital and reserves.

(g) Any dispute regarding this guarantee shall be decided solely by the competent authorities in the Kingdom of Saudi Arabia, in accordance with the applicable laws, decisions, regulations, and instructions.

(S) We hereby unconditionally and irrevocably undertake that this guarantee shall not be released or disposed of upon the customer's claim or by submitting the original guarantee to us, except with your written consent or upon its expiration without a written extension request from you, delivered to us by mail or electronic means.

For/Saudi First Bank

Authorized
Signatory: Abdullah Al-Sas J71
Abdullah ALJassas

Saudi Awwal Bank
Global Trade and Receivable Finance (GTRF)
Area Management Office - Central Province
King Abdullah Road cross Olaya Street, First Floor, Riyadh
P.O. Box 2907, Riyadh 11461, Kingdom of Saudi Arabia
Tel: 800 120 0025
SWIFT Code: SABBSARI, www.sab.com
A listed Saudi joint stock company,
capital SAR 20,547,945,220 (Fully Paid),
C.R. 1010025779, Unified no. 7000018668,
Regulated and supervised by the Saudi Central Bank.



Authorized Signatory
H. ALMOTAN

Saudi First Bank
International Trade and Receivables Finance
Regional Management Office - Central Region
King Abdullah Road, intersection of Al-Olaya Street, First Floor, Riyadh
P.O. Box 2907, Riyadh 11461, Kingdom of Saudi Arabia
Telephone: 800 1200025
www.sab.com SABBSARI Swift Code
A Saudi Joint Stock Company Listed
With a paid-up capital of 20,547,945,220 Saudi Riyals (paid in full)
7000018668 Commercial Registration No. 1010025779, Unified Number
Subject to the control and supervision of the Saudi Central Bank.

Handwritten signature



10.2 Commercial Registration Certificate

الرقم الموحد : ٧٠٢٦٥١٨٤٩٣ رقم المنشأة : ١٠١٠٧٥٦٦٣٦ التاريخ : ١٤٤٣/٠٤/٠٢ هـ	شهادة تسجيل الشركة Company Registration Certificate	وزارة التجارة Ministry of Commerce
الاسم التجاري للشركة : شركة كار تكنولوجيز السعودية لتقنية المعلومات (شخص واحد) نوعها : ذات مسئولية محدودة جنسيتها : سعودي مدة الشركة : تبدأ من : ١٤٤٣/٠٤/٠٢ هـ وتنتهي في : مركزها الرئيسي : هاتف : الرمز البريدي : ص. ب : النشاط : للاطلاع على بيانات الأنشطة الرجاء مسح الرمز التجاري ملكية الشركة : اجنبية رأس المال : ٥.٠٠٠.٠٠٠ ريال سعودي المديرين : 1 شاهينشا عبدول بشير 2 3 4 5 6 7 8 9 10 11 12 13 14 15 16 سلطات المدير/المديرون : حسب ما نص عليه عقد الشركة يشهد مكتب السجل التجاري بمدينة : الرياض بأنه تم تسجيل الشركة المذكورة أعلاه بمدينة : الرياض وتنتهي صلاحية الشهادات في : ١٤٤٧/٠٤/١٤ هـ بموجب الإيصال رقم : ٢٤٠٩٤٣٢٢٠٦٢٨ وتاريخ : ١٤٤٦/٠٣/١٢ هـ		



[Handwritten signature]



10.3 Classification of Contractors Certificate

1/1



الدرجة الثالثة

شهادة

تصنيف مقدمي خدمات المدن

تمنح وزارة الشؤون البلدية والقروية والإسكان شهادة تصنيف بالدرجة

شركة كار تكنولوجيز السعودية لتقنية المعلومات

نظم
مبنى

بلدي
balady

وزارة الشؤون البلدية والقروية والإسكان

1443

بيانات المنشأة	الرقم الوطني الموحد / الترخيص	تاريخ إصدار السجل التجاري / الترخيص	اسم مالك المنشأة	نوع المنشأة	جنسية المنشأة	رأس المال
	7026518493	06/11/2021	كار تكنولوجيز دنيا برايفت ليمتد	محدودة أجنبية	سعودي	35000.0
بيانات شهادة التصنيف	رقم الشهادة	تاريخ الإصدار	درجة التقييم الائتماني	درجة التقييم الفني		
	2024003445	26/03/2024	B+	71.0		
أنشطة شهادة التصنيف	المجال	الأنشطة				
	الاتصالات وتقنية المعلومات	تصميم وبرمجة البرمجيات الخاصة بتطوير التطبيقات				

وكيل الوزارة لتنظيم مشطبي المدن

إبراهيم بن فيصل بن حسن الصقر

26/03/2026

- يسري مفعول هذه الشهادة حتى تاريخ 26/03/2026

- تصدر هذه الشهادة إلكترونياً وعلى الجهات المالكة للمشايخ التحقق من الشهادة المقدمة من خلال موقع الوزارة.



(Handwritten signature)



10.4 ZAKAT Certificate

				المملكة العربية السعودية Kingdom of Saudi Arabia	
TIN	٣١١١٥٨٥١٦٤	الرقم المميز		هيئة الزكاة والضريبة والجمارك Zakat, Tax and Customs Authority	
Certificate No.	١٠٢٢٢٢٩٧٠	رقم الشهادة			
Issue Date	١٤٤٥/١٠/٣٦	تاريخ الانشاء			

شهادة

Certificate

The Zakat, Tax and Customs Authority certifies that the Taxpayer	تشهد هيئة الزكاة والضريبة والجمارك أن المكلف /
---	---

شركة كار تكنولوجيز السعودية لتقنية المعلومات

Entity Unified No. / ID No.	٧٠٢٦٥١٨٤٩٣	الرقم الموحد للمنشأة / رقم هوية
Commercial Registration/License / Contract No	١٠١٠٧٥٦٦٣٦	سجل تجاري / رخصة / عقد رقم

Has submitted his tax return for the period ending on 31/12/2023 AD, and he was granted the certificate to complete all his transactions including the payment of the final amount due on the contract. The Certificate is valid until 02/11/1446 AH corresponding to 30/04/2025 AD (The second of Dhu al-Qi'dah one thousand four hundred forty-six Hijri)	قدم إقراره عن الفترة المنتهية في ١٨/١٢/١٤٤٥ هـ . وقد منح هذه الشهادة لإنهاء جميع معاملاته بما في ذلك صرف مستحققاته النهائية عن العقود . يسري مفعول هذه الشهادة حتى تاريخ ٢٠/٠٤/١٤٤٦ هـ الموافق ٢٠٢٥/٠٤/٣٠ م (الثاني من ذو القعدة ألف وأربعمائة وستة وأربعون هجري)
--	--

لا يعتد بهذه الشهادة إلا بعد التحقق من موقع الهيئة الإلكتروني: www.zatca.gov.sa

This certificate is not valid until verified by the Authority's Website: www.zatca.gov.sa

zatca.gov.sa 19993 @zatca__sa		هذه الوثيقة مستخرجة من النظام الآلي ولا تحتاج إلى توقيع ولا يعتد بهذه الشهادة إلا بعد التحقق من موقع الهيئة www.zatca.gov.sa
--	---	--




10.5 VAT Certificate



100221048761808

تاريخ الإصدار: 2022/01/23
الرقم المميز: 3111585164



الهيئة العامة للزكاة والدخل
General Authority of Zakat & Tax



شهادة تسجيل في ضريبة القيمة المضافة
VAT Registration Certificate

تشهد الهيئة العامة للزكاة والدخل بأن المكلف أدناه مسجل في ضريبة القيمة المضافة بتاريخ 2022/01/23

Hereby, The General Authority of Zakat & Tax (GAZT) certifies that the taxpayer below is VAT registered on 23/01/2022

Taxpayer Name:	شركة كار تكنولوجيز السعودية لتقنية المعلومات	اسم المكلف:
VAT Registration Number:	311158516400003	رقم التسجيل الضريبي:
Effective Registration Date:	2022/02/01	تاريخ نفاذ التسجيل:
Taxpayer Address:	Riyadh Al Malqa D, Anas Bin Malik, 13521	عنوان المكلف:



كمكلف مسجل في ضريبة القيمة المضافة، لا يجوز لك تحصيل ضريبة القيمة المضافة من عملائك قبل تاريخ نفاذ التسجيل بالضريبة. في حال تبين غير ذلك، ستقوم الهيئة العامة للزكاة والدخل بتنفيذ الغرامات المستحقة

هذه الوثيقة مرسلة من النظام الآلي ولا تحتاج إلى توقيع
- الهيئة العامة للزكاة والدخل -




10.6 GOSI Certificate



التاريخ: 21/01/2025

الموافق: 1446/07/21

رمز الشهادة: 90913960

شهادة

اسم المنشأة	شركة كار تكنولوجيز السعودية لتقنية المعلومات
اسم صاحب العمل	
رقم الاشتراك	٦٢٥٨٥٨١٩٤
العنوان	السعودية 13521
رقم السجل التجاري	١٠١٠٧٥٦٦٣٦

عدد المشتركين السعوديين	عدد المشتركين غير السعوديين	المجموع
9	5	14
تسعة مشتركين	خمسة مشتركين	اربعة عشره مشتركاً
رقما		
كتابة		

تشهد المؤسسة العامة للتأمينات الاجتماعية بأن المنشأة المذكورة أعلاه قد أوفت بالتزاماتها تجاه المؤسسة وفق البيانات المقدمة منها حتى تاريخ اصدار هذه الشهادة، والتي تم منحها لتقديمه لأية جهة تطلبها، وهي صالحة لجميع الأغراض التي نصت عليها الفقرة (6) من المادة (التاسعة عشر) من نظام التأمينات الاجتماعية الصادر بالمرسوم الملكي رقم (م/33) بتاريخ 1421/9/3 هـ و المادة (العاشر) من نظام التأمينات الاجتماعية الصادر بالمرسوم الملكي رقم (م/273) وتاريخ 1445/12/26 هـ .

هذه الشهادة سارية المفعول حتى 1446/08/20 هـ.

Public عام

الشهادة معتمدة من صاحب الصلاحية ولا تحتاج لتوقيع أو ختم



تحقق من صحة وصلاحيه الشهادة عبر زيارة الرابط أدناه في الموقع الإلكتروني للمؤسسة العامة للتأمينات الاجتماعية أو عن طريق استخدام الرمز المعرف التالي

تعد هذه الشهادة من الوثائق الإلكترونية الحكومية الرسمية ويحظر قطعاً نقلها أو إدخال أي تعديلات عليها سواء بالإضافة أو الحذف أو التغيير في بياناتها أو غير ذلك من أنواع التعديل. ويعدّ تعديل الشهادة لأية إداة منها شيء من ذلك، كما تعرض صاحبها للملاحقة النظامية أمام الجهات المختصة بالإضافة إلى ما يفرضه نظام التأمينات الاجتماعية من عقوبات، ولا يجوز تداول الشهادة إلا في الأغراض التي أصدرت لأجلها وفقاً لأحكام نظام التأمينات الاجتماعية، والمؤسسة العامة للتأمينات الاجتماعية غير مسؤولة عن أي عملية تزوير أو تعديل تم على البيانات الواردة فيها.

المملكة العربية السعودية، الرياض 12622 - 8308 - حي الوزارات 3795
Kingdom of Saudi Arabia, Riyadh 12622- 8308 Al Wizarat 3795

800 124 3344
gosi.gov.sa




10.7 Chamber of Commerce Certificate

		شهادة اشتراك Membership Certificate		 Riyadh Chamber	
Membership No. :	682665	682665	رقم العضوية الموحد :		
Date of Issue:	11/11/2021	2021/11/11	تاريخ الاصدار:		
Membership Class :	Third	الثالثة	درجة العضوية :		
Riyadh Chamber Certifies	تشهد الغرفة التجارية الصناعية بالرياض بأن				
					شركة كار تكنولوجيا السعودية لتقنية المعلومات
Commercial Registration No.	1010756636	1010756636	مقيدة بالسجل التجاري / الترخيص رقم :		
Certificate Expires on	06/10/2025	2025/10/06	ينتهي سريان هذه الشهادة في		



- يلزم التحقق من الوثيقة عبر الرابط <https://mybusiness.chamber.sa> ، أو تطبيق (سند) للأجهزة المحمولة أو الرقم الموحد دون ادنى مسؤولية على الغرفة عن محتوى الوثيقة.
- تعد هذه الورقة من الوثائق الإلكترونية لغرفة الرياض، ويمنع تعديلها أول محاولة العبث بها وتصبح لاغية حال محاولة تعديلها وتعرض صاحبها للملاحقة القانونية.




10.8 Nationalization Certificate



شهادة التوطين

رقم الشهادة	121289-11539740
تاريخ الإصدار	15/06/2025
تاريخ انتهاء الصلاحية	13/09/2025
تاريخ التجديد/التحديث	—
حالة الشهادة	تم التحقق
اسم المنشأة	شركة كار تكنولوجيا السعودية لتقنية المعلومات
رقم المنشأة	1-2379810
رقم الترخيص	—
الرقم الوطني الموحد	7026518493
مستوى نطاقات	بلائيني
معدل التوطين	% 63



The Ministry of Human Resources and Social Development certifies that the above mentioned Establishment has achieved the required Nationalization rate and has been granted this certificate upon request.

The certificate is electronically generated and approved by the authority. It does not require any signature or stamp.

تشهد وزارة الموارد البشرية والتنمية الاجتماعية بأن المنشأة المذكورة أعلاه حققت نسبة التوطين المطلوبة ولم منحها هذه الشهادة بناءً عن طلبها.

الشهادة تم إنشاؤها إلكترونياً ومعتمدة من الجهة المختصة ولا تحتاج إلى ختم أو توقيع.



10.9 MISA License

 وزارة الاستثمار Ministry of Investment	الرقم الموحد (7026518493) رقم المنشأة (669269) رقم الترخيص (102164302111534) تاريخ الإصدار 1443/02/13 هـ تاريخ الإنتهاء 1447/02/08 هـ م 2025/08/03 م 2021/09/21		 298995
	ترخيص استثمار خدمي Services Investment License		
المركز الرئيسي			
حالة الترخيص: جديد اسم الترخيص: شركة كار تكنولوجيز السعودية لتقنية			
الكيان القانوني: شركة شخص واحد ذات مسؤولية محدودة			
الموقع: الرياض			
رأس المال: 5,000,000 ريال سعودي			
702017: تقديم خدمات الاستشارات الإدارية العليا 721002: البحث والتطوير في مجال الهندسة والتكنولوجيا 854942: التدريب على استخدام الحاسوب والبرامج الملحقة			
تاريخ الطباعة 1446/01/03 هـ			
يمكنك التحقق من صحة وصلاحيّة الشهادة عبر زيارة الرابط https://investsaudi.sa/en/verify على موقع وزارة الاستثمار.			
			
2 - 2			

[Handwritten Signature]



10.10 LCGPA Certificate

التاريخ: 2024/09/10 م
رقم الشهادة: M 86067



هيئة المحتوى المحلي
والمشتريات الحكومية
Local Content & Government
Procurement Authority



شهادة المحتوى المحلي

Local content certification



The Local Content & Government Procurement Authority certifies that the Local Content Score for [Kaar Technologies Saudi for Information Technology] Commercial Registration No.(1010756636) for the year ended 31/12/2023, is 3.4%.

This certificate expires on 31/07/2025.

Note:
This certificate was issued according to the procedures followed by the Authority and based on the disclosure submitted by the entity and the report issued by the approved audit firm, without holding LCGPA minimally responsible.
This certificate is sent via electronic mail / automated system and it does not require a signature.

تشهد هيئة المحتوى المحلي والمشتريات الحكومية أن نسبة المحتوى المحلي لـ [شركة كار تكنولوجيز السعودية لتقنية المعلومات] سجل تجاري رقم (1010756636)، للسنة المالية المنتهية بتاريخ 31/12/2023م، تبلغ 3.4%.

تنتهي صلاحية هذه الشهادة في 31/07/2025م.

تنويه:
تم إصدار هذه الشهادة بحسب الإجراءات المتبعة لدى الهيئة بناءً على الإفصاح المقدم من المنشأة و التقرير الصادر من مكتب المراجعة المعتمد، دون أدنى مسؤولية على الهيئة.
هذه الوثيقة مرسلة عبر البريد الإلكتروني/ النظام الآلي ولا تحتاج إلى توقيع.

You can validate the information in this certificate via the following link [URL](#) or by scanning the above QR code

يمكنك التحقق من صحة البيانات الواردة في الشهادة أعلاه من خلال الرابط التالي [URL](#) أو من خلال مسح الرمز الرقمي أعلاه

[Handwritten signature]



10.11 SME Certificate



رقم الشهادة: 24236139995

تاريخ الإصدار: 15-05-2024

اسم المنشأة: شركة كار تكنولوجيز السعودية
لتقنية المعلومات

صلاحية الشهادة: سنة من تاريخ
الإصدار *

الرقم الوطني: 7026518493

السجل التجاري: 1010756636



**تشهد الهيئة العامة للمنشآت الصغيرة والمتوسطة "منشآت" بأن المنشأة المذكورة أعلاه تندرج
من ضمن المنشآت الصغيرة والمتوسطة وفقاً للتعريف المعتمد لدى "منشآت"**

يتم التحقق من الشهادة من خلال موقع منشآت

<https://profile.monshaat.gov.sa/validate>

تعد هذه الشهادة من الوثائق الحكومية الرسمية، ولا يجوز تداولها أو استعمالها إلا في حدود الأغراض التي أصدرت لأجلها، ويحظر قطعياً تقليدها أو إدخال أي تعديلات عليها سواء بالإضافة أو الحذف أو التغيير في بياناتها أو غير ذلك من أنواع التعديل، وتعد هذه الشهادة لاغية إذا شابهها شيء من ذلك، كما تعرض من ارتكب أي مما سبق إلى الملاحقة النظامية أمام الجهات المختصة دون الإخلال بما تنص عليه الأنظمة ذات العلاقة.

* يجب التحقق من خلال رابط موقع منشآت عن صلاحية الشهادة حيث أنه يتم التحديث بشكل دوري

[Handwritten signature]



10.12 SAP Partnership

partnerfinder.sap.com/profile/0001551662

SAP Partner Finder Partner Name KaarTech

KaarTech
www.kaartech.com

At a Glance Services Locations Resource

Your Dependable & Trustworthy Global SAP Partner

KaarTech, a global SAP leader, powers digital transformation through innovation and expertise. Operating in 20+ locations, we've completed 3000+ projects for 440+ clients, backed by 3500+ employees. Our in-house tool, Ktern.AI, accelerates S/4HANA transformations with Gen AI, leading 75+ projects. Our dedication to [more](#)

[Contact Partner](#)

8 Competencies >

SAP Recognitions

SAP Gold Partner

Partnership

Kaar Technologies Saudi for Informa ID 2816763

Overview Program & Tracks **Level** Authorizations Qualifications Certifications

Partnership Level

SAP Gold Partner

800 Points

This account has reached Gold Partnership Level

New Partner Leveling Framework (2025) Preview

- **New system launching in 2025.** This dashboard previews the projected level for Kaar Technologies Saudi for Information Technology under the new framework.
- **This preview is NOT the currently active, published level but may be identical to it.** The currently active level is Silver. SAP Gold Partners and SAP Platinum Partners can verify this on SAP Partner Finder.
- **Use this preview to prepare.** Understand the new system and take action to reach or maintain the desired level.
- **Progress updates are dynamic.** Updates occur daily or quarterly, depending on the specific metric.
- **Safeguarding:** The level will enter "safeguarding" if points drop below the required threshold for the current level.
- **Official Level:** After the preview period, the displayed level becomes official and any active safeguarding countdown resets to 200 days.

CERTIFICATE

SAP hereby certifies that

Kaar Technologies Saudi for Information Technology

Country : Saudi Arabia
City : Riyadh
Partner ID : 0002816763

is currently an SAP Gold partner, participating in the following engagement model/s*:

SAP PartnerEdge Service Consulting Services: SAP solution design, development, implementation, and integration guidance

COMPETENCY

On the date of issue, the partner has achieved the following competency and specialization designation(s). These designations demonstrate an SAP partner's maturity and expertise in delivery of the solution, or line of business level (LoB), or end-to-end process transformation.

COMPETENCY	SPECIALIZATION	TIER
Intelligent Enterprise	Recruit to Retire	None
Human Capital Management	Compensation and Commission Core HR and Payroll Learning Talent Management	Expert
SAP Business Technology Platform	Analytics and Planning Application Development and Integration Database and Data Management	Expert
Customer Relationship Management	Sales and Service	Essential
GROW with SAP	SAP S/4HANA Cloud Public Edition	Essential

CERTIFICATE

Kaar Technologies Saudi for Information Technology - Saudi Arabia - Riyadh

Continuation

Spend Management	Strategic Sourcing	Essential
Supply Chain Management	Supply Chain Logistics	Essential

*For additional information on engagement models, partner level, partner dimensions and competencies please reference
https://partnedge.sap.com/content/dam/public/dni/cert/Partner_Certificate_Info.pdf

Upon request and in accordance with applicable statutory provisions, regulations or procurement law, SAP is able to issue this certificate in local language and signed by an SAP signatory. To request, please contact the following email-address: partner@sap.com

This is a system generated certificate and therefore not signed by SAP. This certificate is subject to the terms and conditions of the signed and currently valid SAP PartnerEdge agreement and its schedules entered into by and between SAP and Kaar Technologies Saudi for Information Technology.

SAP PartnerEdge



10.13 Delegation letter



26 November 2023

Riyadh

Kaar Technologies Saudi for Information
Technology
3141, Anas Bin Malik Road
Building B, 2nd Floor,
AlMalqa
PO, Box 13521
Riyadh, Kingdom of Saudi Arabia.
CR No: 1010756636

To,

Whomsoever concerned.

Subject: Authorization Letter

We are Kaar Technologies Saudi for Information Technologies authorize our Chief Executive Officer, Mr. Shahinsha Abdul Basheer, to sign on behalf of Kaar Technologies Saudi for Information Technology the Contract document between us and your organization.

We also Authorize him to represent us with your organization for any discussion related to our projects.

Best Regards

Shahinsha Abdul Basheer

Chief Executive Officer

Kaar Technologies Saudi for Information Technologies.



10.14 Most Recent Article of Association



المركز الرئيسي الرياض

رقم النسخة الإلكترونية 1

رقم الطلب 393290

نظام أساس شركة

شركة كار تكنولوجيز السعودية لتقنية المعلومات (شركة ذات المسؤولية المحدودة من شخص واحد)

يعون الله وتوفيقه تم في 10/02/1446 الموافق 14/08/2024م الاتفاق بين كل من :

اسم الشركاء	رقم الهوية	الهوية	تاريخ الميلاد	الجنسية	مكان الإقامة	مدينة الإقامة
كار تكنولوجيز انديا برايفت ليميتد	U7122071N30000P1C2007045			الهند		

حيث يرغب الأطراف المذكورين اعلاه بتصحيح لوضع شركة كار تكنولوجيز السعودية لتقنية المعلومات والتعديله بالسجل التجاري رقم 1010756636 وتاريخ 02/04/1443 وتعديل نظام اساسي وفقاً لنظام الشركات الصادر بالمرسوم الملكي رقم (م/132) وتاريخ 01/12/1443هـ، ولتولاه التنفيذيه وأصبحت بنود نظام اساسي كما يلي:

للادة الأولى : أسم الشركة

شركة كار تكنولوجيز السعودية لتقنية المعلومات (شركة ذات المسؤولية المحدودة من شخص واحد)

للادة الثانية : للمركز الرئيس للشركة

يكون للمركز الرئيس للشركة في مدينة الرياض والشركة الحق في افتتاح فروع لها داخل وخارج المملكة متى اقتضت مصلحة الشركة وذلك بموافقة مالك رأس المال

للادة الثالثة : أغراض الشركة

الغرض	النوع
المساعدات الاجتماعية	استخراج ومعالجة المعلومات
التجارة والتصدير	أنشطة شركات نقل البضائع
المعلومات والتكنولوجيا	أنشطة البرمجة الحاسوبية
المعلومات والتكنولوجيا	أنشطة العمارة المعمارية الحاسوبية وإدارة البيانات الحاسوبية
المعلومات والتكنولوجيا	تطوير البنى التحتية والتكنولوجيا على شبكة ومراكزها وذلك من أنشطة
المعلومات والتكنولوجيا	أنشطة العمارة المعمارية في مجال التجارة
المعلومات والتكنولوجيا	البحث والتطوير لتسويق في مجال العلوم الطبيعية والهندسة

وتعتمد الشركة أغراضها وفق الأنظمة للتجارة وبعد الحصول على التراخيص اللازمة من الجهات المختصة إن وجدت.

للادة الرابعة : رأس المال

حدد رأس مال الشركة بـ 5000000 ريال خمسة ملايين ريال مقسم إلى 500000 حصة ، متساوية القيمة قيمة كل حصة 10 ريال تم توزيعها على الشركاء كالآتي:

الشركاء	النسبة المئوية	النسبة المئوية	قيمة كل حصة	إجمالي قيمة الأسهم
كار تكنولوجيز انديا برايفت ليميتد	500000	0	10	5000000
المساهمين	500000	0	10	5000000

16 - 1




10.15 National Address

Proof Number	IG4878134	رقم الإثبات
Original Date	15/5/2024	تاريخ الإصدار
Expiration Date	15/11/2024	تاريخ الانتهاء



العنوان الوطني
NATIONAL ADDRESS

إثبات عنوان Address Proof

Address Holder Details

Name:

Customer No.:

Reg. Date:

بيانات صاحب العنوان

الاسم:

رقم الحساب:

التاريخ التسجيل:

Address Details

Short Address:

Building No.: Street:

Secondary No.: District:

Postal Code:

City:

تفاصيل العنوان

العنوان المختصر:

رقم المبنى: الشارع:

الرقم الثانوي: الحي:

الرمز البريدي:

المدينة:



To Verify للتحقق

<https://portal.address.gov.sa/VerifyProofNA.aspx>

لم إصدار هذا الإثبات إلكترونياً ولا يتطلب التوقيع عليه
لم إصدار هذا الإثبات بناءً على طلب الموضح أعلاه ويحظر نسخاً أو تغييراً أو حذفاً لأي بيانات منه سواء باليد أو إلكترونياً أو بأي وسيلة أخرى. الإثبات هو ملك الدولة ولا يمكن بيعه أو تداوله أو استخدامه لأغراض أخرى غير الغرض المحدد.
This proof has been issued electronically and does not require a signature
This proof has been issued upon the request of the above-mentioned, and it is absolutely prohibited to produce it or make any modifications to it, whether by addition or deletion, and the proof is considered void if it is altered by tampering, and its owner is subject to legal accountability.

19492 <https://portal.address.gov.sa/portal/address-address/5/>

[Handwritten Signature]



10.16 ISO Certifications

KaarTech has attached the **ISO Certification** which demonstrates KaarTech commitment to the highest standards of quality, safety, and operational excellence. This certification ensures that our processes comply with internationally recognized standards, allowing us to deliver consistent, reliable, and high-quality results.



[Signature]





CERTIFICATE

This is to Certify that the
Occupational Health & Safety Management System
of
Kaar Technologies Saudi for Information Technology

Building 3141, Secondary Number :8292, Anas Bin Malik street, Al Malaqa Dist, Riyadh,
PO 13521, Kingdom of Saudi Arabia

Has been independently assessed and is compliant
with requirement of

ISO 45001:2018

This Certificate is applicable to the following
product or service ranges:

“Digital Transformation Services Encompassing Software License
Resale, Infrastructure Services, Software Development and Support,
With a Specialization Not Limited to SAP System Implementation, Upgrades,
Enhancements, Maintenance Support, Consultancy and Auditing”

Certificate No: CX260389KSA

Date of Initial registration	03-Nov-2023
Date of Certification	04-Nov-2024
Date of Next Surveillance	02-Nov-2025
Recertification Due	02-Nov-2026



This certificate is a property of Inter Continental Assessments and shall be returned immediately when demanded

Director



For Verification & Updated Information
Concerning the Present certificate visit to
Website: www.icassessments.com
email: contact@icassessments.com

INTER CONTINENTAL ASSESSMENTS

128 City Road, London,
United Kingdom, EC1V 2NX





CERTIFICATE

This is to Certify that the
Information Security Management System
of
Kaar Technologies Saudi for Information Technology

Building 3141, Secondary Number :8292, Anas Bin Malik street, Al Malaqa Dist, Riyadh,
PO 13521, Kingdom of Saudi Arabia

Has been independently assessed and is compliant
with requirement of

ISO 27001:2022

This Certificate is applicable to the following
product or service ranges:

“Digital Transformation Services Encompassing Software License
Resale, Infrastructure Services, Software Development and Support,
With a Specialization Not Limited to SAP System Implementation, Upgrades,
Enhancements, Maintenance Support, Consultancy and Auditing”

Certificate No: CX260390KSA

Date of Initial registration	03-Nov-2023
Date of Certification	04-Nov-2024
Date of Next Surveillance	02-Nov-2025
Recertification Due	02-Nov-2026



Director

This certificate is a property of Inter Continental Assessments and shall be returned immediately when demanded



For Verification & Updated Information
Concerning the Present certificate visit to
Website: www.icassessments.com
email: contact@icassessments.com

INTER CONTINENTAL ASSESSMENTS
128 City Road, London,
United Kingdom, EC1V 2NX





CERTIFICATE

This is to Certify that the
Information Technology
of
Kaar Technologies Saudi for Information Technology

Building 3141, Secondary Number :8292, Anas Bin Malik street, Al Malaqa Dist, Riyadh,
PO 13521, Kingdom of Saudi Arabia

Has been independently assessed and is compliant
with requirement of

ISO 27000:2018

This Certificate is applicable to the following
product or service ranges:

“Digital Transformation Services Encompassing Software License
Resale, Infrastructure Services, Software Development and Support,
With a Specialization Not Limited to SAP System Implementation, Upgrades,
Enhancements, Maintenance Support, Consultancy and Auditing”

Certificate No: CX260391KSA

Date of Initial registration	03-Nov-2023
Date of Certification	04-Nov-2024
Date of Next Surveillance	02-Nov-2025
Recertification Due	02-Nov-2026



This certificate is a property of Inter Continental Assessments and shall be returned immediately when demanded

Director



For Verification & Updated Information
Concerning the Present certificate visit to
Website: www.icassessments.com
email: contact@icassessments.com

INTER CONTINENTAL ASSESSMENTS
128 City Road, London,
United Kingdom, EC1V 2NX



10.17 Wage Protection System Certificate



Wage Protection System Certificate

Certificate ID	Issue date	Expiration date
136419-43453739	08/07/2025	08/08/2025

Certificate status Verified

Establishment name شركة كار تكنولوجيز السعودية
لتقنية المعلومات

Establishment Number 1-2379810

National Unified Number 7026518493



The Ministry of Human Resources and Social Development certifies that the above mentioned Establishment has achieved the required Wage Protection rate and has been granted this certificate upon request.

The certificate is electronically generated and approved by the authority. It does not require any signature or stamp.

Please note, this certificate does not guarantee that no Notes will not be applied to this establishment.

تشهد وزارة الموارد البشرية والتنمية الاجتماعية بأن المنشأة المذكورة أعلاه حققت نسبة الالتزام بحماية الأجور المطلوبة وتم منحها هذه الشهادة بناءً عن طلبها.

الشهادة تم إنشاؤها إلكترونياً ومعتمدة من الجهة المختصة ولا تحتاج إلى ختم أو توقيع

يرجى الملاحظة أن هذه الشهادة لا تعفي عدم تطبيق نظام الملاحظات على هذه المنشأة

رؤية
VISION 2030
المملكة العربية السعودية
KINGDOM OF SAUDI ARABIA





شهادة الإلتزام بحماية الأجور

رقم الشهادة	تاريخ الإصدار	تاريخ انتهاء الصلاحية
136419-43453739	08/07/2025	08/08/2025



حالة الشهادة

اسم المنشأة
شركة كار تكنولوجيز السعودية
لتقنية المعلومات

رقم المنشأة
1-2379810

الرقم الوطني الموحد
7026518493



The Ministry of Human Resources and Social Development certifies that the above mentioned Establishment has achieved the required Wage Protection rate and has been granted this certificate upon request.

تفهد وزارة الموارد البشرية والتنمية الاجتماعية بأن
الشهادة المذكورة أعلاه حظيت نسبة الإلتزام بحماية الأجور
المطلوبة وتم منحها هذه الشهادة بناءً عن طلبها.

The certificate is electronically generated and approved by the authority. It does not require any signature or stamp.

الشهادة تم إنشاؤها إلكترونياً ومعتمدة من الجهة
المختصة ولا تحتاج إلى ختم أو توقيع

Please note, this certificate does not guarantee that no Notes will not be applied to this establishment.

يرجى الملاحظة أن هذه الشهادة لا تعفي عدم تطبيق
نظام الملاحظات على هذه المنشأة

رؤية
2030
المملكة العربية السعودية
KINGDOM OF SAUDI ARABIA



10.18 Saudi Council of Engineer



رؤية
2030
المملكة العربية السعودية
KINGDOM OF SAUDI ARABIA



شهادة
اعتماد مهني
Certificate
Professional Accreditation



الهيئة السعودية للمهندسين
SAUDI COUNCIL OF ENGINEERS

Membership no.: 907708

عضوية رقم: 907708

In accordance with the Regulations of Saudi Council of Engineers by Royal Decree M/36 Date 26/9/1423H and the Engineering Professions Practice Regulation by Royal Decree M/36 Date 19/4/1438 H. SCE has approved:

استناداً إلى نظام الهيئة السعودية للمهندسين الصادر بالمرسوم الملكي رقم م/٣٦ وتاريخ ٢٦/٩/١٤٢٣هـ ونظام مزاولة المهن الهندسية الصادر بالمرسوم الملكي رقم م/٣٦ وتاريخ ١٩/٤/١٤٣٨هـ ولأئحته التنفيذية فقد قررت الهيئة اعتماد:

**RAGAVENDRAN THIRUMALAI
GOTHANDARAMAN**
 Membership Category: Engineer
 Specialization: Electronics & Communications Engineering
 Membership Start Date: 12/18/2022


راجافيندران تيرومالاي غوثاندارامان
 فئة العضوية: مهندس
 التخصص: هندسة الإلكترونيات واتصالات
 تاريخ بداية العضوية: 12/18/2022

This Certification is valid until: 18 December 2024

هذه الشهادة صالحة إلى تاريخ 17 جمادى الثانية 1446



Secretary General الأمين العام



م. عبدالمحسن بن ضاوي المجنوني



Digitally signed by Saudi Council of Engineers at 1/27/2024

10.19 Recent financial statements

S. No	Description	Attachments
1	Financial statements for the past 3 years (2022, 2023, 2024)	 Kaar_2022 Audit Report Eng 4.pdf  KAAR FS2023Eng 12.pdf  KT KSA FS - Q3 Sep'24 In-house.pdf
